



Proposed Residential Development
31 Barkham Ride, Barkham

Construction Method Statement

For

A1 Roberts Properties

Document Control Sheet

Proposed Residential Development

31 Barkham Ride, Barkham

A1 Roberts Properties

This document has been issued and amended as follows:

Date	Issue	Prepared by	Approved by
22/08/2025	1 st Draft	GL	DM
03/09/2025	2 nd Draft	GL	DM
16/09/2025	Revised Report	GL	DM
30/09/2025	Revised Report V2	GL	DM
03/10/2025	Revised Report V3	GL	DM
06/10/2025	Revised Report V4	GL	DM



Motion
 84 North Street
 Guildford
 GU1 4AU
T 01483 531300
F 01483 531333
E info@motion.co.uk
W www.motion.co.uk

Contents

1.0 Introduction 1

2.0 Considerate Contractors..... 2

3.0 Site Context 3

4.0 Construction Site Layout and Programme..... 5

5.0 HGV Activity 8

6.0 Mitigation Measures10

7.0 Monitoring and Review11

Figures

Figure 3.1 - Site Location..... 3

Figure 4.1 - Vehicle Route to Site 7

Appendices

A Site Setup

B Swept Path Analysis

1.0 Introduction

- 1.1 This Construction Method Statement has been prepared by Motion on behalf of A1 Roberts Properties in relation to the proposed construction of 31 static mobile homes at 31 Barkham Ride, Barkham (herein referred to as 'the site').
- 1.2 The site is located on the northern edge of Finchampstead and is approximately 2.3km south-west of Wokingham. To the south west, the site is bound by Barkham Ride, and to the south east is bound by a number of bungalows. The site benefits from close proximity to local bus stops, and the M4. The site is located within the administrative authority of Wokingham Borough Council (WBC).
- 1.3 The proposals seek planning permission for the demolition of the existing dwelling and the subsequent construction of 31 static mobile homes. Access will be achieved via an existing junction from Barkham Ride which serves the existing mobile home site to the east. The existing access serving the house on site will be formally stopped up. Appropriate levels of car and cycle parking will be provided in-line with relevant standards.

Scope of the Construction Management Plan

- 1.4 The purpose of this CMS is to outline the strategy for the efficient movement and management of demolition and construction traffic associated with the site.
- 1.5 This CMS is a 'live' document, and given that no contractor has yet been appointed, the information contained within may be subject to changes / amendments, which would be agreed, in advance, with WBC.
- 1.6 The aim of this CMS is to minimise the impacts of demolition and construction on the local road network and to minimise any environment impact of the works. The principal issues addressed by the CMS are:
 - ▶ Programme of work;
 - ▶ Loading and unloading of plant and materials;
 - ▶ Hoarding provision;
 - ▶ Site compound layout and access;
 - ▶ HGV deliveries and hours of operation; and
 - ▶ Mitigation measures such as measures to control noise, vibration and dust.
- 1.7 Following this introduction, the remainder of this report comprises the following sections:
 - ▶ Section 2 – Site Management Contact Details and Considerate Contract Scheme;
 - ▶ Section 3 – Site Context;
 - ▶ Section 4 – Construction Site Layout and Programme;
 - ▶ Section 5 – HGV Activity;
 - ▶ Section 6 – Mitigation Measures; and,
 - ▶ Section 7 – Monitoring and Review.

2.0 Considerate Contractors

Site Management Contact Details

- 2.1 The Construction Project Manager (CPM) will be responsible for implementing the measures contained in the CMS and will be the point of contact for local residents.
- 2.2 The 24-hour contact details of the CPM will be displayed on the frontage of the site. The CPM will liaise with local residents when necessary to ensure that they are aware of the program of works taking place and to give advance notice of any noisy or disruptive works.
- 2.3 The CPM will be responsible for the monitoring and reviewing of the CMS and will deal with any concerns of local residents and businesses.
- 2.4 The CPM will be set out in any updated Construction Method Statement once planning consent has been granted.

Considerate Contractors Scheme

- 2.5 All the demolition and construction contractors will be signed up for the Considerate Scheme upon appointment.
- 2.6 The Considerate Contractors Scheme is a non-profit scheme which encourages best practice beyond statutory requirements. Contractors follow a 'Code of Considerate Practice' requiring adherence to the following topics to improve the image of construction:
 - ▶ Care about Appearance;
 - ▶ Respect the Community;
 - ▶ Protect the Environment;
 - ▶ Secure Everyone's Safety; and Value their Workforce.
- 2.7 The scheme provides information, advice and e-learning for the aforementioned topics in relation to real world scenarios through a 'Best Practice Hub'. This uses previous projects as example of best practice, leading to future improvement.

3.0 Site Context

- 3.1 The site is located to the north of the built up area of Finchampstead and 2.3km south west of Wokingham. The site is located along Barkham Ride, adjacent to Rook's Nest Wood Country Park. The site benefits from close proximity to local bus stops and the M4, as well as a number of amenities within walking distance. The site is situated within the administrative authority of the Wokingham Borough Council. The site in relation to strategic transport links is shown in Figure 3.1 below.

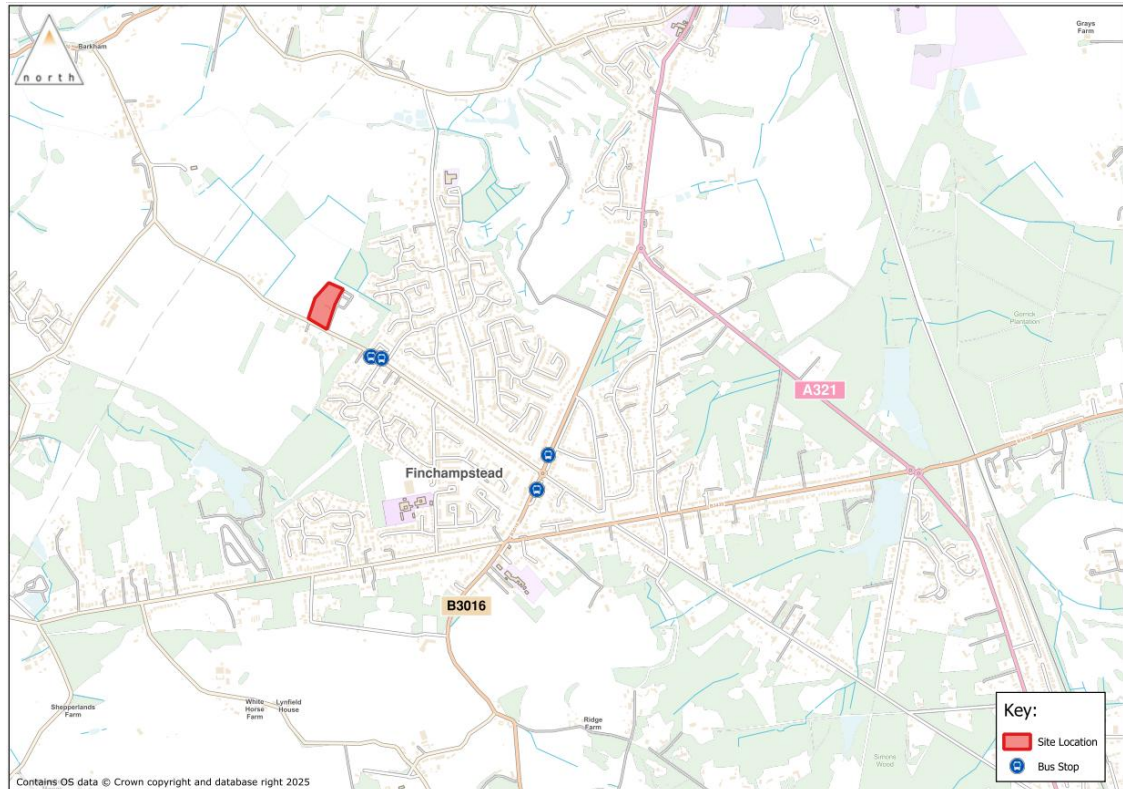


Figure 3.1 - Site Location

Existing Highway Network

- 3.2 Vehicular access to the site will be achieved via Barkham Ride. Barkham Ride is a single carriageway road operating a 40mph speed limit in the vicinity of the site. The speed limit along road decreases to 30mph approximately 230m south east of the site access. The road connects with Finchampstead Road in the south and provides access to Barkham village in the north.
- 3.3 Finchampstead Road is a single carriageway residential street operating a 30mph speed limit. The road provides access to Wokingham in the north.
- 3.4 Consideration has been given to crashmap.com to identify any incidents that have occurred on the road network surrounding the site in the last 5 years (up until the end of 2022). One accident has occurred on the road network bordering the site, this accident was 'slight' in severity. The accident occurred in 2019 and involved a vehicle in the act of turning left getting hit by the vehicle from behind. The driver of one of the vehicles sustained slight injuries. The accident occurred in the dark during dry conditions.

Accessibility

- 3.5 The site is accessible on foot via the footway on the north eastern edge of Barkham Ride. Approximately 210 metres south east of the site, a footway is established on the southern edge of the road. These footways provide access into the residential area of Finchampstead, where residents can access a range of amenities. While Barkham Ride is not lit in the immediate vicinity of the site, street lighting is provided from approximately 250m south east of the site and continues throughout the majority of the residential area.
- 3.6 While there are no designated cycling facilities on the roads in the vicinity of the site, it is considered they are suitable for cycling due to the wide width of the roads.
- 3.7 There are a number of bus stops within walking distance of the site. The closest stops to the site located 240m south east of the site on Barkham Ride, these stops serve the '3' Leopard service. The stops on Finchampstead Road are located 1.2km south-east of the site, these serve the '3' Leopard, 125, 125A, 125B, 145 and 406 bus services. These services provide routes towards Reading, Wokingham, Crowthorne and Farnborough.
- 3.8 The site is located in between Wokingham railway station and Crowthorne railway station. Wokingham station is located 4.6km north east of the site, while Crowthorne Station is located 4.1km south east of the site, both take 15 minutes to access by bike. Wokingham station offers a wider variety of rail services including Reading, London Waterloo and Gatwick Airport.

4.0 Construction Site Layout and Programme

- 4.1 This section of the CMS sets out the overall construction programme and provides information for the construction phases.

Overall Programme

- 4.2 The overall duration of the construction works is estimated at around 12 months. The programme includes the following key phases.

Phase of Works	Duration
Site Setup	2 Weeks
Foundation Works	2 months
Sub Drainage	2 month
Delivery/Installation of Static Homes	2 months
Construction of Community Building	6 months

Table 4.1 – Indicative Programme of Works

Delivery Hours

- 4.3 Works will take place on-site between the hours of 08:00 -18:00 Monday to Friday, and the hours of 08:00 to 13:00 on Saturdays which accords with the standard working hours for construction sites.
- 4.4 Vehicles arriving and departing the site will be limited to the following time periods to also avoid network peak times:
- ▶ Monday to Friday 09:00 to 17:00 hours.
- 4.5 A record will be kept indicating all anticipated vehicles and their arrival time daily. This will be maintained by a relevant site manager to ensure that drivers are aware of when they are permitted on site. This will assist in avoiding nearby school peak periods.
- 4.6 On a weekly basis the site co-ordinator will evaluate details of the daily profile of deliveries proposed for the upcoming week. Hauliers will be required to contact the site on a daily basis and indicate their delivery schedule for the following day. The proposed deliveries will be checked against the weekly delivery schedule. This will be overseen by the site co-ordinator to ensure deliveries are controlled and vehicles are not waiting on local roads, thereby ensuring that there is always space at the site to accommodate the necessary deliveries.

Construction Signs

- 4.7 Throughout the duration of construction, temporary signage indicating the movement of construction vehicles will be installed. At the site access a sign stating 'Caution Site Access' will be installed. Along Barkham Ride approximately 45 metres east and west a sign stating 'Site Access Ahead' will be installed.

Material Storage and Security

- 4.8 Storage of plant will be provided on site in a secure location. The proposed site set-up plan is shown at **Appendix A**. This illustrates the material and plant storage area, as well as the staff accommodation (cabin/toilets).

4.9 Noisy plant will be sited as far away as is practicable from neighbouring buildings. The use of barriers, such as acoustic sheds or partitions to deflect noise away from noise sensitive areas will be employed wherever practicable. Other measures relevant to plant operation include:

- ▶ All plant and equipment will be powered by mains electricity in preference to locally powered sources such as diesel generators;
- ▶ Plant will be maintained in good workmanlike condition so that extraneous noise from mechanical vibration, creaking and squeaking is kept to a minimum; and
- ▶ Plant will be well maintained and measures taken to ensure that it is shut down in the intervening periods between work. Mechanical plant will be fitted with effective exhaust silencers, maintained in good and efficient working order and operated to minimise noise emissions. All plant will comply with the relevant statutory and manufacturers requirements.

Hoarding

4.10 The site will be secured with a hoarding around the property where required. Hoarding will accord with the following principles:

- ▶ The standard hoarding will be 2.4 metres in height;
- ▶ The hoarding will be increased in height and possibly altered in form to enhance acoustic or visual considerations for specific locations;
- ▶ Where reasonably practicable existing walls, fences, hedges and earth banks will be retained; and,
- ▶ Notices will be displayed on all site boundaries to warn of hazards on site such as deep excavations, construction access, etc.

4.11 The hoarding will also include access gates onto Barkham Ride.

Access and Parking

4.12 The hoarding will also include access gates onto Barkham Ride, which will allow vehicle to access and egress the site in forward gear.

4.13 Lights will be allocated around the development site. The lights will point downwards so as not to interfere with neighbouring properties or local wildlife. All vehicles will be guided into the designated unloading area by a banksman to ensure that vehicles are parked appropriately.

4.14 All vehicles will be required to telephone ahead to the full time Site Manager. A plan showing the route construction vehicles will take from the service station to the Application Site can be seen below in figure 4.1.

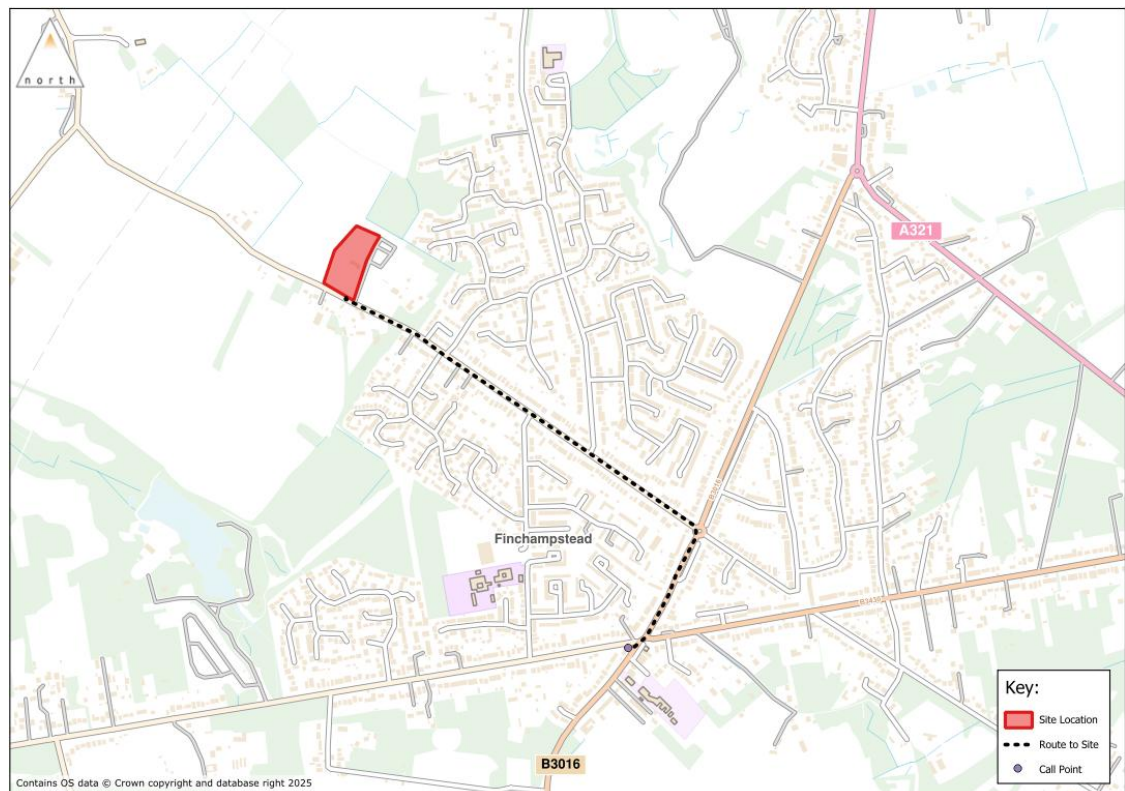


Figure 4.1 - Vehicle Route to Site

- 4.15 Vehicles accessing the site will call from the petrol station along Nine Mile Ride, then head north along the B3016 and west along Barkham Ride. The drive takes around 3 minutes.
- 4.16 Staff car parking will be provided on site. This will include 12 car parking spaces. However, all staff and visitors will be encouraged to travel via public transport, where possible. Staff will be educated in advance on sustainable travel and encourage car sharing.

5.0 HGV Activity

- 5.1 Proactive management of deliveries will be required to reduce the number of vehicle movements. All material unloading will be undertaken on site.
- 5.2 At this stage no certainty can be given as to anticipated vehicles numbers in detail.

Vehicle Activity

- 5.3 It is anticipated that during construction there will be between 10-15 deliveries per day, excluding vans.
- 5.4 Anticipated vehicles during the construction phase are set out in Table 5.1 below. This is indicative at this stage, and may vary due to alterations to the programme or particular aspects of construction.

Vehicle Type	Frequency
3-axle tipper (8.0 metres long, 2.5 metres wide, and 3.5 metres high)	On average two per day
Concrete Lorries (8.3 metres long, 2.5 metres wide, and 4.0 metres high)	On average three per day
Skip Lorries (6.3 metres long, 2.5 metres wide, and 3.7 metres high)	On average two per day
Flat-bed Truck/Panel Van (7.0 metres long, 2.4 metres wide)	On average two per day
Articulated HGV operating as a flatbed (16.5 metres long, 2.5 metres wide, and 3.7 metres high)	On average two per day

Table 5.1 – Construction Vehicle Activity

- 5.5 The movement of construction vehicles to/from the construction site will be the subject of a rigorous 'turn up, load and go' management regime. The contractor will implement a pre-booking system such that the movement of vehicles can be appropriately scheduled. It will be the responsibility of the CMP Co-ordinator to ensure that this system, together with the entire CTMP, is promoted to all workers and delivery personnel. All companies delivering goods to the site will be made aware of the contents of the CMP in advance.
- 5.6 The numbers of HGV movements to and from the site are expected to vary between the differing phases of construction. Throughout each phase, the HGV routing will remain the same, providing the shortest distance travelled on local roads.

HGV Routing

- 5.7 Larger vehicles with goods or machinery will be able to continuously access the site. Given the nature of the development, all HGVs will be able to park on site at all times.
- 5.8 All vehicles will be guided into the designated unloading area by a banksman to ensure that vehicles are parked appropriately. All vehicles will be required to telephone ahead to the full time Site Manager and will use the same route as all other vehicles as illustrated within Figure 4.1.

Loading/ Unloading Activity

- 5.9 Various construction vehicles will need to access the site at various stages throughout the development. An overview of the swept paths of various vehicles accessing the site and parking on the highway are included for reference at **Appendix B**. The drawings and swept paths include the following:
- ▶ 2301002-TK101 [Tipper];
 - ▶ 2301002-TK102 [Rigid]; and
 - ▶ 2301002-TK105 [Large Articulated HGV].

-
- 5.10 It is worth noting that the landscaping will be completed once construction has finished as this allows larger vehicles to move easier within the curtilage of the site and not cause any concerns to pedestrians or staff.
- 5.11 Mobile homes are transported in two fully built parts, it is envisaged that they would be delivered to site using the larger articulated HGV. They are then stationed on site. The static homes are then towed onto their independent pitches using a 4x4 vehicle provided by the park home supplier.
- 5.12 It is not possible for a large articulated HGV to turn on-site. As a result, two banksmen will be positioned at the site access when deliveries are taking place to both guide the HGV into the site as well as control passing vehicles on Barkham Ride to allow the HGV time to reverse into the site unhindered.
- 5.13 When parked on site, the HGV will unload the mobile home before departing the site to avoid unnecessary delay to existing residents on site. Emergency access will be maintained at all times to the existing mobile homes.
- 5.14 The email trail attached to **Appendix C** refers to the contractors method of delivery, which not only mirrors the above but is also identical to how the 25 existing mobile homes were delivered which are now operational to the east of the application site. The process would be identical to that already undertaken on the adjacent site.

Consolidation Centres

- 5.15 The construction manager will explore the potential for a delivery consolidation centre close to the site. Should this be deemed as beneficial, then the construction manager will provide WBC with further details of location.

6.0 Mitigation Measures

Wheel Washing Facilities

- 6.1 Wheel washing facilities will be accommodated on site where necessary. The contractor will operate a hose and pressure washer at the entrance/exit to prevent any dirt/dust leaving the site. Any overspill will be washed off the road surface at regular intervals.
- 6.2 Vehicles will be cleaned where necessary prior to leaving the site to minimise deposits of spoil or debris on the local highway network.

Site Waste Management Plan

- 6.3 The following on-site measures will be adopted:
 - ▶ Promotion of the reuse, recycling and recovery of waste, rather than disposal;
 - ▶ Reduce fly-tipping by keeping a full audit trail of waste removed from sites and complying with waste duty of care regulations;
 - ▶ Increase environmental awareness on the part of staff and management. Environmental management performance is likely to improve the more staff are aware of their responsibilities. Including SWMP information in induction training or as part of environmental awareness training can help with this; and,
 - ▶ There will be no burning of any waste or other materials on site.

7.0 Monitoring and Review

- 7.1 As a live document, the CMS will be reviewed and updated by the CPM Co-ordinator on a regular basis. The CPM Co-ordinator will be the first point of contact regarding the CPM and its implementation on site.
- 7.2 The CPM Co-ordinator will liaise with WBC, where appropriate to provide regular updates on the implementation of the CMS and its effectiveness.

Appendix A

Site Setup



Path (um)



12 x Car Parking Spaces

Material Storage

Staff Wellbeing


Wheel Washing Facilities

Hoarding

Rook's
Nest
Farm

CR

24



SCALE IN METRES
1:1000

Notes

1. All levels and dimensions to be checked on site before any work commences. All dimensions in metres unless stated otherwise.
2. This drawing is based on OS mapping and Motion cannot guarantee the accuracy of the data.

A	Second Issue	GL	DM	DM	16/09/2025
-	First Issue	GL	DM	DM	21/08/2025
Rev.	Description	Drm	Chk	App	Date

Drawing Status:

FOR PLANNING
NOT FOR CONSTRUCTION

motion

Guildford - Reading - London
www.motion.co.uk

Client:

A1 Roberts Properties

Project:

Barkham Road

Title:

Construction Site Setup

Scale: 1:1000 (@ A3)

Drawing:

2301002-101

Revision:

A


Appendix B

Swept Path Analysis

C:\Users\glester\Motion\StaffSite - Albark 2301002\Drawings\2301002-CTMP [2].dwg



Path (um)



Mercedes Actros Rigid Tipper 8x4 3236K
meters
Width : 2.49
Track : 2.49
Lock to Lock Time : 6.0
Steering Angle : 30.7

A	Updated	GL	DM	DM	16/09/2025
-	First Issue	GL	DM	DM	21/08/2025
Rev.	Description	Drm	Chk	App	Date

Drawing Status:

FOR PLANNING
NOT FOR CONSTRUCTION




Client:
A1 Roberts Properties

Project:
Barkham Road

Title:
**Construction Site Setup
Swept Path Analysis
Tipper**

Scale: 1:1000 (@ A3)

Drawing: **2301002-TK101** Revision: **A**





Path (um)



pond

Co Const & Ward Bdy

OIK 12

OIM 11

OIM 10

OIK 9

OIM 8

OIM 7

OIK 6

OIK 5

OIM 4

OIK 3

OIM 2

OIK 1

OIM 0

OIK 31

OHE 30

OIM 29

OHE 28

OIM 27

OHE 26

OIM 25

OHE 24

OIK 23

OIM 22

OHE 21

OIM 20

OHE 19

OIM 18

OHE 17

OIM 16

OHE 15

OIM 14

OHE 13

OIM 12

OHE 11

OIM 10

OHE 9

OIM 8

OHE 7

OIM 6

OHE 5

OIM 4

OHE 3

OIM 2

OHE 1

OIM 0

OHE 31

OIM 30

OHE 29

OIM 28

OHE 27

OIM 26

OHE 25

OIM 24

OHE 23

OIM 22

OHE 21

OIM 20

OHE 19

OIM 18

OHE 17

OIM 16

OHE 15

OIM 14

OHE 13

OIM 12

OHE 11

OIM 10

OHE 9

OIM 8

OHE 7

OIM 6

OHE 5

OIM 4

OHE 3

OIM 2

OHE 1

OIM 0

OHE 31

OIM 30

OHE 29

OIM 28

OHE 27

OIM 26

OHE 25

OIM 24

OHE 23

OIM 22

OHE 21

OIM 20

OHE 19

OIM 18

OHE 17

OIM 16

OHE 15

OIM 14

OHE 13

OIM 12

OHE 11

OIM 10

OHE 9

OIM 8

OHE 7

OIM 6

OHE 5

OIM 4

OHE 3

OIM 2

OHE 1

OIM 0

OHE 31

OIM 30

OHE 29

OIM 28

OHE 27

OIM 26

OHE 25

OIM 24

OHE 23

OIM 22

OHE 21

OIM 20

OHE 19

OIM 18

OHE 17

OIM 16

OHE 15

OIM 14

OHE 13

OIM 12

OHE 11

OIM 10

OHE 9

OIM 8

OHE 7

OIM 6

OHE 5

OIM 4

OHE 3

OIM 2

OHE 1

OIM 0

OHE 31

OIM 30

OHE 29

OIM 28

OHE 27

OIM 26

OHE 25

OIM 24

OHE 23

OIM 22

OHE 21

OIM 20

OHE 19

OIM 18

OHE 17

OIM 16

OHE 15

OIM 14

OHE 13

OIM 12

OHE 11

OIM 10

OHE 9

OIM 8

OHE 7

OIM 6

OHE 5

OIM 4

OHE 3

OIM 2

OHE 1

OIM 0

OHE 31

OIM 30

OHE 29

OIM 28

OHE 27

OIM 26

OHE 25

OIM 24

OHE 23

OIM 22

OHE 21

OIM 20

OHE 19

OIM 18

OHE 17

OIM 16

OHE 15

OIM 14

OHE 13

OIM 12

OHE 11

OIM 10

OHE 9

OIM 8

OHE 7

OIM 6

OHE 5

OIM 4

OHE 3

OIM 2

OHE 1

OIM 0

OHE 31

OIM 30

OHE 29

OIM 28

OHE 27

OIM 26

OHE 25

OIM 24

OHE 23

OIM 22

OHE 21

OIM 20

OHE 19

OIM 18

OHE 17

OIM 16

OHE 15

OIM 14

OHE 13

OIM 12

OHE 11

OIM 10

OHE 9

OIM 8

OHE 7

OIM 6

OHE 5

OIM 4

OHE 3

OIM 2

OHE 1

OIM 0

OHE 31

OIM 30

OHE 29

OIM 28

OHE 27

OIM 26

OHE 25

OIM 24

OHE 23

OIM 22

OHE 21

OIM 20

OHE 19

OIM 18

OHE 17

OIM 16

OHE 15

OIM 14

OHE 13

OIM 12

OHE 11

OIM 10

OHE 9

OIM 8

OHE 7

OIM 6

OHE 5

OIM 4

OHE 3

OIM 2

OHE 1

OIM 0

OHE 31

OIM 30

OHE 29

OIM 28

OHE 27

OIM 26

OHE 25

OIM 24

OHE 23

OIM 22

OHE 21

OIM 20

OHE 19

OIM 18

OHE 17

OIM 16

OHE 15

OIM 14

OHE 13

OIM 12

OHE 11

OIM 10

OHE 9

OIM 8

OHE 7

OIM 6

OHE 5

OIM 4

OHE 3

OIM 2

OHE 1

OIM 0

OHE 31

OIM 30

OHE 29

OIM 28

OHE 27

OIM 26

OHE 25

OIM 24

OHE 23

OIM 22

OHE 21

OIM 20


OHE 19

OIM 18

OHE 17


OIM 16

C:\Users\williammcaney\Motion\StaffSite - A1 bark_2301002\Drawings\2301002-CTMP [2]_recover.dwg

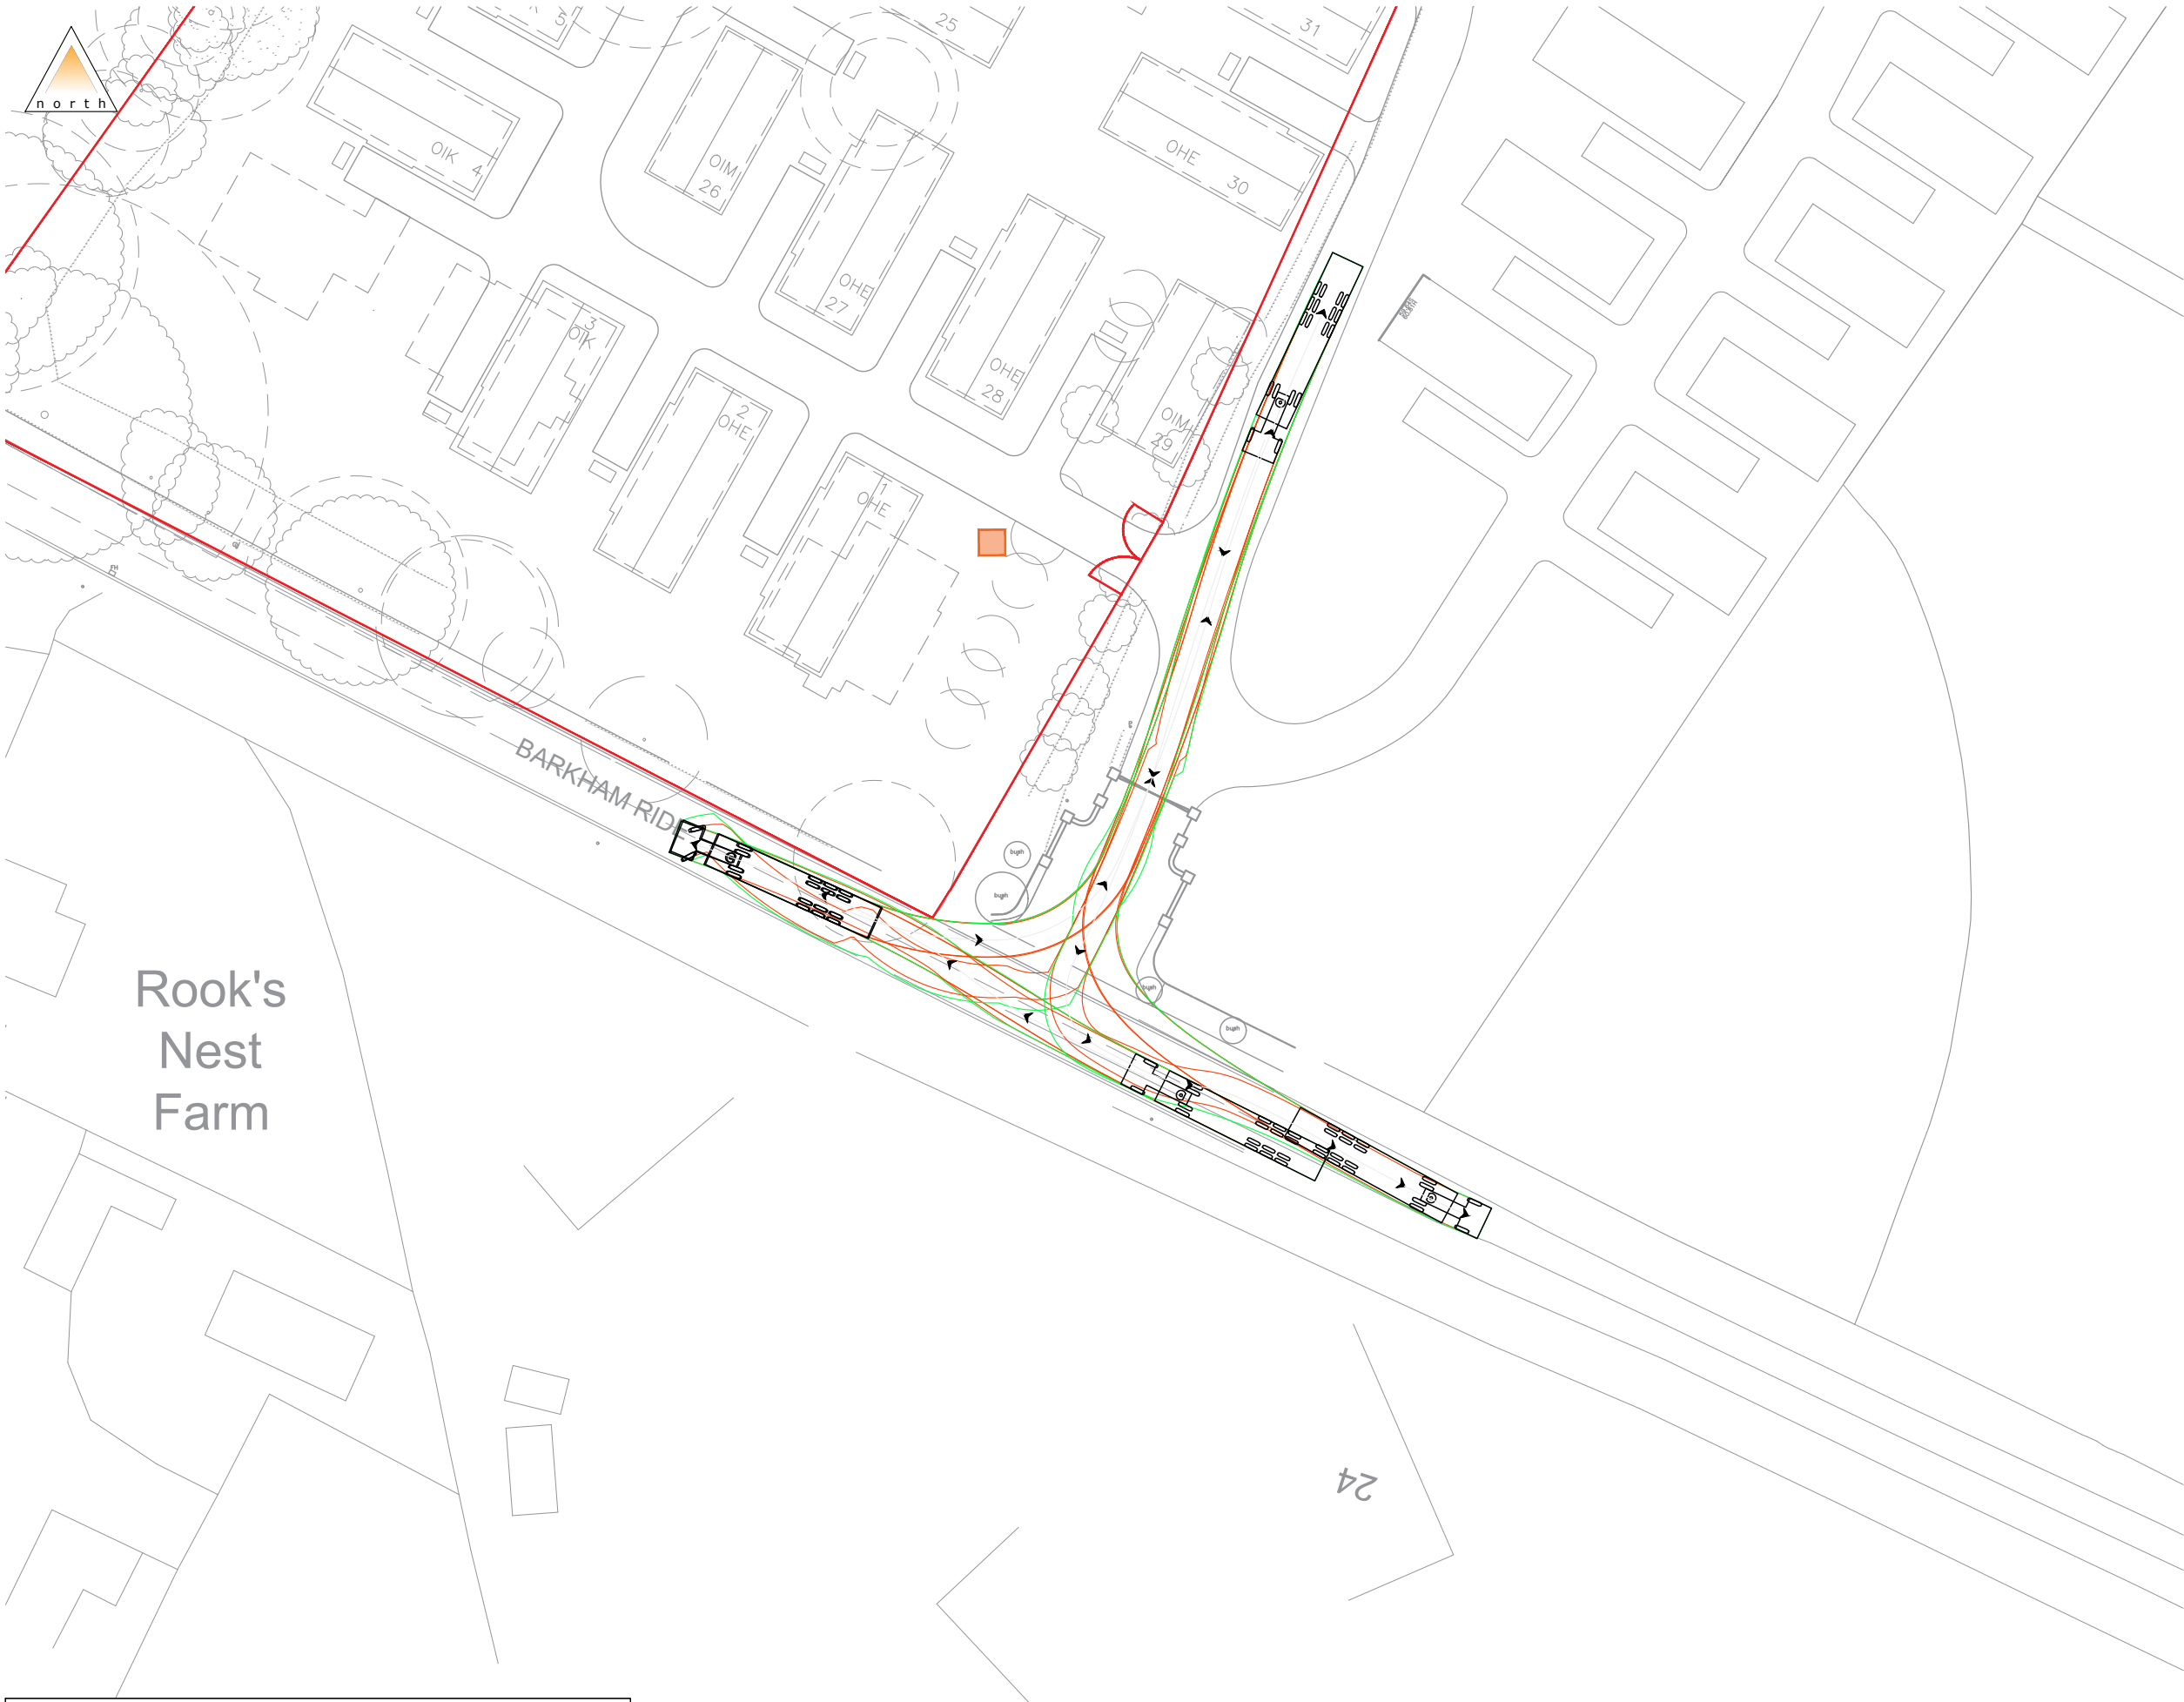

Notes

1. All levels and dimensions to be checked on site before any work commences. All dimensions in metres unless stated otherwise.
2. This drawing is based on OS mapping and Motion cannot guarantee the accuracy of the data.



Articulated Vehicle with Twin Steered Tractor

meters			
Tractor Width	: 2.55	Lock to Lock Time	: 6.0
Trailer Width	: 2.55	Steering Angle	: 41.0
Tractor Track	: 2.49	Articulating Angle	: 90.0
Trailer Track	: 2.55		

-	First Issue	WMC	DM	DM	26/09/2025
Rev.	Description	Dm	Chk	App	Date

Drawing Status:

FOR PLANNING
NOT FOR CONSTRUCTION



Guildford - Reading - London
www.motion.co.uk

Client:
A1 Roberts Properties

Project:
Barkham Road

Title:
**Construction Site Setup
Swept Path Analysis
16.5m Artic**

Scale: 1:500 (@ A3)

Drawing: **2301002-TK105** Revision: -

Appendix C

Method for Delivery – Contractors Commentary

Subject: FW: Delivery & Siting Process – Victoria Gardens

----- Forwarded message -----

From: Transport Boxhill Caravans <Transport@boxhillcaravans.co.uk>

Date: Tue, 23 Sep 2025 at 12:59

Subject: Delivery & Siting Process – Victoria Gardens

To:

Cc: Boxhill Caravans <boxhill@boxhillcaravans.co.uk>

Hi Tommy

I hope you're well.

To confirm the process for the delivery and siting of the new units at Victoria Gardens should planning permission be forthcoming, will be handled entirely by Boxhill Caravans Ltd, as with the previous phase.

Each unit will be collected in two halves from the manufacturer, Omar, and transported to site by our team using either articulated lorries or large rigid vehicles, depending on access and scheduling. We will coordinate all traffic management and escort requirements as needed to ensure safe and compliant delivery to site.

On arrival at Victoria Gardens, our drivers will reverse the vehicle into position, with the full assistance of a banksman. The banksman will be responsible for managing the manoeuvre safely, guiding the driver, and ensuring the surrounding area is clear at all times.

Once the units are unloaded, the delivery vehicle will exit the site. The units (delivered on wheels) will then be towed into final position using a 4x4 vehicle, operated by our team. We will then assemble and site the unit in its final location, ensuring it is fully positioned and joined to specification.

As you know, Boxhill Caravans Ltd carried out the delivery and siting of the first phase at Victoria Gardens (25 units), we would be pleased to continue with this next stage.

Our team is experienced and committed to delivering a professional, efficient service throughout.

If you have any questions or specific site requirements ahead of delivery, please don't hesitate to get in touch.

Many thanks

Samantha Demianow

Transport Manager

Boxhill Caravans Ltd

Old Kiln Farm, Coles Lane, Capel, Dorking RH5 5HS

Tel: 01306 712862



Members of:

LOGISTICS UK

