



DUCKWORTHS
ARBORICULTURE LTD.

BS:5837 ARBORICULTURAL REPORT

ARBORICULTURAL METHOD STATEMENT

SILVER BIRCHES
HEATH RIDE
FINCHAMPSTEAD
BERKSHIRE
RG40 3QJ

CLIENT: J. RAHI

MAY 2026

Ref: AMS 07028 / 2026

REPORT BY: SARAH DUCKWORTH

DipArb(RFS), TechCert(ArborA), M. Arbor.A, BA (Hons)
LANTRA Professional Tree Inspector

E: sarahcduckworth@hotmail.com

M: 07810 440546



Project: Permitted demolition of the existing dwelling & erection of a replacement dwelling.

Prepared by: Sarah Duckworth

Position: Arboricultural Consultant

Qualifications: DipArb(RFS),TechCert(ArborA),M. Arbor.A, BA (Hons),
LANTRA Professional Tree Inspector

File ref: AMS 07028/2026

Date Issued: 18th May 2026

Report History					
Version	Date	Author	Checked	Comments	Status
1	18/05/2026	SCD	HDT		ISSUE

CONTENTS

1.	INTRODUCTION	5
1.1	INSTRUCTION	5
1.2	SCOPE.....	5
1.3	DOCUMENTS.....	5
1.4	CAVEATS.....	5
2.	PLANNING CONSTRAINTS.....	6
2.1	TREE PRESERVATION ORDERS.....	6
2.2	CONSERVATION AREA.....	6
2.3	ANCIENT WOODLAND.....	6
3.	ARBORICULTURAL METHOD STATEMENT (AMS)	7
3.1	INTRODUCTION.....	7
3.2	SITE SUPERVISION AND MONITORING	7
3.3	ON-SITE TREE SUPERVISOR	8
3.4	TREE PROTECTION FENCING	8
3.5	TEMPORARY GROUND PROTECTION	9
3.6	CONSTRUCTION EXCLUSION ZONE	9
3.7	TREE WORKS	10
3.8	SERVICES	10
3.9	BASEMENT EXCAVATION	10
3.10	NO-DIG FOUNDATIONS.....	10
3.11	NEW BIN STORE WITHIN THE RPA OF T011 (OAK).....	11
3.12	REINSTATEMENT OF SOFT LANDSCAPING	11
3.13	NO-DIG PERMEABLE RESIN DRIVEWAY CONSTRUCTION.....	12
3.14	GENERAL CONSIDERATIONS	13
3.15	LANDSCAPING	14
3.16	UNFORESEEN CIRCUMSTANCES.....	14
	APPENDICES.....	15
	APPENDIX A - SURVEY DATA	16
	APPENDIX B - KEY.....	17
	APPENDIX C - BS:5837 (2012) TABLE 1: CASCADE CHART FOR TREE QUALITY ASSESSMENT	18
	APPENDIX D - TREE DATA.....	19
	APPENDIX E – TREE PLANS.....	23
	APPENDIX F – PHASING OF WORKS	24
	APPENDIX G – CONTACTS	25
	APPENDIX H - TREE PROTECTION FENCING	26
	APPENDIX I - TREE PROTECTION SIGNAGE	27
	APPENDIX J - QUALIFICATIONS	28

1. INTRODUCTION

1.1 INSTRUCTION

This Arboricultural report has been prepared by Sarah Duckworth, Arboricultural Consultant and provides the Arboricultural Method Statement relating to the preservation and protection of trees during the course of the permitted construction of a new replacement dwelling at Silver Birches, Heath Ride, Finchampstead, Berkshire, RG40 3QJ, following the demolition of the existing property.

The Arboricultural Method Statement and Tree Protection Plan which details the steps which will be taken to ensure significant trees can be successfully protected and retained during and on completion of the permitted building works.

1.2 SCOPE

The British Standard 5837:2012 'Trees in Relation to Design, Demolition and Construction' is designed to assist those concerned with trees and planning to form balanced judgments. This report does not therefore seek to put arguments for or against development but provides a means of protecting the trees which may be affected during development.

The report is for the sole use of the client and its reproduction or use by anyone else is forbidden unless written consent is given by the author.

1.3 DOCUMENTS

The Tree Protection Plan which accompanies this report is illustrative and should be used for dealing with tree issues only. The precise location of all tree protection measurements should be confirmed with a pre-commencement site meeting before any demolition or construction activity takes place.

1.4 CAVEATS

The report is valid for a period of two years from the date of issue being 18th May 2026 and will expire on 18th May 2028.

The report is not a Tree Risk Management Report or a Hazard Analysis Report and its use as such is invalid.

The report refers to the condition of tree(s) and an assessment of the site on the day the evaluation was undertaken. The trees were assessed from ground level only and not climbed. My assessment of third-party trees was limited where direct access was not available to the adjoining properties.

DISCLAIMER: This is an independently produced Arboricultural Report. I have no connection with any of the parties involved in this site or application that could influence or bias the opinions expressed in this report.

2. PLANNING CONSTRAINTS

2.1 TREE PRESERVATION ORDERS

I have confirmed on the Wokingham Borough Council website that there are a number of Tree Preservation Orders on trees within and directly adjacent to the curtilage of Silver Birches, Heath Ride.

No work should be undertaken to trees subject of a Tree Preservation Order without the prior written consent of the Local Planning Authority – exemptions apply.

The protected status of trees is subject to change. You are advised to reconfirm the protected status of trees prior to carrying out any works to trees on site.

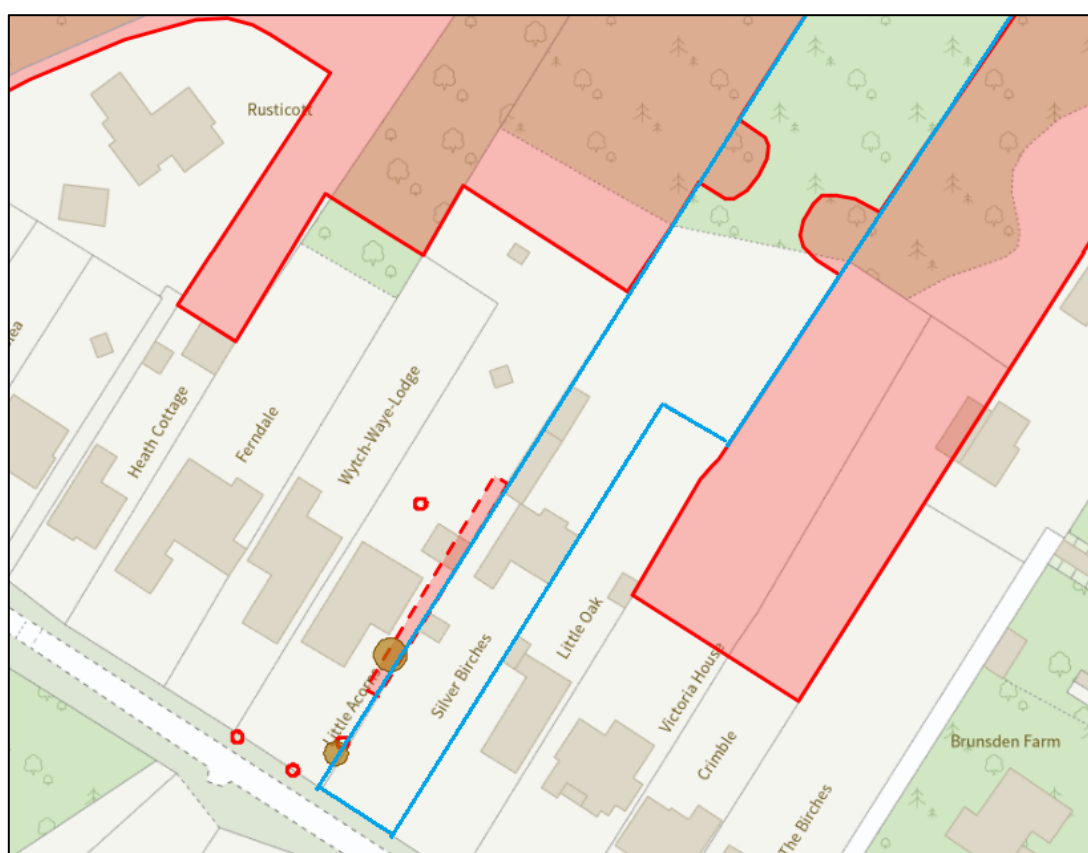


Figure 1 – Wokingham Borough Council Tree Preservation Order Information

2.2 CONSERVATION AREA

Silver Birches is not within a Conservation Area.

2.3 ANCIENT WOODLAND

Silver Birches does not include Ancient Woodland, nor is the site within an Ancient Woodland Buffer Zone.

3. ARBORICULTURAL METHOD STATEMENT (AMS)

3.1 INTRODUCTION

The correct and timely installation of tree protection measures such as tree protection fencing is critical to ensure the long-term retention of a healthy tree stock on or adjacent to the development.

This method statement will be read, approved and agreed to by all key personnel prior to the commencement of works within the site. A copy of the Arboricultural Method Statement and Tree Protection Plan will be available on site for reference.

The Arboricultural Method Statement and Tree Protection Plan once approved, will be provided to all contractors working on site, so that the practical aspects of the above precautions are included in their method statements, and financial provision made for these.

WARNING: FAILURE TO FOLLOW THE ARBORICULTURAL METHOD STATEMENT ONCE APPROVED CAN CAUSE IRREPARABLE HARM TO TREES IN CONTRAVENTION OF A TREE PRESERVATION ORDER AND MAY INVALIDATE YOUR PLANNING CONSENT.

3.2 SITE SUPERVISION AND MONITORING

In accordance with BS:5837 'Trees in Relation to Design, Demolition and Construction' 2012, there will be an auditable system of arboricultural site monitoring in place during the build.

A pre-commencement site visit will be held once the Tree Protection Fencing and temporary ground protection is installed as shown on the Tree Protection Plan. The Local Authority Tree Officer will be given a minimum of five days' notice of the time and date of the meeting so that they may attend should they wish to do so.

The purpose of the pre-commencement meeting will be for the appointed Arboricultural Consultant to confirm the location and construction of the Tree Protection Measures and ensure a common understanding of the requirements for Tree Protection within the site. If the Local Planning Authority is unable to attend, photographic evidence of the tree protection fencing will be emailed to the appointed planning officer once it has been erected.

The project arboriculturist must attend site during the following phases of development:

1. During the hand-dig excavation of footings for the front boundary wall and bin stores under an Arboricultural Watching Brief
2. During the removal of existing areas of hand landscaping at the front of the property and reinstatement with soft landscaping.
3. During the installation of the no-dig subbase of the permeable resin driveway.

A signed copy of each inspection report will be sent to Wokingham Borough Council's Planning Department following each visit.

The final site visit will be made on completion of the building works and 5-days prior to the removal of the approved tree protection measures. The appointed arboricultural consultant will review the trees and advise on any remedial works that may be required. The Local Authority Tree Officer will be given a minimum of five days' notice of the time and date of the meeting so that they may attend should they wish to do so.

3.3 ON-SITE TREE SUPERVISOR

In addition to the appointed Arboriculturist, there will be a designated on-site 'tree supervisor', a member of the build team who is responsible for ensuring no works are undertaken on site except in complete accordance with the approved Arboricultural Method Statement when the Arboricultural Consultant is not present.

The on-site tree supervisor will:

- Be present on site most of the time.
- Be aware of the arboricultural responsibilities relating to the trees on site.
- Have the authority to stop any work that will, or have the potential to, cause harm to any tree.
- Be responsible for ensuring that all site personnel are aware of their responsibilities towards trees on site and the consequences of the failure to observe those responsibilities.
- Make immediate contact with the Council and/or the retained arboriculturist in the event of any related tree problems occurring whether actual or potential.

3.4 TREE PROTECTION FENCING

No works in relation to the build will be undertaken, including construction, excavation or demolition, prior to the Tree Protection Fencing being installed as identified in the Tree Protection Plan.

The Tree Protection Fencing will consist of a vertical and horizontal scaffold framework braced well to resist impact. The vertical tubes will be spaced at a maximum distance of 3m and driven securely into the ground. Onto this framework welded mesh – 'Heras' style fencing panels or similar will be securely fixed. (See Appendix H).

All-weather signage stating 'TREE PROTECTION AREA – KEEP OUT' will be attached to the outer perimeter of the Tree Protection Fencing. A sample sign is attached in Appendix I of this report.

The fencing will be located to protect trees and their rooting areas and will remain vertical, rigid and complete during development.

At no time will Tree Protection Fencing be removed or relocated contrary to the recommendations in this report, without professional arboricultural advice and without the prior consent of the Local Authority Tree Officer.

The appointed Site Manager will notify the Arboricultural Consultant once Tree Protection Measures are installed on site.

The appointed Site Manager will also notify the Local Authority Planning Officer 5 days prior to the Protection Fencing being removed on completion of development so that a representative from the Local Authority may visit the site if considered necessary.

3.5 TEMPORARY GROUND PROTECTION

The root protection areas (RPAs) of trees are shown on the Tree Protection Plan as a continuous magenta line around each tree / tree group.

Temporary ground protection is required to create an accessible workspace at the rear of the property and when excavating the foundations for the front boundary wall within the identified root protection areas of neighbouring trees. These areas are indicated in a magenta hatch on the Tree Protection Plan.

No work in relation to the permitted building work will be undertaken, including receipt of deliveries, ground excavation or construction, prior to this Temporary Ground Protection being installed. Temporary Ground Protection must be maintained in good order until all construction operations have been completed.

Temporary ground protection will be formed of rigid load bearing temporary roadway sheets such as 'euroboards' or similar or ply sheets a minimum of 15mm thick. The temporary protection should be replaced / upgraded with an alternative product if panels start to move or any sign of ground compaction is seen.

Existing areas of hard landscaping and compacted hardcore at the front of the property will also be retained and used to protect the roots under this surface during the course of the construction works. On completion of the residential dwelling, the hard landscaping will be removed by hand within the RPA of trees and replaced with soft landscaping and / or the no-dig permeable resin drive (See Sections 3.12 & 3.13).

The storage and preparation of materials will be on existing areas of hard landscaping only and outside of the identified root protection areas (RPAs) of all trees.

3.6 CONSTRUCTION EXCLUSION ZONE

Areas behind the tree protection barriers are designated CONSTRUCTION EXCLUSION ZONES and will be isolated from all activity during permitted demolition and construction work.

Construction Exclusion Zones must remain completely undisturbed for the duration of all development works. No activity of any description including (but not limited to) the following will occur within these areas at any time:

- No excavation of any description.
- No storage, disposal of soil, rubble or materials of any other description.
- No alterations to existing levels or ground conditions.
- No vehicular access, parking or use of any tracked or wheeled machinery of any description.
- No tree works, without the written consent of the Council's Tree Service.
- No erection of temporary structures of any description.
- No storage disposal handling or use of any chemicals including cement washings.
- No fixtures or fittings of any description, security lighting, signage etc shall be attached to any part of a tree.
- No chemicals, fuel, liquids/waste residues of any other description to be stored or disposed of within close proximity to or drained towards/into protection areas.
- No storage, parking, vehicle movement or pedestrian activity, temporary or otherwise, within the construction exclusion zone at any time.

3.7 TREE WORKS

No tree works are required or proposed to facilitate the proposed building works.

3.8 SERVICES

Water, gas and electricity to the new property will be connected to those of the existing dwelling within the development footprint.

Soakaways, where required will be located 5m from the rear elevations of the property within the garden area and outside of the rooting areas of all trees.

If at any point these routes are found not to be viable, then a revised plan will be drawn up in consultation with the Arboricultural Consultant and submitted to Wokingham Borough Council for approval. There will be no trenching for services within the identified root protection area of any tree without the prior written consent of the Local Authority – Wokingham Borough Council.

3.9 BASEMENT EXCAVATION

The new basement lies outside the identified Root Protection Areas (RPAs) of all trees. Tree Protection fencing must be in place, braced and fit for purpose prior to commencement of any ground works or excavation. Tree Protection fencing must remain braced and fit for purpose for the duration of construction.

Excavated spoil and construction materials shall be stored at the front of the property and cleared from site on a regular basis to avoid the need to store large piles of earth.

Spoil will not be stored within the Root Protection Areas of retained trees or allowed to build up at the bases of trees.

Spoil will not be stored under the canopies of retained trees where lower branches may be damaged by removal plant and vehicles.

Particular care will be taken in the planning of deliveries if they require wide or tall loads and plants with booms, rigs or counterweights which can cause serious and permanent damage to trees making their safe retention impossible.

All site operations shall be managed to prevent soil compaction, contamination, and accidental damage to retained trees and their rooting environment.

3.10 NO-DIG FOUNDATIONS

Foundations for the front boundary wall will be excavated by hand under an Arboricultural Watching Brief where it sits within the root protection areas of adjacent trees.

The applicant is advised that a 'Watching Brief' cannot be fulfilled retrospectively or on completion of the development. Therefore, failure to comply with the requirements of this document during the course of the building works may invalidate your planning consent.

The appointed Arboricultural Consultant is to attend site during the ground excavation to monitor for tree roots and to be on hand in case of unforeseen Arboricultural issues. If any roots are identified within the point of excavation, they will be cut back to the edge of the trench using sharp, clean hand tools.

Proprietary cutting tools only can be used to prune roots i.e. secateurs, loppers and sharp pruning saws to prevent longitudinal shattering of roots which results in significant root damage back towards the stem of the tree.

Foundation trenches will be fully lined with a non-porous plastic membrane prior to concrete being poured. The membrane will prevent potentially toxic concrete coming into direct contact with tree roots or leaching toxic exudates which is harmful to trees.

3.11 NEW BIN STORE WITHIN THE RPA OF T011 (OAK)

The new bin store is located within the root protection area of T011 – a category ‘B’ Oak. To prevent unacceptable harm to the tree, the bin store shall be erected onto a no-dig raft foundation. This design of foundation will prevent damage to tree roots during construction.

Existing concrete within the footprint of the existing garage is to be broken up and removed from site. No excavation will be made deeper than the subbase of the existing garage.

Loose gravel and hardcore can be raked back within the build area down to the compacted soil layer below. Below the hard landscaping, existing ground levels shall be retained with no excavation, grading, or soil stripping within the RPA. Any exposed roots encountered shall be retained intact and protected in accordance with BS5837:2012.

A permeable geotextile membrane shall be laid directly onto the existing ground surface to prevent contamination and maintain soil separation.

Timber edge shuttering shall be installed to contain the raft foundation concrete pour. The shuttering shall be fixed using pinned timber pegs or a minimal above-ground restraint system designed to avoid root damage. Peg locations shall be adjusted on site to avoid any roots greater than 25mm diameter encountered during installation.

A no-fines granular sub-base (e.g. clean angular stone) shall be installed above the membrane in shallow layers and compacted using lightweight pedestrian-operated equipment only. No heavy machinery shall enter the RPA at any time.

The reinforced concrete raft slab shall be cast above existing ground level, founded entirely on the engineered no-dig sub-base.

The bin store structure shall be a lightweight wooden structure to minimise loading within the RPA.

3.12 REINSTATEMENT OF SOFT LANDSCAPING

On completion of the build, areas of hard standing either side of the access drive and compacted hardcore at the front of the site will be removed prior to the restoration of soft landscaping.

Existing hard standing will be broken up using a whacker or the toothless bucket of a long-armed excavator positioned outside of the trees’ rooting areas to pull the hardcore into site and away from the trees.

Existing concrete within the footprint of the existing garage is to be broken up and removed from site. No excavation will be made deeper than the subbase of the existing garage.

The ground in these areas will be extremely compacted. Decompaction breaks up the soil and improves water flow, aeration, nutrient accessibility, root growth and microsite availability. Decompaction will be necessary to

improve water and root penetration and to ensure the new landscape planting will successfully establish and grow in this location.

Prior to the application of topsoil, the existing ground level should be irrigated and tined to break up the upper soil crust to improve aeration. Care must be taken not to damage tree roots during these works. Any roots exposed during these works will be immediately covered with a layer of topsoil to prevent desiccation.

Once broken up, good quality topsoil will be applied to fill the required ground level and with a 200mm increase to allow for settlement.

The topsoil will have a high organic matter content to encourage earthworm activity to continue de-compacting the soil. The new topsoil layer will be porous and free draining and will improve the growing conditions for the adjacent trees. Care should be taken to ensure the topsoil and mulch do not obscure the root-flare at the base of any trees. The ground can then be seeded with grass or turfed.

There will be no vehicles tracked or otherwise working / driven / stored or parked within soft landscaped areas within the identified Root Protection Areas of any trees during these works. Each side of the driveway shall be worked on separately with the tree protection in place on the opposite side of the drive to protect trees and tree roots before and after the reinstatement of soft landscaping.

If large plant and equipment remain on site, tree protection fencing will be re-erected after the ground works to avoid damage to the newly exposed soft landscaped areas where the tree roots will be extremely vulnerable to damage. Fencing will only be permanently removed once the building is fully finished and fitted out, ready for occupation.

3.13 NO-DIG PERMEABLE RESIN DRIVEWAY CONSTRUCTION

The new driveway and parking area at the front of the dwelling will be porous and installed using a no-dig construction. Timber or aluminium edging boards will be installed to provide an upstand of approximately 200mm between the ground level and finished driveway surface to contain the porous resin surface as per the manufacturer's recommendations.

A Geotextile Fabric will be laid across the site, overlapping adjacent rolls by a minimum of 150mm. It may be necessary to lightly pin the Geotextile in place until the overlying layers are installed.

A Cell web system (such as Geosynthetics Cellweb) 150mm deep will then be opened out and pinned in place between the edging boards. Pin spacing will vary according to the site conditions but will generally be required at 1m – 2m centres on flat surfaces, mainly placed around the perimeter of the area and where adjacent sections of the cellular confinement system abut each other, with less in the middle of the area.

The open cells will be filled with clean, open graded aggregates with particles between 20mm and 45mm, (no fines) working toward the tree from the furthest point away and using the filled cells as a platform.

Once the cellular confinement subbase has been installed and filled with aggregate, the final permeable resin surface layer can be applied in accordance with the manufacturer's instruction.

Where necessary, following completion of the development, topsoil can be used to grade the edge of the surface to meet the adjacent ground levels.

Posts should be sunk to mark the edge of the driveway and prevent vehicles from leaving the driveway when maneuvering.

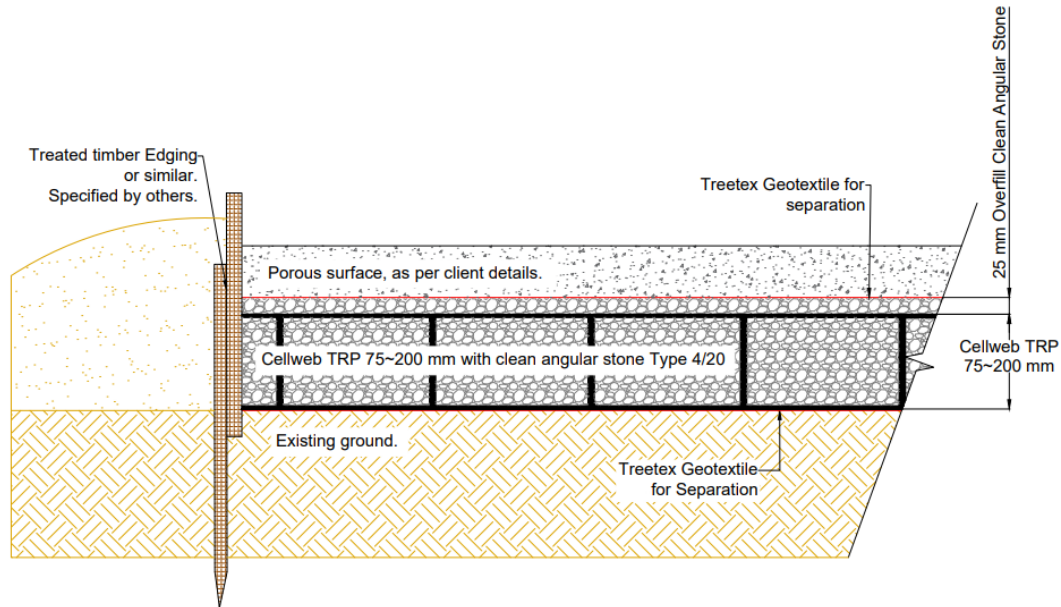


Figure 2 - Indicative no-dig driveway construction using Geosynthetics Cellweb cellular confinement subbase.

Any new patio to the rear of the property will also be within the root protection areas of trees and therefore the above no-dig installation methodology much also be adhered to.

3.14 GENERAL CONSIDERATIONS

Building foundations should be constructed in accordance with the guidelines and recommendations in HNBC Chapter 4.2 considering the presence of any potentially shrinkable clay soil and the future growth of existing trees adjacent to the property.

All storage and preparation of materials, parking, skips etc. in relation to the build will be on existing hard landscaping and outside of the identified root protection areas of all trees at all times.

Roots can be killed by pollution of the rooting area by chemicals and leaching. Loose, granular or liquid materials, including cement mix and fuel will be stored on an impermeable membrane placed outside of the rooting areas of all trees.

Particular care will be taken in the planning of deliveries if they require wide or tall loads and plants with booms, rigs or counterweights which can cause serious and permanent damage to trees making their safe retention impossible.

Any transit or traverse of plant in proximity to the trees and or tree protection barriers will be conducted under the supervision of a banksman to ensure that adequate clearance from trees is maintained at all times.

Materials will be delivered to site regularly in small quantities in order to keep vehicle delivery sizes small and on-site storage to an absolute minimum.

There will be no open fires on site during the building works.

3.15 LANDSCAPING

The following rules will be followed during all future landscaping works:

- Tree roots can be damaged by severance, compaction, pollution and desiccation. In view of this, there should be no excavation or changes in ground levels within the identified rooting areas of trees following completion of the development.
- Any electrical ducts to gates or external lights will be routed outside of the root protection area of all trees. There will be no open trenching within the root protection areas of any tree at any time during or on completion of the building and associated landscaping work.
- On completion of the build, new fence panels should include holes or gaps at ground level a minimum of 100x100mm to allow small mammals such as hedgehogs to forage within the property.
- Where new fencing is proposed, post holes within the rooting areas of trees will be dug using a post hole digger to keep hole size to a minimum. Where substantial roots over 30mm are encountered, the location of the hole will be moved in order to avoid them. Post holes will be fully lined in order to prevent concrete coming into direct contact with tree roots.

3.16 UNFORESEEN CIRCUMSTANCES

In the event of unforeseen circumstances whereby it is not possible to work in accordance with the Arboricultural Method Statement, then advice should be sought immediately from a qualified Arboriculturist.

THERE SHALL BE NO DEVIATION FROM THIS METHOD STATEMENT WITHOUT CONSULTATION WITH A QUALIFIED ARBORICULTURIST AND / OR THE WRITTEN CONSENT OF THE LOCAL PLANNING AUTHORITY.

APPENDICES

- A. Survey Data
- B. Key
- C. Cascade Chart for Tree Quality Assessment
- D. Tree Data
- E. Tree Plans
- F. Phasing of works
- G. Contacts
- H. Tree Protection Fencing
- I. Tree Protection Signage
- J. Qualifications

APPENDIX A - SURVEY DATA

- The trees were surveyed on Tuesday 12th August 2025 from ground level only.
- On the day of the survey the weather was bright and sunny. Visibility was good.
- Heights were estimated as part of a group. Soil samples were not taken.
- The tree survey identified 35 trees and 2 tree groups growing on or adjacent to the site which were relevant to this planning application.
- The trees on site were assessed for their quality and benefits within the context of the approved development and categorised in accordance with the recommendations in the BS: 5837:2012 – ‘Trees in Relation to Design, Demolition and Construction’.

APPENDIX B - KEY

Ref:	T001 = Tree 1	G001 = Group 1
	A001 = Area 1	W001 = Woodland 1
Species:	Common name (Botanical name)	
Height:	Measured with a clinometer (m) where possible or estimated when part of a group	
Stem:	Stem diameter taken at 1.5m with girth tape or rule and recorded in millimeters	
Branch spread:	Paced measurements at compass points or with a laser measure.	
Crown clearance:	Existing height above ground level of canopy and / or first significant branch direction of growth in metres e.g., 2.4 (N) where relevant.	
Epics:	Lower canopy created by epicormic growth.	
Age Class:	Newly planted - 3 years following planting.	
	Young - Tree well established but with juvenile crown form	
	Young Mature - Tree in first third of usual life expectancy for species	
	Mature - Tree in second third of usual life expectancy for species	
	Over Mature - Tree in final third of usual life expectancy for species / exhibiting signs of crown retrenchment & senescence.	
	Veteran - Older than usual for species or with historical/ cultural / ecological value	
General Observations:	Made with reference to physiological condition (health, vigour) and structural condition, noting evidence of decay, structural weakness and physical defect and preliminary management recommendations.	
Estimated Remaining Contribution:	Estimated in years - less than 10, 10-20, 20-40, 40+	
BS: 5837:2012 category rating:	In accordance with the guidelines of the British Standard.	
	 Category 'A' tree (Green)	 Category 'C' tree (Grey)
	 Category 'B' tree (Blue)	 Category 'U' tree – Fell (Red)
RPA Area	BS:5837 (2012) Root Protection Area calculation in square metres	
RPA Radius	BS:5837 (2012) Root Protection Area calculation circle radius in metres. ¹	

¹ The root protection area radius is for information only and may not be appropriate in every case. BS:5837 advises that *'the RPA for each tree should initially be plotted as a circle centered on the base of the stem. Where pre-existing site conditions or other factors indicate that rooting may have occurred asymmetrically, a polygon of equivalent area should be produced. Modifications to the shape of the RPA should reflect a soundly based arboricultural assessment of likely root distributions.'*

APPENDIX C - BS:5837 (2012) TABLE 1: CASCADE CHART FOR TREE QUALITY ASSESSMENT

CATEGORY & DEFINITION	CRITERIA (including sub-categories where appropriate)		
Trees unsuitable for retention			
Category 'U' Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years.	Trees that have a serious, irremediable, structural defect such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g., where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning. Trees that are dead or showing signs of significant, immediate, and irreversible overall decline. Trees infected with pathogens of significance to the health and / or safety of other trees nearby or very low-quality trees suppressing adjacent trees of better quality. NOTE: Category U trees can have existing or potential conservation value which it might be desirable to preserve		
	Mainly Arboricultural Qualities	Mainly Landscape Qualities	Mainly cultural values including conservation
Trees considered suitable for retention			
Category 'A' Trees of High Quality with an estimated remaining life expectancy of at least 40 years.	Trees that are particularly good examples of their species especially if rare or unusual; or those that are essential components of groups or formal or semi-formal arboricultural features (e.g. the dominant and / or principal trees within an avenue)	Trees, groups, or woodlands of particular visual importance as arboricultural and / or landscape features.	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood pasture)
Category 'B' Trees of Moderate Quality with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g., presence of significant though remedial defects, including unsympathetic past management and storm damage), such that they are unlikely to be suitable for retention for beyond 40 years; or trees lacking the special quality to merit the category 'A' designation.	Trees present in numbers, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals; or trees occurring as collectives but situated so as to make little contribution to the wider locality.	Trees with material conservation or other cultural value.
Category 'C' Trees of Low Quality with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150mm.	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories.	Trees are present in groups or woodlands but without this conferring on them significantly greater collective landscape value; and/ or trees offering low or only temporary / transient landscape benefits.	Trees with no material conservation or other cultural value.

APPENDIX D - TREE DATA

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
G001	Leyland cypress (<i>X Cuprocyparis leylandii</i>)	Group	Height (m): 3 Stem Diam(mm): 100 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 20+ Years	N:0.5 E:0.5 S:0.5 W:0.5	Tight clipped off-site hedge.	C2	Area: 84 sq m.	Physiological Condition: Good Structural Condition: Unknown Public Amenity Value: Low Inspection Limitations: Access
G002	Chinese juniper x11 (<i>Juniperus chinensis</i>)	Group 11 trees	Height (m): 3.5 11 stems, avg.(mm): 100 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 20+ Years	N:0.5 E:0.5 S:0.5 W:0.5	Off-site hedge. Poor form. Browning on west side where previously suppressed by dense vegetation.	C1	Area: 38 sq m.	Physiological Condition: Poor Structural Condition: Fair Public Amenity Value: Low
T001	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 16 Stem Diam(mm): 400 Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:6 S:6 W:5	Off-site tree. Ivy clad.	B2	Radius: 4.8m. Area: 72 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good Inspection Limitations: Access
T002	Turkey oak (<i>Quercus cerris</i>)	Tree	Height (m): 18 Stem Diam(mm): 400 Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: 40+ Years	N:8 E:10 S:9 W:8	Off-site tree. Broad crown.	B2	Radius: 4.8m. Area: 72 sq m.	Physiological Condition: Good Structural Condition: Unknown Public Amenity Value: High Inspection Limitations: Access
T003	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 15 Stem Diam(mm): 690 Crown Clearance (m): 7 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:3 S:4 W:4	Mature tree. Crown lifted. Needles dense and even.	B2	Radius: 8.3m. Area: 216 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate
T004	Aspen (<i>Populus tremula</i>)	Tree	Height (m): 16 Stem Diam(mm): 390 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 20+ Years	N:5.5 E:5.5 S:3 W:5.5	Slender tree, high crown.	B2	Radius: 4.7m. Area: 69 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T005	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 150 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Small tree, slender high crown.	C2	Radius: 1.8m. Area: 10 sq m.	Physiological Condition: Fair Structural Condition: Unknown Public Amenity Value: Moderate Inspection Limitations: Access
T006	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 320 Crown Clearance (m): 7 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2.5 E:3 S:2 W:4	Off-site tree, canopy in decline.	C2	Radius: 3.8m. Area: 45 sq m.	Physiological Condition: Poor Structural Condition: Unknown Public Amenity Value: Moderate Inspection Limitations: Access

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T007	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 170 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Small tree, slender high crown.	C2	Radius: 1.8m. Area: 10 sq m.	Physiological Condition: Fair Structural Condition: Unknown Public Amenity Value: Moderate Inspection Limitations: Access
T008	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 120 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1 E:5 S:1 W:1	Small tree in dense group. Leaning trunk over Silver Birches garage. Apical Dieback in crown.	C2	Radius: 1.4m. Area: 6 sq m.	Physiological Condition: Fair Structural Condition: Unknown Public Amenity Value: Moderate Inspection Limitations: Access
T009	Common holly (<i>Ilex aquifolium</i>)	Tree	Height (m): 8 Stem Diam(mm): 100 Crown Clearance (m): 2.5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:2 S:1.5 W:1.5	Off-site tree. Slender feathered form.	C1	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T010	Common holly (<i>Ilex aquifolium</i>)	Tree	Height (m): 8 Stem Diam(mm): 90 Crown Clearance (m): 2.5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Off-site tree. Slender feathered form.	C1	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T011	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 14 Stem Diam(mm): 460 Crown Clearance (m): 3 Life Stage: Mature Rem. Contrib.: 20+ Years	N:5 E:5 S:4 W:4.5	Off-site tree. Low crown over existing outbuilding.	B1,2	Radius: 5.5m. Area: 95 sq m.	Physiological Condition: Good Structural Condition: Unknown Public Amenity Value: Good Inspection Limitations: Access
T012	English yew (<i>Taxus baccata</i>)	Tree	Height (m): 6.5 Stem Diam(mm): 280 Crown Clearance (m): 1.5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2 E:2 S:2.5 W:1	Small off-site tree. No wider amenity value	C2	Radius: 3.4m. Area: 36 sq m.	Physiological Condition: Fair Structural Condition: Unknown Public Amenity Value: Low Inspection Limitations: Access
T013	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 17 Stem Diam(mm): 690 Crown Clearance (m): 2 Rem. Contrib.: 40+ Years	N:3 E:4 S:8 W:7	Off-site tree. Kinked trunk. Asymmetrical crown. Deadwood.	B1	Radius: 8.3m. Area: 216 sq m.	Physiological Condition: Fair Structural Condition: Sunken Public Amenity Value: Moderate Inspection Limitations: Access
T014	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 17 Stem Diam(mm): 520 Crown Clearance (m): 2 Rem. Contrib.: 40+ Years	N:3 E:3 S:8 W:7	Off-site tree. Crown lifted. Suppressed, oval crown.	B1	Radius: 6.2m. Area: 121 sq m.	Physiological Condition: Fair Structural Condition: Sunken Public Amenity Value: Moderate Inspection Limitations: Access
T015	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 17 Stem Diam(mm): 650 Crown Clearance (m): 2 Rem. Contrib.: 40+ Years	N:8 E:6 S:7 W:6	Off-site tree. Suppressed, asymmetrical crown.	B1	Radius: 7.8m. Area: 191 sq m.	Physiological Condition: Fair Structural Condition: Sunken Public Amenity Value: Moderate Inspection Limitations: Access

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T016	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 610 Crown Clearance (m): 3.5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:4 W:2	Needle density normal. Form usual for species.	B2	Radius: 7.3m. Area: 167 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T017	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 570 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2 E:7 S:3 W:1	Swept stem, kinked upper trunk. Needle density normal. Form usual for species.	B2	Radius: 6.8m. Area: 145 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T018	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 550 Crown Clearance (m): 9 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	Needle density normal. Form usual for species. Collective amenity value.	B2	Radius: 6.6m. Area: 137 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T019	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 460 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:1 E:4 S:3 W:0	Swept stem, asymmetrical crown. Needle density normal. Form usual for species. Collective amenity value.	B2	Radius: 5.5m. Area: 95 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T020	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 380 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2 E:2 S:2 W:2	Needle density normal. Form usual for species. Collective amenity value.	B2	Radius: 4.6m. Area: 66 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T021	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 470 Crown Clearance (m): 13 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:1 S:1 W:3	Needle density normal. Asymmetrical upper crown. Collective amenity value.	B2	Radius: 5.6m. Area: 99 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T022	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 430 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:1 E:1 S:2.5 W:3	Needle density normal. Form usual for species. Collective amenity value.	B2	Radius: 5.2m. Area: 85 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T023	Norway spruce (<i>Picea abies</i>)	Tree	Height (m): 8 Stem Diam(mm): 90 Life Stage: Semi Mature Rem. Contrib.: 20+ Years	N:2 E:2 S:2.5 W:2	Small tree, low feathered crown.	C2	Radius: 1.1m. Area: 4 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Dense vegetation
T024	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 620 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3.5 E:2 S:5 W:2	Swept stem. Asymmetrical lower trunk. Needle density normal. Collective amenity value.	B2	Radius: 7.4m. Area: 172 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T025	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 460 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	Needle density normal. Collective amenity value.	B2	Radius: 5.5m. Area: 95 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T026	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 530 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4.5 E:3.5 S:3 W:2	Needle density normal. Collective amenity value.	B2	Radius: 6.4m. Area: 129 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T027	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 480 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:1 S:3 W:3	Needle density normal. Collective amenity value.	B2	Radius: 5.8m. Area: 106 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T028	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 350 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:1.5 E:1 S:1.5 W:1	Needle density normal. Collective amenity value.	B2	Radius: 4.2m. Area: 55 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T029	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 490 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4 E:2 S:3.5 W:3	Superficial bark wounds on trunk. Needle density normal. Collective amenity value.	B2	Radius: 5.9m. Area: 109 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T030	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 520 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:6 E:6 S:1.5 W:2	Asymmetrical crown. Needle density normal. Collective amenity value.	B2	Radius: 6.2m. Area: 121 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T031	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 600 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:7 S:3 W:2	Superficial bark wounds on trunk. Needle density normal. Collective amenity value.	B2	Radius: 7.2m. Area: 163 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T032	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 16 Stem Diam(mm): 530 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4 E:1 S:3 W:3.5	Mature tree, asymmetrical crown.	B2	Radius: 6.4m. Area: 129 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate
T033	Pedunculate oak (<i>Quercus robur</i>)	Tree	1 stems Crown Clearance (m): 1.5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:7 E:8.5 S:6.5 W:5	Mature tree, asymmetrical crown. Superficial damage to buttress roots.	B2	No RPA.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good

APPENDIX E – TREE PLANS

Attached as separate pdf documents

- Tree Protection Plan ref: [SILVER BIRCHES TPP 07028 2026](#)

APPENDIX F – PHASING OF WORKS

STAGE 1 (PRE-COMMENCEMENT)

INSTALLATION OF TREE PROTECTION FENCING
& TEMPORARY GROUND PROTECTION



SITE MEETING TO SIGN OFF TREE PROTECTION FENCING
(NOTIFY LOCAL AUTHORITY -MIN 5 DAYS)



STAGE 2 (DEMOLITION & CONSTRUCTION)

DEMOLITION OF EXISTING STRUCTURES



EXCAVATION OF BASEMENT &
CONSTRUCTION OF REPLACEMENT DWELLING



TREE PROTECTION MEASURES TO REMAIN RIGID AND INTACT
THROUGHOUT BUILD WORKS.



STAGE 3 (POST DEVELOPMENT)

HAND DIG FOUNDATIONS FOR FRONT BOUNDARY WALL
UNDER ABORICULTURAL WATCHING BRIEF



CAREFULLY REMOVE HARD LANDSCAPING
WITHIN RPA OF TREES AT THE FRONT OF PROPERTY PRIOR TO
REINSTATEMENT OF SOFT LANDSCAPING
(REPLACE TREE PROTECTION FENCING AFTER THESE WORKS)



INSTALL NO-DIG BIN STORE



INSTALL PERMEABLE RESIN DRIVE ON NO-DIG SUBBASE



FINAL SITE VISIT FROM ARB CONSULTANT TO SIGN OFF
TREE PROTECTION FENCING & TEMPORARY GROUND PROTECTION PRIOR TO REMOVAL
(NOTIFY LOCAL AUTHORITY -MIN 5 DAYS)

APPENDIX G – CONTACTS

Arboricultural Consultant

Sarah Duckworth

Glebelands Bungalow

Mildenhall

Marlborough

Wiltshire

SN8 2LR

E: sarahcduckworth@hotmail.com

M: 07810 440546

Architect

The Keen Partnership

The Courtyard

Edinburgh Road

Reading

Berkshire

RG30 2UA


T: 01189 510 855

Local Planning Authority

Wokingham Borough Council

T: 0118 974 6000

APPENDIX H - TREE PROTECTION FENCING

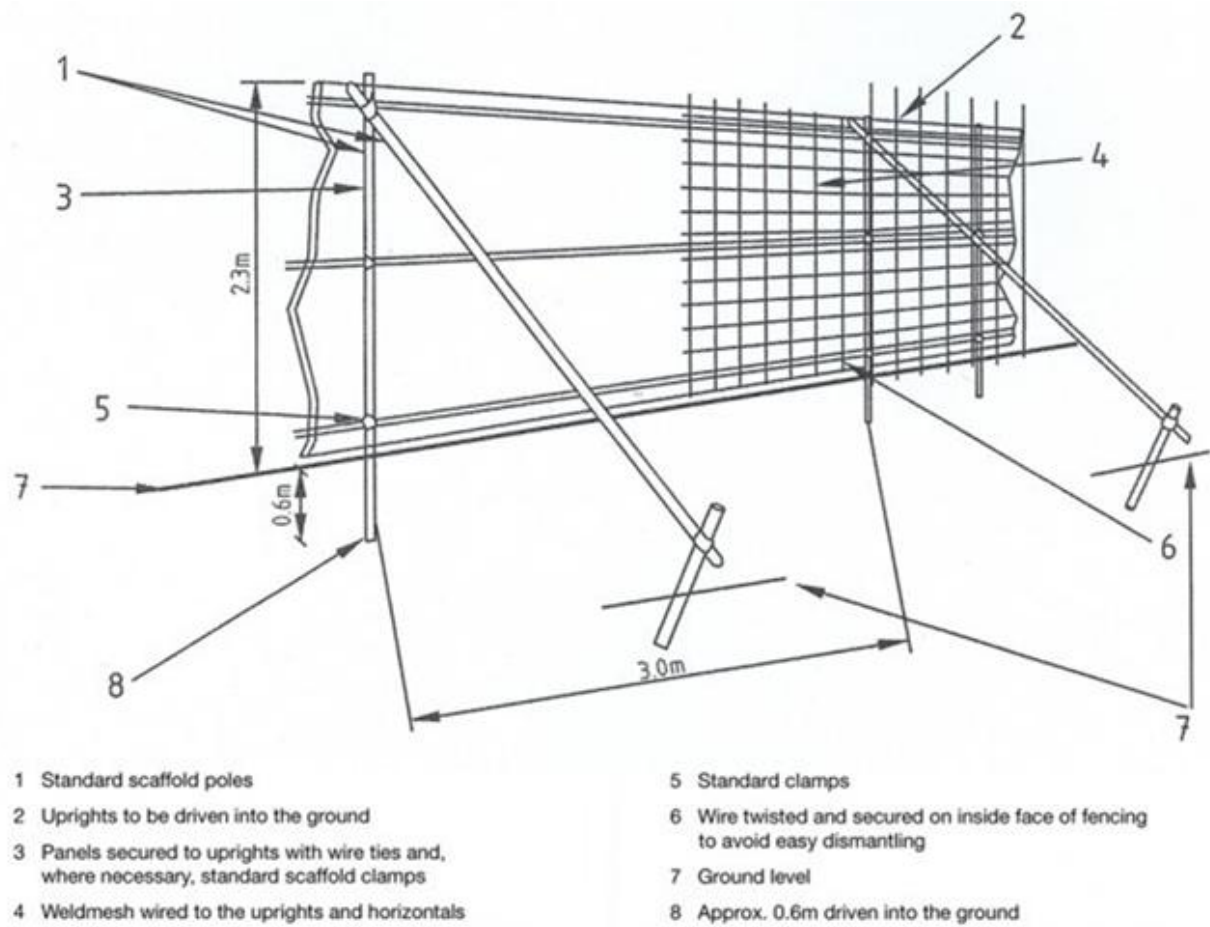



**TREE PROTECTION AREA
KEEP OUT !**

**(TOWN & COUNTRY PLANNING ACT 1990)
TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY
PLANNING CONDITIONS AND/OR ARE THE SUBJECTS OF
A TREE PRESERVATION ORDER.
CONTRAVENTION OF A TREE PRESERVATION ORDER MAY
LEAD TO CRIMINAL PROSECUTION.**

**ANY INCURSION INTO THE PROTECTED AREA MUST BE
WITH THE WRITTEN PERMISSION OF THE LOCAL
PLANNING AUTHORITY.**

APPENDIX J - QUALIFICATIONS

This Arboricultural report has been prepared by Sarah Duckworth, Independent Arboricultural Consultant, trading as Duckworth's Arboriculture Limited.

I have over 20 years' experience working in the field of Arboriculture and for the past 17 years I have worked as a Local Authority Tree Officer both directly and independently providing contracted support. Since 2010 I have worked as a private consultant carrying out a range of Arboricultural Reports and Assessments for private clients.

I hold the Royal Forestry Society's Professional Diploma (Level 6) for which I received the Lockhart Garrett Award. I also hold the Arboricultural Association's Technicians Certificate (with Distinction).

I am a LANTRA qualified Professional Tree Inspector and a Professional Member of the Arboricultural Association.
