



ALLARBORICULTURE

23 Southernhay Avenue, Bristol, BS8 4TJ

07375110399 | 0800 107 3652

e – info@allarboriculture.co.uk

ARBORICULTURAL IMPACT ASSESSMENT AND METHOD STATEMENT

BS5837:2012

On behalf of:
Mr S Kendrick
Land adjacent 12
Shepherds Hill,
Earley,
RG6 1BB

Prepared by:
Kristian
Chesterman BSc
(Hons)

Report Reference:
AAAIA12SH

Report Date:
24th January 2025

Contents

Chapters	Content	Page no.
1.0	Instruction	3
2.0	Statement Of Purpose	3
3.0	Associated Documents	3
4.0	Site Description	3
5.0	Vegetation Description	3
6.0	Arboricultural Impact Assessment	4
7.0	Method Statement	6
Appendix 1	Tree Survey Schedule	
Appendix 2	Protection	
Appendix 3	Tree Protection Plan	

1.0 Instruction

All Arboriculture has been instructed by Mr S Kendrick to undertake a tree survey in accordance with BS5837:2012 *Trees In relation to design, demolition and construction – Recommendations*, and to produce an Arboricultural Impact Assessment, Arboricultural Method Statement and Tree Protection Plan. The instruction was received on the 20th August 2024. The tree survey was carried out on the 22nd August 2024.

2.0 Statement of purpose

The purpose of this report is to provide local planning authorities with sufficient arboricultural information to consider the effect of the proposed development on nearby trees, and to demonstrate that trees have been carefully considered throughout the development process.

The report includes an arboricultural method statement that describes how work will be undertaken to provide adequate protection of retained trees.

3.0 Associated documents and drawings

This report should be read in conjunction with the following documents and drawings:

1. 24-896_WD_12 Shepherds Hill_24-11-11-ACCESS
2. British Standards Institute - BS5837:2012 *Trees in relation to design, demolition and construction – Recommendations*
3. Tree Protection Plan – AATPP12SH

4.0 Site description

The site is in the urban area of Earley and is land. The proposal is the erection of a residential dwelling. The site falls under the jurisdiction of Wokingham Borough Council and it was unclear from their website if the trees are subject to a Tree Preservation Order or within a conservation area.

5.0 Vegetation description

The vegetation consists of 10 off site category C trees. They are all very low quality self seeded Ash trees that have been reduced to 0.5m and have then regenerated.

Some tree protection measures and working methodology (in accordance with BS 5837:2012) will ensure they are not detrimentally affected during construction.

6.0 Arboricultural impact assessment

Table 1: Summary of impacts	
Tree removal	T1, T2, T4, T5, T6, T7, T8, T9
Facilitation pruning	None
Demolition within RPA	None
New surfacing within RPA	None
New structures within RPA	None

Building construction in relation to tree roots: The removal of T1, T2, T4, T5, T6, T7, T8, T9 will be required to facilitate the development. These trees are all poor quality self seeded specimens. Following removal, traditional construction methods may be used.

Building construction in relation to tree crowns: No facilitation pruning is required. It is important that sufficient growing space is allowed between the crown extent of each tree and the roof edge of the proposed structures. This is to reduce conflicts of interest in the future and to reduce the pressure to prune trees to keep them clear of roofs: A clearance of two metres from the mature tree crown is generally considered acceptable which is the case with this proposal.

Tree root and canopy protection: The RPA (Root protection area) of the retained trees should be protected during the development phase with heras fencing and/or ground protection to ensure heavy machinery is not operated, or materials stored within the rooting area. This can be detrimental to the trees, causing soil compaction and root die back. The protection of the RPA and canopy spread is detailed in the Arboricultural Method Statement below.

Special surfacing: Special surfacing will not be required.

Materials delivery, storage and handling: Materials should not be handled or stored within the RPA's of retained trees; the load exerted can result in soil compaction and leachate from spills can be toxic to trees.

Surface drains, soakaways and services: It is important that services, surface drains and soakaways avoid the RPA's of retained trees as roots can be damaged during trench excavations. Services will be connected to the existing and therefor will have no impact.

7.0 Arboricultural method statement

Implementation and phasing of the proposed development: Prior to any building work commencing on site, a meeting will be held with the tree consultant and site manager present. During the meeting details regarding the location of heras fencing and ground protection will be discussed and a time to reconvene in order to assess the heras fencing and ground protection will be agreed. The schedule of events during the development phase will be as follows:

Heras fencing will be installed as indicated in plan AATPP12SH.

During the development phase, the arboricultural consultant will be notified and asked to supervise any excavating within the RPA's of retained trees.

Tree protection barriers: Protective fencing will be installed prior to the commencement of any development activity and will be retained in the positions shown on the tree protection plan (AATPP12SH). The fencing will be to the BS 5837:2012 'Trees in relation to design, demolition and construction – recommendations' (section 6.2) i.e. preformed galvanised steel mesh panels ('Heras' or similar) facings on a driven braced scaffold pole framework. It will be retained at the locations shown until construction is completed. It may be moved or removed only with notice to and consent from the local planning authority.

Ground protection: Ground protection will not be required.

Storage and handling of materials: This site has sufficient space for materials to be stored and handled.

Contractors parking: There is sufficient space on site for parking and London Road.

Welfare facilities: There is sufficient space for temporary facilities onsite.

Surface drains, soakaways and services: RPA's will be avoided and there is sufficient space for services outside of the retained trees RPA's.

Supervision: The project arboriculturalist will attend the site to inspect the heras fencing and ensure that it has been laid out as prescribed in the method statement and meets the requirements of BS5837:12.

Tree works: The removal of T1, T2, T4, T5, T6, T7, T8, T9 are required. All tree work shall be carried out in accordance with BS 3998:2010 Tree Works - Recommendations by suitably qualified personnel.

Tree planting: It is respectfully suggested that if additional tree planting is required then this should be secured through an appropriately worded planning condition.

Sequencing of works

1. Tree works
2. Installation of Tree Protective Fencing as shown on the TPP.
3. Arboricultural Consultant to check Tree Protection at this stage.
4. Main construction phase
5. Remove tree protection when all construction activity has ended.
6. Carry out landscaping works (if required).
7. Completion

Contacts

Architect and Agent:

Name:

Tel:

E:

Arboricultural Consultant:

Name: K Chesterman

Tel: 07375110399

E: info@allarboriculture.co.uk

APPENDIX 1 - Tree Schedule Schedule

Tree No	Species	Height (m)	Trunk Diameter (cm)	Crown spread (m)		Crown height above ground (m)	Life stage	General observations	BS 5837 cat	Root protection area (m)
1	Ash <i>Fraxinus excelsior</i>	6	22	1	1	1	Early Mature	Self seeded. Co dominant. Previously reduced. Off site tree.	C	2.6
				1	1					
2	Ash <i>Fraxinus excelsior</i>	6	11	1	1	2	Semi Mature	Self seeded. Co dominant. Previously reduced. Off site tree.	C	1.3
				1	1					
3	Ash <i>Fraxinus excelsior</i>	6	16	1	1	1	Early Mature	Self seeded. Co dominant. Previously reduced. Off site tree.	C	1.9
				1	1					
4	Ash <i>Fraxinus excelsior</i>	5	13	1	1	1	Early Mature	Self seeded. Off site tree.	C	1.5
				1	1					
5	Ash <i>Fraxinus excelsior</i>	5	7	1	1	1	Semi Mature	Self seeded. Off site tree.	C	0.8
				1	1					
6	Ash <i>Fraxinus excelsior</i>	6	10	1	1	1	Semi Mature	Self seeded. Co dominant. Previously reduced. Off site tree.	C	1.5
			8	1	1					

Tree No	Species	Height (m)	Trunk Diameter (cm)	Crown spread (m)		Crown height above ground (m)	Life stage	General observations	BS 5837 cat	Root protection area (m)
7	Ash <i>Fraxinus excelsior</i>	6	23	2	2	2	Early Mature	Previously reduced. Off site tree.	C	2.7
				2	2					
8	Ash <i>Fraxinus excelsior</i>	6	18	1	1	2	Early Mature	Self seeded. Co dominant. Previously reduced. Off site tree.	C	6.4
				1	1					
9	Ash <i>Fraxinus excelsior</i>	8	8	1	1	1	Semi Mature	Self seeded. Co dominant. Previously reduced. Off site tree.	C	0.9
				1	1					
10	Ash <i>Fraxinus excelsior</i>	9	30	2	3	2	Early Mature	Off site tree.	C	3.6
				3	3					

APPENDIX 1 - Tree Schedule Schedule

Survey Key

Diameter (mm)

Stem diameter in millimetres measured at 1.5m above ground level. Where the stem is divided below 1.5m, measurement is taken as directed by BS:5837 Annex

C. RPA - Root Protection Area

RPA circle radius is determined from Annex D of BS:5837. R- Radius

A – Area

Branch Spread (m)

Radial crown spread in metres, measured for each of the four cardinal points of the compass from the centre of the trunk. Low branches

N E
W S

Height above ground in metres of the lowest branch and use of the 4 cardinal points of the compass.

Age class

(NP) Newly planted – a tree within 3 years after planting

(Y) Young – a tree within its first one third of life expectancy

(EM) Early Mature – a tree within its second third of life expectancy

(M) Mature – a tree in its final one third of life expectancy

(OM) Over Mature – a tree having reached its maximum life span and is declining in health and size due to old age

(V) Veteran – a tree in the second or mature stage of its life and has important wildlife and habitat features including; hollowing or associated decay fungi, holes, wounds and large dead branches.

(A) Ancient – a tree in the ancient or third and final stage of their life that is of interest biologically, aesthetically or culturally because of its age, size and condition

Physiological Condition

GOOD – a tree in a healthy condition with no significant problems

FAIR – a tree generally in good health with some problems that can be remediated POOR – a tree in poor health with significant problems that can't be remediated DEAD – a tree without sufficient live material to sustain life

Structural Condition

An assessment of the structural/safe condition of the tree categorised into:

GOOD – a tree in a safe condition with no significant defects

FAIR – a tree in a safe condition at present but with defects or with significant defects that can be remediated POOR – a tree with significant defects that can't be remediated.

EC - Estimated remaining contribution in years (based on the species and its current condition)

<10 Up to 10 years

10+ 10 years or more

20+ 20 years or more

40+ 40 years or more

Category (Tree quality assessment)

Category U – Tree in poor condition that cannot realistically be retained for longer

than 10 years Category A – Trees of high quality

Category B – Trees of moderate quality Category


C – Trees of low quality

APPENDIX 2 – Protective Fencing


Protective fencing should be erected before any construction commences on site. It should also be in position to protect important trees prior to demolition.

Protective fencing should stay in position until all construction activity has finished.

'Fencing should be established at the minimum distance set out in British Standard 5837:2012 '*Trees in relation to design, demolition and construction - Recommendations*'. Excavations should not encroach into the fence position and it is appropriate to keep at least 0.5m between the fence and any changes in level.

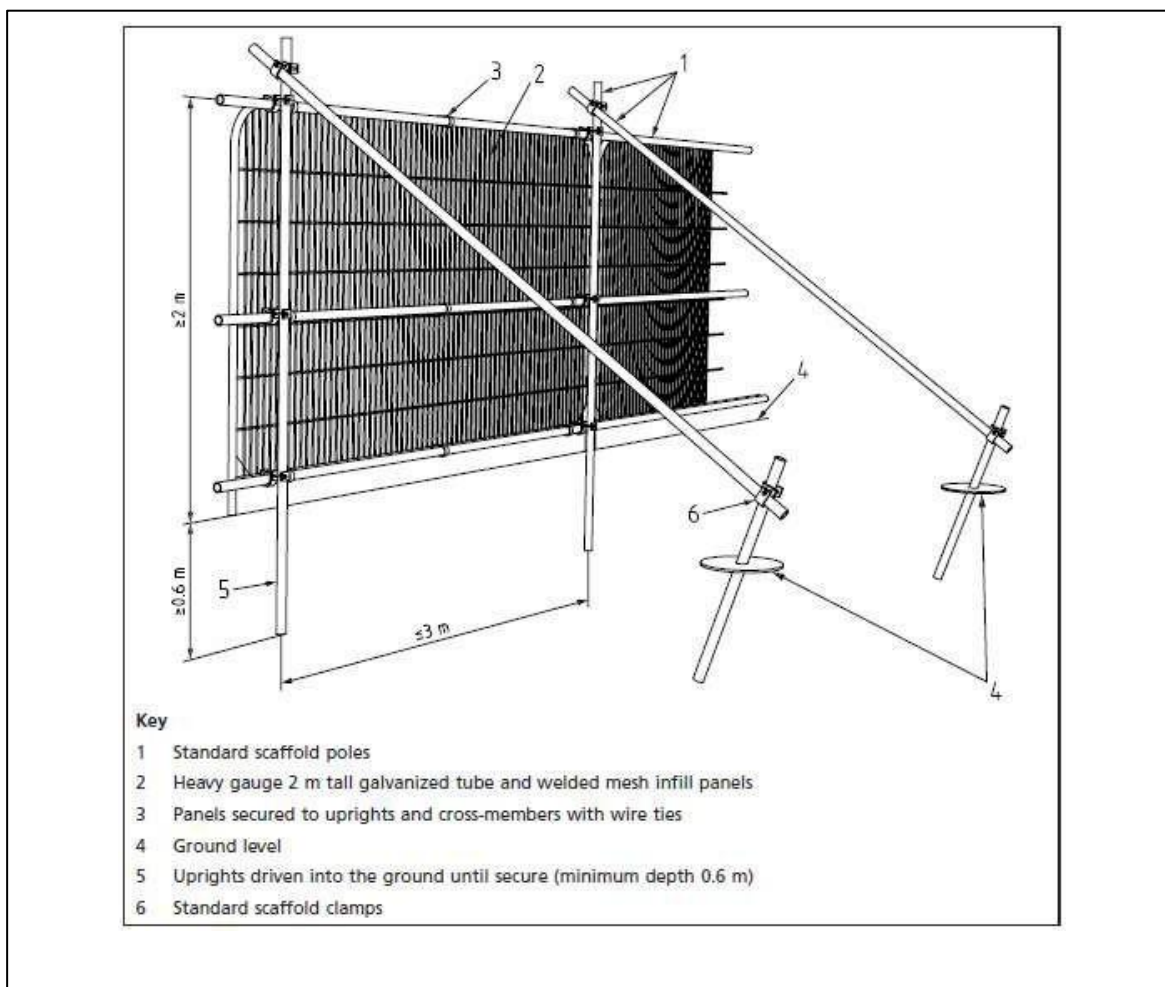

Protective Fencing:
Protective fencing should be erected before any construction commences on site. It should also be in position to protect important trees prior to demolition. Protective fencing should stay in position until all construction activity has finished.
'Fencing should be established at the minimum distance set out in British Standard 5837:2012 'Trees in relation to design, demolition and construction - Recommendations'.
Excavations should not encroach into the fence position and it is appropriate to keep at least 0.5m between the fence and any changes in level.

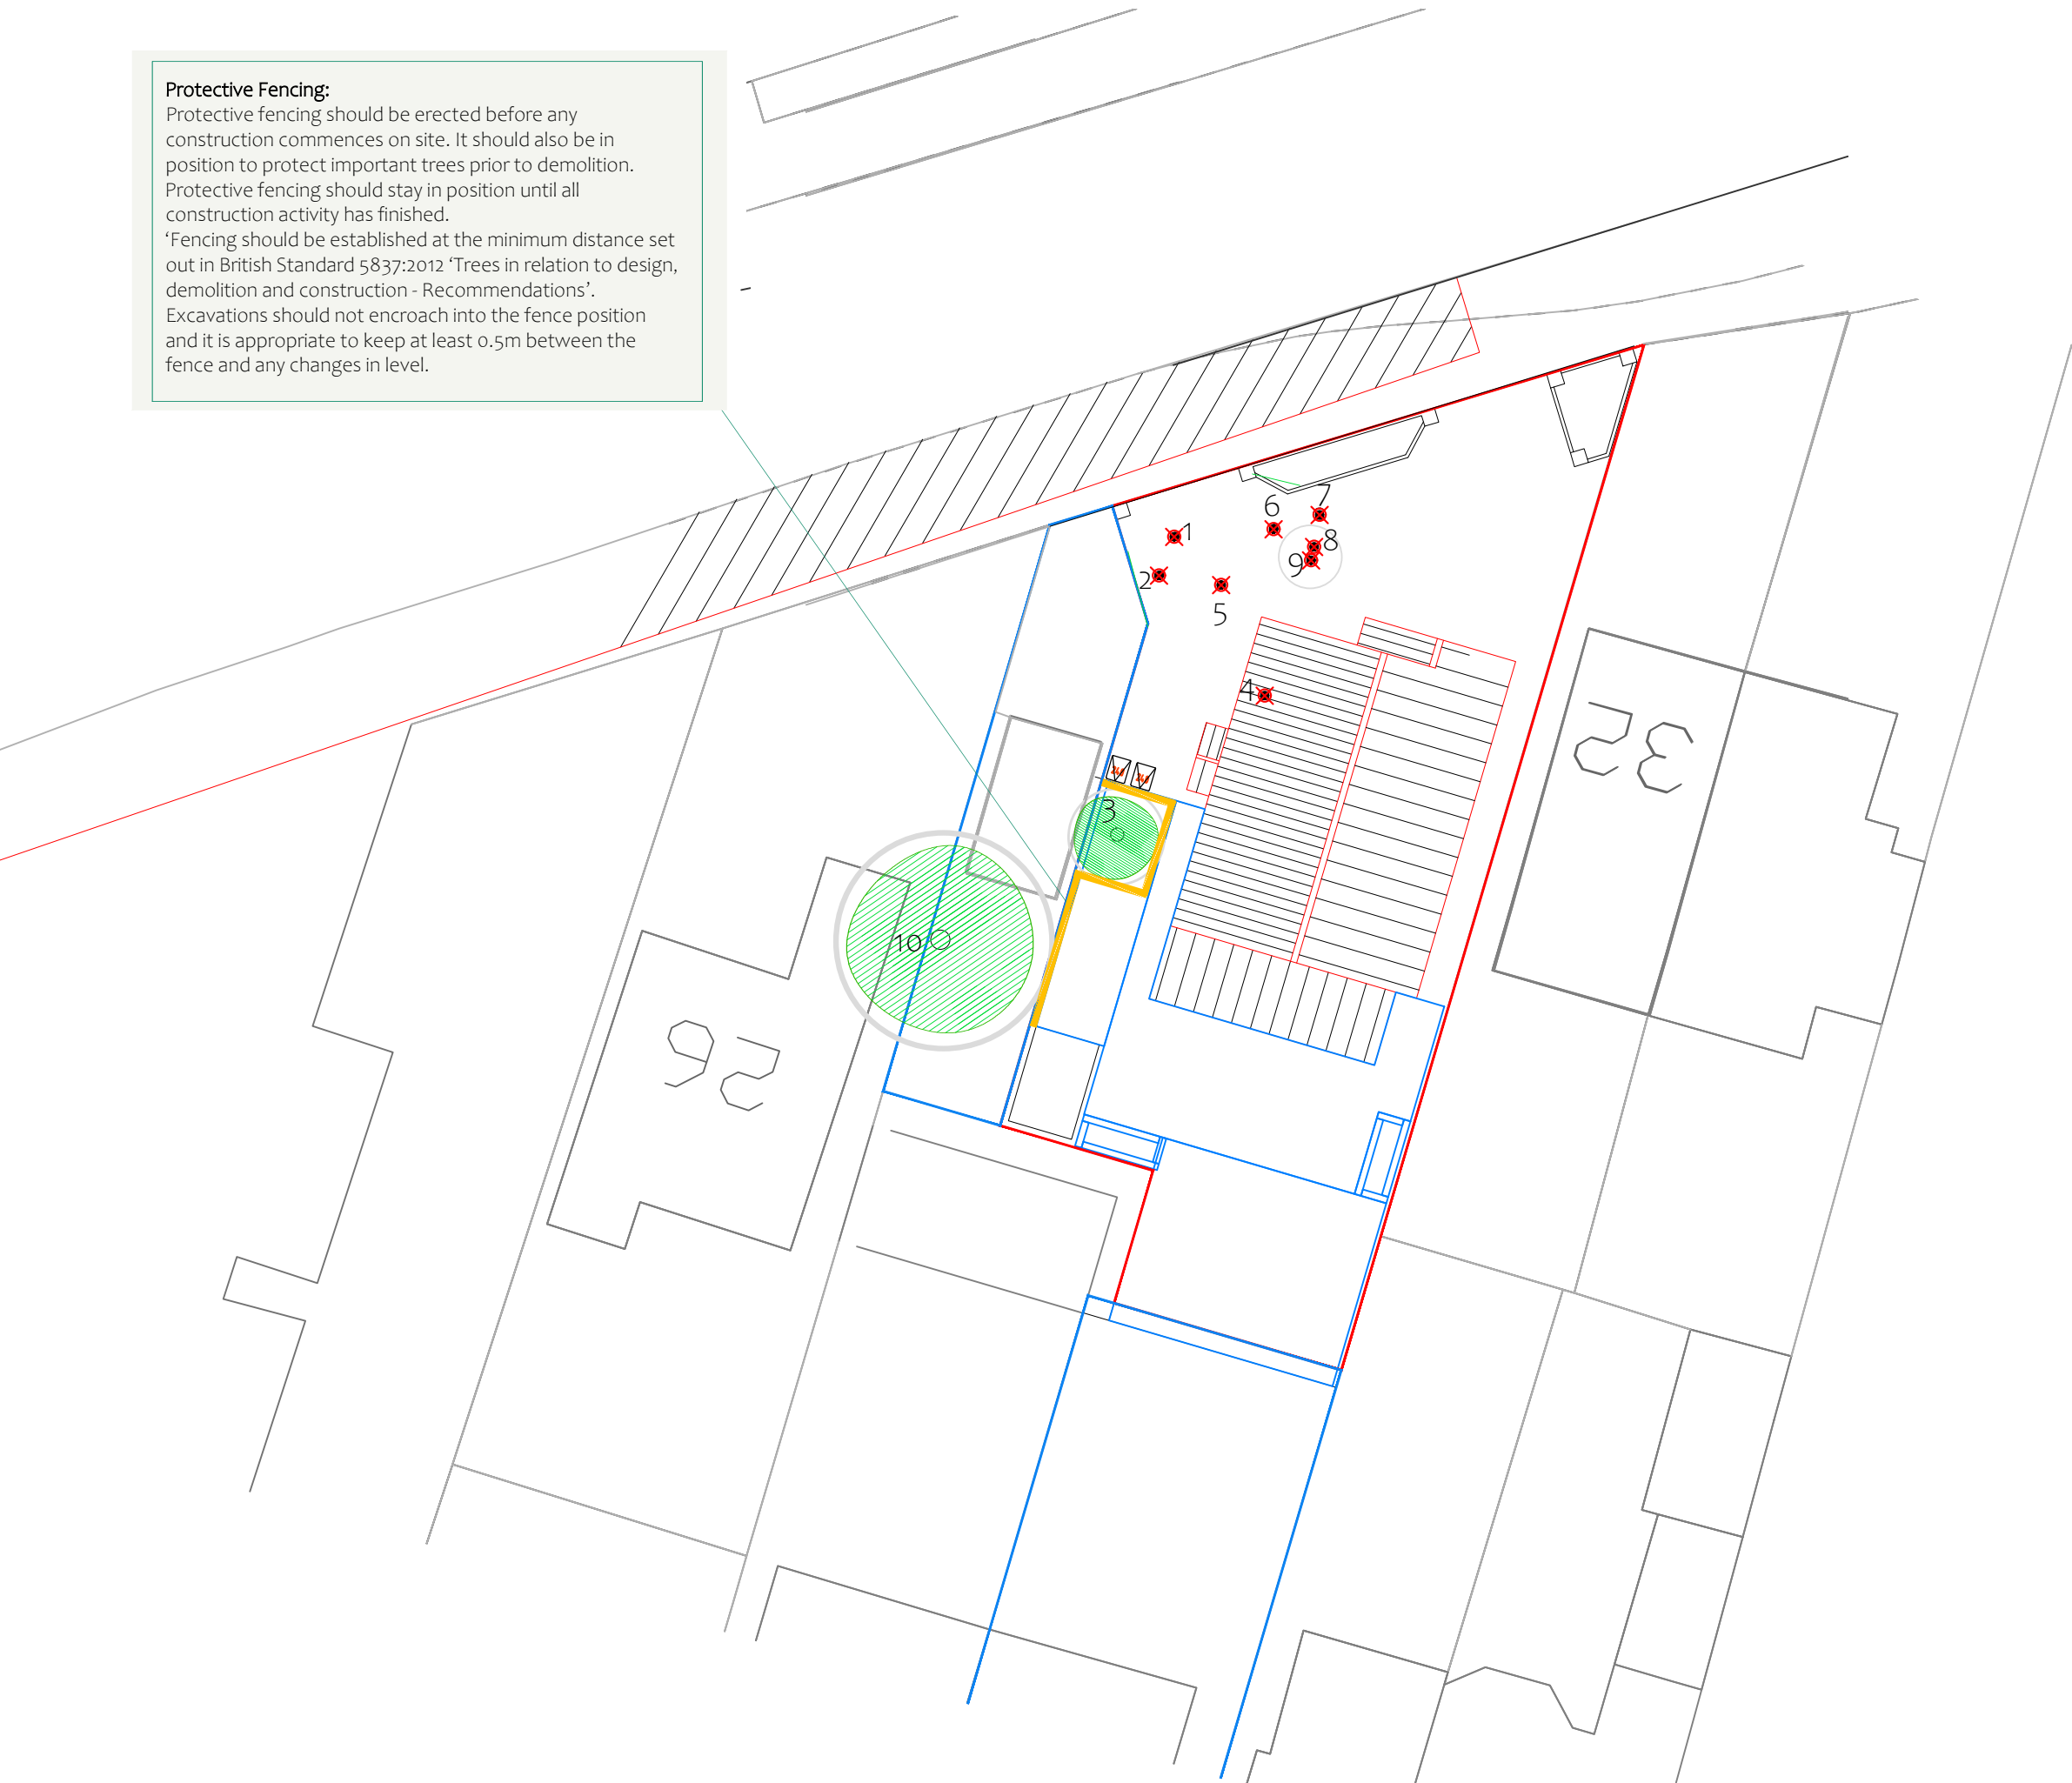

- RPA for Cat A* tree
- RPA for Cat B* tree
- RPA for Cat C* tree
- RPA for Cat U* tree
- Tree Canopy
- Tree Removal
- Heras Fencing
- Ground Protection

All Arboriculture
23 Southernhay Avenue
Bristol
BS8 4TJ



Client: Mr S Kendrick

Consultant: Kristian Chesterman

Site: Land adjacent 12 Shepherds Hill, Earley, RG6 1BB

Title: Tree Protection Plan

Scale at A3:	Date:	Document Ref.
1:200	24/01/2025	AATPP12SH
