




Heras fencing to be put in place at 5m from the rear boundary. This is to provide a buffer zone so that constructions activities do not harm habitats and wildlife. It allows movement of wildlife animals and provides buffer for their natural movement and would not be affected by construction. Fencing will be 1.8m tall and will be fit in weighted concrete bases to provide stability.

Positioned away from entrance to avoid blocking it. Not too far back of the site to ensure deliveries are efficient and construction vehicles do not spend too much time with in the site

Designated site parking for site workers, contractors, authorised visitors, which eliminates need to park on residential roads

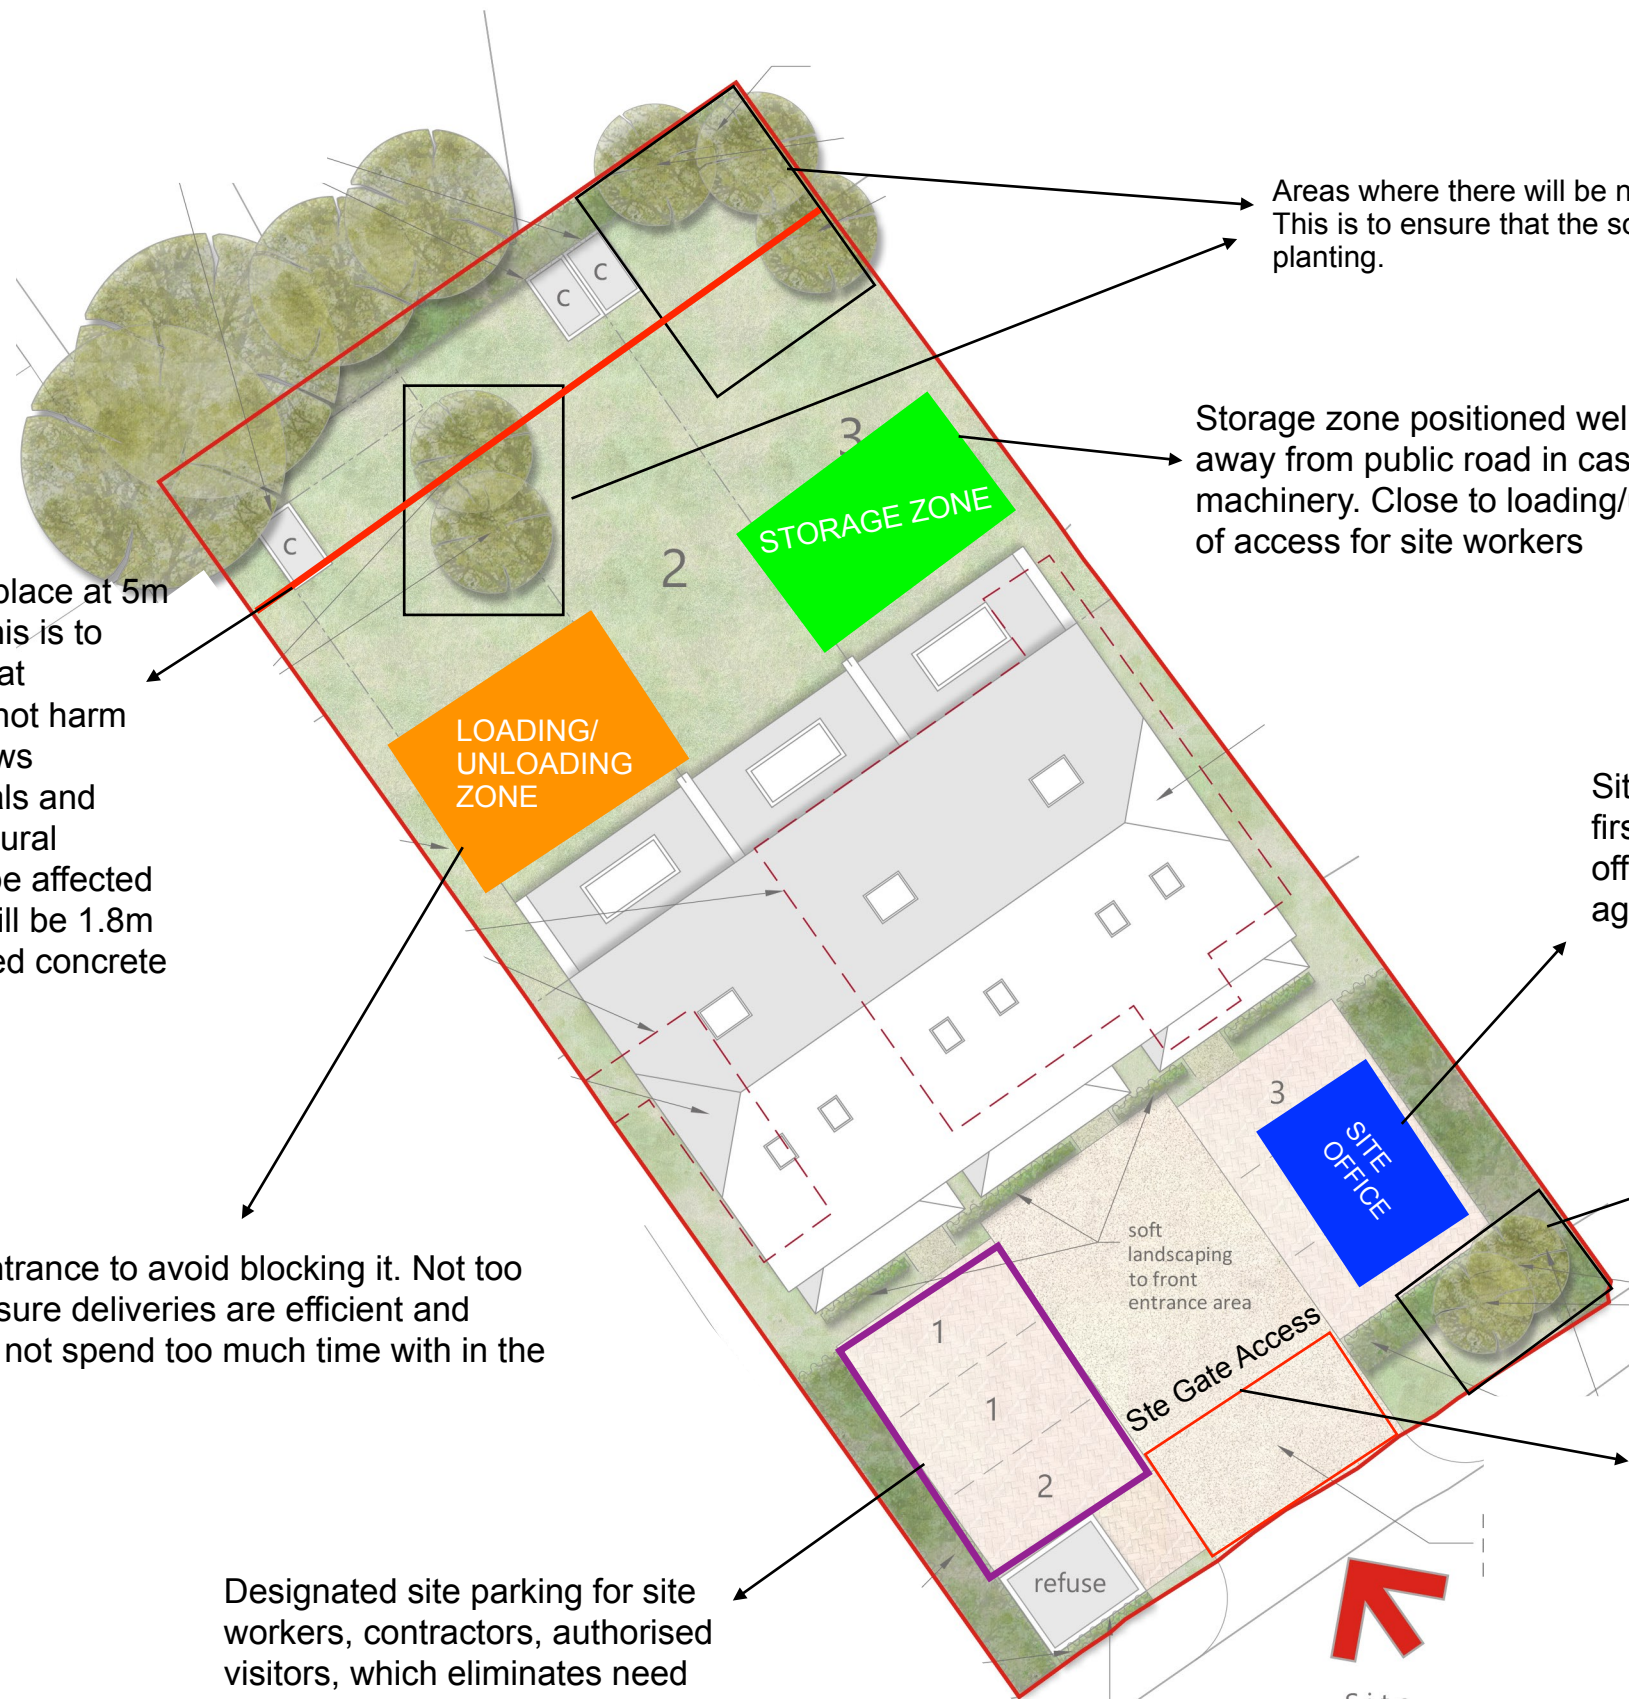

Areas where there will be no loading, parking or material storage. This is to ensure that the soil is protected and safe for future tree planting.

Storage zone positioned well back within the site so it is far away from public road in case of dangerous tools and machinery. Close to loading/unloading zone to ensure ease of access for site workers

Site office near site entrance - To include welfare facilities, first aid kit, toilet and utilities. Once site office is collected off site, the ground will be replenished and made good again for the planting of native hedges

Areas where there will be no loading, parking or material storage. This is to ensure that the soil is protected and safe for future tree planting.

Site gate - this is the only point entry and exit and will be set back from the site boundary to ensure that delivery vehicles and construction traffic is not waiting on the public highway. Gate to open inwards into the site so as not to affect public and pedestrians. Fencing to have warning signs at regular intervals

SITE SAFETY			
	Construction work in progress. Parents are advised to warn children of the dangers of entering this site		Danger Demolition work in progress
	No admittance for unauthorised personnel		Use ear protectors
	This is a hard hat area		High visibility jackets must be worn
	Protective footwear must be worn		Warning Look out for overhead loads
