



DUCKWORTHS
ARBORICULTURE LTD.

BS:5837 ARBORICULTURAL REPORT

ARBORICULTURAL SURVEY & ARBORICULTURAL IMPACT ASSESSMENT &
METHOD STATEMENT

SILVER BIRCHES (POOL & POOLHOUSE)
HEATH RIDE
FINCHAMPSTEAD
BERKSHIRE
RG40 3QJ

CLIENT: J. RAHI

OCTOBER 2025
Ref: 06806 / 2025

REPORT BY: SARAH DUCKWORTH

DipArb(RFS),TechCert(ArborA),M. Arbor.A, BA (Hons)
LANTRA Professional Tree Inspector

E: sarahcduckworth@hotmail.com
M: 07810 440546

Project: Proposed construction of a new swimming pool & pool house

Prepared by: Sarah Duckworth

Position: Arboricultural Consultant

Qualifications: DipArb(RFS),TechCert(ArborA),M. Arbor.A, BA (Hons),
LANTRA Professional Tree Inspector

File ref: AIA/AMS 06806/2025

Date Issued: 20th October 2025

Report History					
Version	Date	Author	Checked	Comments	Status
1	20/10/2025	SCD	HDT		ISSUE

EXECUTIVE SUMMARY

This report provides detailed and site-specific information on the steps which will be undertaken to ensure trees are not harmed during the proposed construction of a new pool and pool house on land at Silver Birches, Heath Ride, Finchampstead, Berkshire, RG40 3QJ.

Trees growing on and adjacent to the property have been surveyed in accordance with the guidelines and recommendations from BS:5837 'Trees in Relation to Design, Demolition and Construction'.

The location of the proposed new pool and pool house has been designed to sit outside of the identified Root Protection Areas of all trees. No trees are to be removed or cut back to facilitate the proposed construction works.

Trees on site will be protected with Tree Protection Fencing installed in accordance with BS:5837 2012 – Trees in Relation to Design, Demolition and Construction. Temporary trackway will be used to create vehicle access where necessary across the root protection areas of trees. Trenching for services can be routed around the root protection areas of key trees and will have minimal impact on trees

I am therefore satisfied that provided the methodology specified within the Arboricultural Method Statement is followed in full during the building works, the proposed new pool and pool house can be constructed without unacceptable harm to the trees and therefore this application acceptable as it relates to trees.

CONTENTS

1.	INTRODUCTION	6
1.1	INSTRUCTION	6
1.2	SCOPE.....	6
1.3	DOCUMENTS.....	6
1.4	CAVEATS	7
2.	ARBORICULTURAL IMPACT ASSESSMENT.....	8
2.1	INTRODUCTION	8
2.2	SOIL.....	8
2.3	PLANNING CONSTRAINTS	9
2.4	TREES APPRAISAL.....	10
2.5	APPLICATION ASSESSMENT.....	10
2.6	SERVICES	11
2.7	CONCLUSIONS.....	11
3.	ARBORICULTURAL METHOD STATEMENT (AMS)	12
3.1	INTRODUCTION	12
3.2	SITE SUPERVISION AND MONITORING	12
3.3	ON-SITE TREE SUPERVISOR.....	13
3.4	TREE PROTECTION FENCING.....	13
3.5	TEMPORARY TRACKWAY.....	14
3.6	CONSTRUCTION EXCLUSION ZONE.....	14
3.7	SERVICES	15
3.8	GENERAL CONSIDERATIONS.....	15
3.9	LANDSCAPING	15
3.10	UNFORESEEN CIRCUMSTANCES.....	16
	APPENDICES.....	17
	APPENDIX A - SURVEY DATA.....	18
	APPENDIX B - KEY	19
	APPENDIX C - BS:5837 (2012) TABLE 1: CASCADE CHART FOR TREE QUALITY ASSESSMENT.....	20
	APPENDIX D - TREE DATA	21
	APPENDIX E – TREE PLANS.....	37
	APPENDIX F – PHASING OF WORKS.....	38
	APPENDIX G – CONTACTS	39
	APPENDIX H - TREE PROTECTION FENCING	40
	APPENDIX I - TREE PROTECTION SIGNAGE.....	41
	APPENDIX J - QUALIFICATIONS	42

1. INTRODUCTION

1.1 INSTRUCTION

This Arboricultural report has been prepared by Sarah Duckworth, Arboricultural Consultant and provides an Arboricultural Survey, Impact Assessment and Method Statement relating to trees growing on and adjacent to land at Silver Birches, Heath Ride, Finchampstead, Berkshire, RG40 3QJ.

I have been instructed to survey relevant trees in accordance with BS:5837 (2012) to ascertain the constraints posed by the trees to the proposed construction of a new pool and pool house within the rear garden of the property.

The Arboricultural Impact Assessment in this report uses the tree data to identify any short or longer-term impact the proposed building works might have on the surrounding trees and makes recommendations for amendments or mitigation where appropriate.

This report also includes a site-specific Arboricultural Method Statement and Tree Protection Plan which details the steps which will be taken to ensure trees are successfully protected and retained during the proposed construction works.

1.2 SCOPE

The British Standard 5837:2012 'Trees in Relation to Design, Demolition and Construction' is designed to assist those concerned with trees and planning to form balanced judgments. This report does not therefore seek to put arguments for or against development but provides a means of protecting the trees which may be affected during development.

The report is for the sole use of the client and its reproduction or use by anyone else is forbidden unless written consent is given by the author.

1.3 DOCUMENTS

The position of trees within the tree plan has been taken from a topographical survey provided by the client. Trees not covered by the survey have been plotted by eye by the Tree Surveyor, their positions measured against boundaries and triangulated against fixed objects on site. The position of these trees should not therefore be taken as exact, but the plan is a fair representation of their locations in relation to the proposed build area.

The Tree Protection Plan which accompanies this report is illustrative and should be used for dealing with tree issues only. The precise location of all tree protection measurements should be confirmed with a pre-commencement site meeting before any demolition or construction activity takes place.

1.4 CAVEATS

The report is valid for a period of two years from the date of issue being 20th October 2025 and will expire on 20th October 2027.

The report is not a Tree Risk Management Report or a Hazard Analysis Report and its use as such is invalid.

The report refers to the condition of tree(s) and an assessment of the site on the day the evaluation was undertaken. The trees were assessed from ground level only and not climbed. My assessment of third-party trees was limited where direct access was not available to the adjoining properties.

DISCLAIMER: This is an independently produced Arboricultural Report. I have no connection with any of the parties involved in this site or application that could influence or bias the opinions expressed in this report.

2. ARBORICULTURAL IMPACT ASSESSMENT

2.1 INTRODUCTION

The purpose of the Arboricultural Impact Assessment (AIA) is to evaluate the direct and indirect effects of the proposed building works and where necessary recommend solutions or mitigation as appropriate.

The assessment will take account of the effects of any tree works which may be required to implement the design and identify any potentially damaging activities proposed in the vicinity of the trees.

2.2 SOIL

The soil on site was assessed by an appraisal on the British Geological Drift Survey Map only. According to the 1:50,000 scale map records, the bedrock geology for Silver Birches is Windlesham Formation consisting of sand, silt and clay.

The surveyors visual observations indicate the ground is very sandy. However, if clay is present the nutrient levels may be higher and the water holding capacity greater. Clay can also give the soil capacity to shrink and swell with changing moisture levels which can lead to property subsidence damage.

Foundation depths should be calculated in accordance with NHBC Chapter 4.2 following a detailed on-site soil analysis, taking into account the presence of any clay and future growth of the adjacent trees.

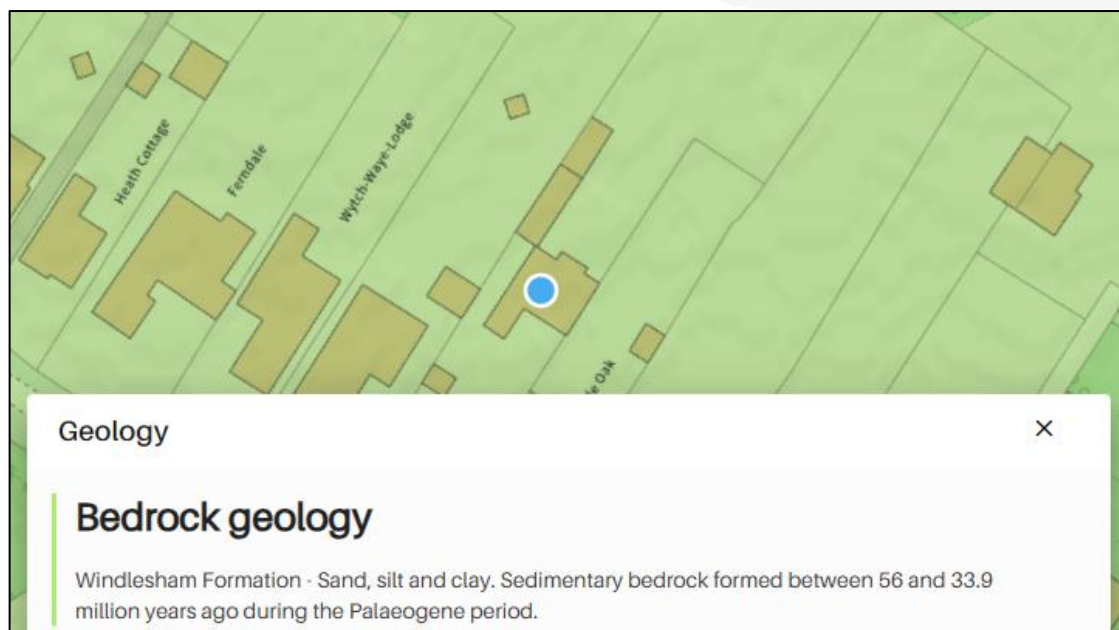


Figure 1 - Detail from the British Geological Survey

2.3 PLANNING CONSTRAINTS

TREE PRESERVATION ORDERS

I have confirmed on the Wokingham Borough Council website that there are Tree Preservation Orders on trees within and directly adjacent to the curtilage of Silver Birches, Heath Ride.

No work should be undertaken to trees subject of a Tree Preservation Order without the prior written consent of the Local Planning Authority – exemptions apply.

The protected status of trees is subject to change. You are advised to reconfirm the protected status of trees prior to carrying out any works to trees on site.

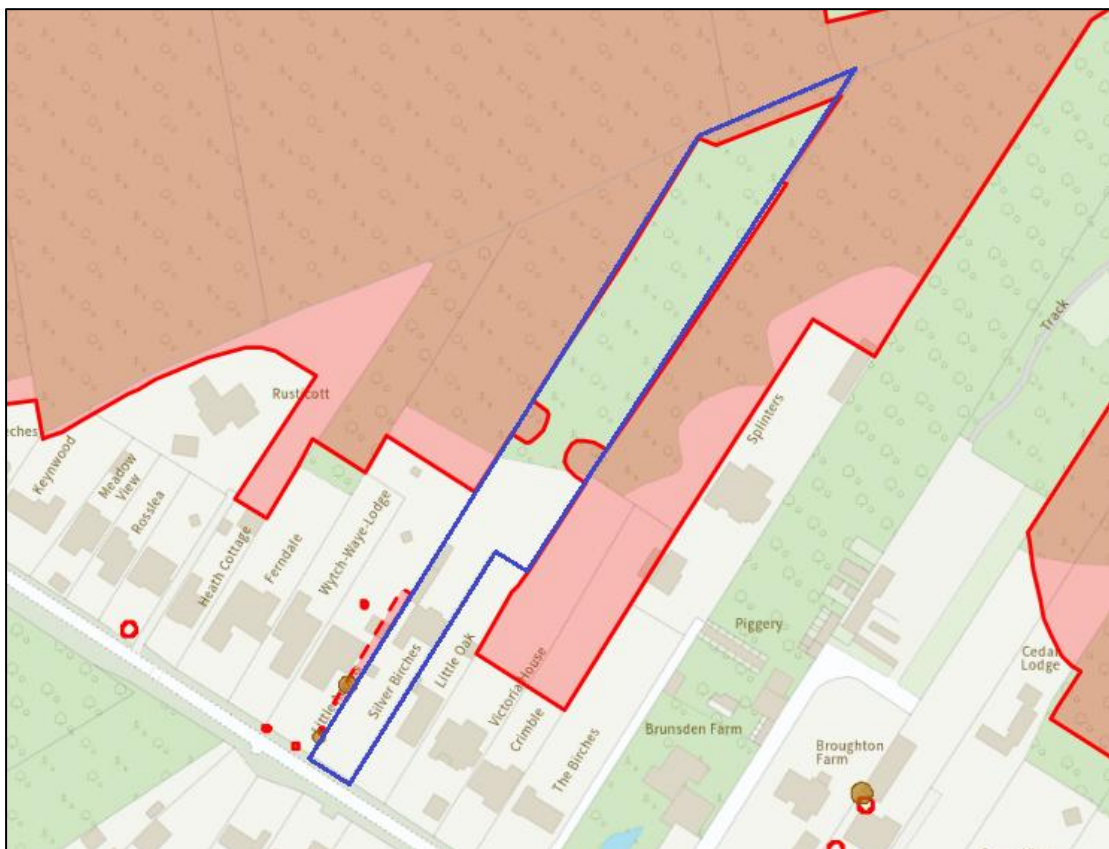


Figure 2 – Wokingham Borough Council Tree Preservation Order Information

CONSERVATION AREA

Silver Birches is not within a Conservation Area.

ANCIENT WOODLAND

Silver Birches does not include Ancient Woodland, nor is the site within an Ancient Woodland Buffer Zone.

2.4 TREES APPRAISAL

Number of individual trees surveyed:	139
Number of tree groups surveyed:	4
Number of category 'A' trees / groups:	1
Number of category 'B' trees / groups:	88
Number of category 'C' trees / groups:	50
Number of category 'U' trees / groups:	4

Figure 1 - Tree quality summary

2.5 APPLICATION ASSESSMENT

The suitability of planning development in relation to trees is assessed by the Local Authority in accordance with the British Standard 5837: 2012 'Trees in Relation to Design, Demolition and Construction.

This document requires that the conception and design of the final development layout must take into account the constraints posed by the trees on site. These constraints include not only the existing canopy and likely root spread but also:

- The ultimate height and spread of the trees.
- Potential impact of species characteristics for future residents – evergreen / deciduous, density of foliage, seasonal leaf drop / berries etc.
- Current and future shade patterns.

The default position in planning is that every effort should be made to retain and protect the category A and B trees on site and that new structures should be located outside of the identified RPA's of trees.

The proposed new pool and poolhouse are located outside of the root protection areas of all trees, therefore the building and its construction will not have any foreseeable harm to the trees on site.

Furthermore, no trees are to be removed or cut back to facilitate the proposed building works.

Trees will be protected during construction with fit for purpose Tree Protection Barriers in accordance with BS:5837 (2012).

A suitable load-bearing temporary trackway will be required to facilitate access to the build area across the root protection areas of a number of pines.

The fencing must remain rigid and complete during development. The area behind the tree protection fencing is designated the Construction Exclusion Zone and should be isolated from all activity during work on the site.

In terms of sustainability, there will be a good gap between the canopies of the adjacent trees and the pool house on completion of the build with no further foreseeable need for pruning works in the future.

2.6 SERVICES

I have not received any drainage or service plans for the site. However, services can connect to those of the existing property around the root protection areas of retained trees and this route has been shown on the Tree Protection plan.

As a matter of course, the Local Authority may request confirmation on services and routes, including the locations of any new soakaways to be submitted for approval in support of any future application to ensure it does not conflict with the trees on site.

2.7 CONCLUSIONS

This Arboricultural Impact Assessment has reviewed the proposed redevelopment of Silver Birches in relation to the existing tree stock and arboricultural constraints.

A total of 139 individual trees and 4 groups were surveyed, with the majority falling into category B, indicating moderate quality and value. One category A tree was identified.

The new pool and pool house have been designed to sit outside of the root protection areas of all trees. All trees are to be retained and will be protected throughout the proposed construction works with fit for purposed Tree Protection Fencing and a temporary loadbearing trackway will provide access to the build area.

In this way, the trees growing on and adjacent to Silver Birches can be fully protected and retained in accordance with the guidelines and recommendations in BS:5837 2012 - Trees in Relation to Design, Demolition and Construction.

Provided the steps detailed in the Arboricultural Method Statement are followed in full, the application is therefore considered to be acceptable as it relates to trees.

3. ARBORICULTURAL METHOD STATEMENT (AMS)

3.1 INTRODUCTION

The correct and timely installation of tree protection measures such as tree protection fencing is critical to ensure the long-term retention of a healthy tree stock on or adjacent to the development.

This method statement will be read, approved and agreed to by all key personnel prior to the commencement of works within the site.

WARNING: FAILURE TO FOLLOW THE ARBORICULTURAL METHOD STATEMENT ONCE APPROVED CAN CAUSE IRREPARABLE HARM TO TREES IN CONTRAVENTION OF A TREE PRESERVATION ORDER AND MAY INVALIDATE YOUR PLANNING CONSENT.

3.2 SITE SUPERVISION AND MONITORING

A site visit will be held once the Tree Protection Fencing and temporary ground trackway is installed as shown on the Tree Protection Plan. The Local Authority Tree Officer will be given a minimum of five days' notice of the time and date of the meeting so that they may attend should they wish to do so.

The purpose of the pre-commencement meeting will be for the appointed Arboricultural Consultant to confirm the location and construction of the Tree Protection Measures and ensure a common understanding of the requirements for Tree Protection within the site.

If the Local Planning Authority is unable to attend, photographic evidence of the tree protection fencing will be emailed to the appointed planning officer once it has been erected.

A copy of the Arboricultural Method Statement and Tree Protection Plan will be available on site for reference.

The Arboricultural Method Statement and Tree Protection Plan once approved, will be provided to all contractors working on site, so that the practical aspects of the above precautions are included in their method statements, and financial provision made for these.

3.3 ON-SITE TREE SUPERVISOR

In addition to the appointed Arboriculturist, there will be a designated on-site 'tree supervisor', a member of the build team who is responsible for ensuring no works are undertaken on site except in complete accordance with the approved Arboricultural Method Statement when the Arboricultural Consultant is not present.

The on-site tree supervisor will:

- Be present on site most of the time.
- Be aware of the arboricultural responsibilities relating to the trees on site.
- Have the authority to stop any work that will, or have the potential to, cause harm to any tree.
- Be responsible for ensuring that all site personnel are aware of their responsibilities towards trees on site and the consequences of the failure to observe those responsibilities.
- Make immediate contact with the Council and/or the retained arboriculturalist in the event of any related tree problems occurring whether actual or potential.
- Ensure commitment from all parties to the healthy retention of the trees. These details will be passed on to any contractors working on site, so that the practical aspects of the above precautions are included in their method statements, and financial provision made for these.

3.4 TREE PROTECTION FENCING

No works in relation to the build will be undertaken, including construction, excavation or demolition, prior to the Tree Protection Fencing being installed as identified in the Tree Protection Plan.

The Tree Protection Fencing will consist of a vertical and horizontal scaffold framework braced well to resist impact. The vertical tubes will be spaced at a maximum distance of 3m and driven securely into the ground. Onto this framework welded mesh – 'Heras' style fencing panels or similar will be securely fixed. (See Appendix H).

All-weather signage stating 'TREE PROTECTION AREA – KEEP OUT' will be attached to the outer perimeter of the Tree Protection Fencing. A sample sign is attached in Appendix I of this report.

The fencing will be located to protect trees and their rooting areas and will remain vertical, rigid and complete during development. At no time will Tree Protection Fencing be removed or relocated contrary to the recommendations in this report, without professional arboricultural advice and without the prior consent of the Local Authority Tree Officer.

The appointed On-Site Tree Supervisor will also notify the Local Authority Tree Officer 5 days prior to the tree protection measures being removed on completion of development.

3.5 TEMPORARY TRACKWAY

No work in relation to the permitted building work will be undertaken, including receipt of deliveries, ground excavation or construction, prior to the Temporary Trackway access road and area of Ground Protection being installed as per the Tree Protection Plan.

The trackway / temporary ground protection will be fit for purpose capable of distributing the predicted loads evenly to prevent soil compaction.

There will be no excavation, grading, or stripping of topsoil within the RPA of any tree prior to the installation of the trackway. Where necessary, the ground can be levelled and ruts filled with topsoil / chipped bark or a pH natural sand. A geotextile membrane can then be installed over the existing ground level to protect the soil structure.

The temporary loadbearing panels will be installed by hand or with light machinery operating from the laid trackway or working outside of the root protection areas of trees only. Panels must be laid flush to ensure stability and effective weight distribution and interlocked or pinned into place to prevent movement.

When in use the trackway will be regularly inspected for signs of movement, damage, or compaction around the edges. Individual sections will be adjusted or reinforced as necessary to maintain full protection of the underlying soil.

On completion of the pool house construction the temporary trackway panels will be carefully removed by hand or with machinery operating from hardstanding or outside the RPA. Soil will be inspected and trees examined for signs of stress or damage.

If required, remedial measures will be carried out such as adding more topsoil and reseeding under arboricultural supervision.

3.6 CONSTRUCTION EXCLUSION ZONE

The areas behind the tree protection barriers are designated the Construction Exclusion Zone and will be isolated from all activity during construction work on the site.

Construction Exclusion Zones must remain completely undisturbed for the duration of all development works. No construction activity of any description including (but not limited to) the following will occur within these areas at any time:

- No excavation of any description or alterations to existing levels or ground conditions.
- No storage, disposal of soil, rubble or materials of any other description.
- No vehicular access, parking or use of any tracked or wheeled machinery of any description.
- No erection of temporary structures of any description.
- No storage disposal handling or use of any chemicals including cement washings.
- No fixtures or fittings of any description, security lighting, signage etc shall be attached to any part of a tree.
- No chemicals, fuel, liquids/waste residues of any other description to be stored or disposed of within close proximity to or drained towards/into protection areas.

3.7 SERVICES

The route of services is to be confirmed. An indicative route has been proposed on the Tree Protection Plan in which location; service trenches will have limited impact on the rooting areas of trees on site.

If at any point this route is found not to be viable then a revised plan will be drawn up in consultation with the Arboricultural Consultant and submitted to Wokingham Borough Council for approval.

3.8 GENERAL CONSIDERATIONS

Poolhouse foundations should be constructed in accordance with the guidelines and recommendations in HNBC Chapter 4.2 considering the presence of any potentially shrinkable clay soil and the future growth of existing trees adjacent to the property.

All storage and preparation of materials, parking, skips etc. in relation to the build will be outside of the identified rooting areas of all trees.

Roots can be killed by pollution of the rooting area by chemicals and leaching. Loose, granular or liquid materials, including cement mix and fuel will be stored on an impermeable membrane placed outside of the rooting areas of all trees.

Particular care will be taken in the planning of deliveries if they require wide or tall loads and plants with booms, rigs or counterweights which can cause serious and permanent damage to trees making their safe retention impossible.

Any transit or traverse of plant in proximity to the trees and or tree protection barriers will be conducted under the supervision of a banksman to ensure that adequate clearance from trees is maintained at all times.

Materials will be delivered to site regularly in small quantities in order to keep vehicle delivery sizes small and on-site storage to an absolute minimum.

There will be no open fires on site during the building works.

3.9 LANDSCAPING

The following rules will be followed during all future landscaping works:

- Tree roots can be damaged by severance, compaction, pollution and desiccation. In view of this, there should be no excavation or changes in ground levels within the identified rooting areas of trees following completion of the development.
- On completion of the build, any new fence panels should include holes or gaps at ground level a minimum of 100x100mm to allow small mammals such as hedgehogs to forage within the property.
- Where new fencing is proposed, post holes within the rooting areas of trees will be dug using a post hole digger to keep hole size to a minimum. Where substantial roots over 30mm are encountered, the location of the hole will be moved to avoid them.

- Post holes will be fully lined in order to prevent potentially toxic concrete coming into direct contact with tree roots.

3.10 UNFORESEEN CIRCUMSTANCES

In the event of unforeseen circumstances whereby it is not possible to work in accordance with the Arboricultural Method Statement, then advice should be sought immediately from a qualified Arboriculturist.

THERE SHALL BE NO DEVIATION FROM THIS METHOD STATEMENT WITHOUT CONSULTATION WITH A QUALIFIED ARBORICULTURIST AND / OR THE WRITTEN CONSENT OF THE LOCAL PLANNING AUTHORITY.

APPENDICES

- A. Survey Data
- B. Key
- C. Cascade Chart for Tree Quality Assessment
- D. Tree Data
- E. Tree Plans
- F. Phasing of works
- G. Contacts
- H. Tree Protection Fencing
- I. Tree Protection Signage
- J. Qualifications

APPENDIX A - SURVEY DATA

- The trees were surveyed on 12th August and 1st October 2025 from ground level only.
- On the days of the survey the weather was dry and overcast. Visibility was good.
- Heights were estimated as part of a group. Soil samples were not taken.
- The tree survey identified 139 trees and 4 tree groups growing on or adjacent to the site which were relevant to this planning application.
- The trees on site were assessed for their quality and benefits within the context of the proposed development and categorised in accordance with the recommendations in the BS: 5837:2012 – 'Trees in Relation to Design, Demolition and Construction'.

APPENDIX B - KEY

Ref:	T001 = Tree 1	G001 = Group 1
	A001 = Area 1	W001 = Woodland 1
Species:	Common name (Botanical name)	
Height:	Measured with a clinometer (m) where possible or estimated when part of a group	
Stem:	Stem diameter taken at 1.5m with girth tape or rule and recorded in millimeters	
Branch spread:	Paced measurements at compass points or with a laser measure.	
Crown clearance:	Existing height above ground level of canopy and / or first significant branch direction of growth in metres e.g., 2.4 (N) where relevant.	
Epics:	Lower canopy created by epicormic growth.	
Age Class:	Newly planted - 3 years following planting. Young - Tree well established but with juvenile crown form Young Mature - Tree in first third of usual life expectancy for species Mature - Tree in second third of usual life expectancy for species Over Mature - Tree in final third of usual life expectancy for species / exhibiting signs of crown retrenchment & senescence. Veteran - Older than usual for species or with historical/ cultural / ecological value	
General Observations:	Made with reference to physiological condition (health, vigour) and structural condition, noting evidence of decay, structural weakness and physical defect and preliminary management recommendations.	
Estimated Remaining Contribution:	Estimated in years - less than 10, 10-20, 20-40, 40+	
BS: 5837:2012 category rating:	In accordance with the guidelines of the British Standard.  Category 'A' tree (Green)  Category 'C' tree (Grey)  Category 'B' tree (Blue)  Category 'U' tree – Fell (Red)	
RPA Area	BS:5837 (2012) Root Protection Area calculation in square metres	
RPA Radius	BS:5837 (2012) Root Protection Area calculation circle radius in metres. ¹	

¹ The root protection area radius is for information only and may not be appropriate in every case. BS:5837 advises that *'the RPA for each tree should initially be plotted as a circle centered on the base of the stem. Where pre-existing site conditions or other factors indicate that rooting may have occurred asymmetrically, a polygon of equivalent area should be produced. Modifications to the shape of the RPA should reflect a soundly based arboricultural assessment of likely root distributions.'*

APPENDIX C - BS:5837 (2012) TABLE 1: CASCADE CHART FOR TREE QUALITY ASSESSMENT

CATEGORY & DEFINITION	CRITERIA (including sub-categories where appropriate)		
Trees unsuitable for retention			
Category 'U' Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years.	Trees that have a serious, irremediable, structural defect such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g., where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning. Trees that are dead or showing signs of significant, immediate, and irreversible overall decline. Trees infected with pathogens of significance to the health and / or safety of other trees nearby or very low-quality trees suppressing adjacent trees of better quality. NOTE: Category U trees can have existing or potential conservation value which it might be desirable to preserve		
	Mainly Arboricultural Qualities	Mainly Landscape Qualities	Mainly cultural values including conservation
Trees considered suitable for retention			
Category 'A' Trees of High Quality with an estimated remaining life expectancy of at least 40 years.	Trees that are particularly good examples of their species especially if rare or unusual; or those that are essential components of groups or formal or semi-formal arboricultural features (e.g. the dominant and / or principal trees within an avenue)	Trees, groups, or woodlands of particular visual importance as arboricultural and / or landscape features.	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood pasture)
Category 'B' Trees of Moderate Quality with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g., presence of significant though remedial defects, including unsympathetic past management and storm damage), such that they are unlikely to be suitable for retention for beyond 40 years; or trees lacking the special quality to merit the category 'A' designation.	Trees present in numbers, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals; or trees occurring as collectives but situated so as to make little contribution to the wider locality.	Trees with material conservation or other cultural value.
Category 'C' Trees of Low Quality with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150mm.	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories.	Trees are present in groups or woodlands but without this conferring on them significantly greater collective landscape value; and/ or trees offering low or only temporary / transient landscape benefits.	Trees with no material conservation or other cultural value.

APPENDIX D - TREE DATA

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
G001	Leyland cypress (<i>X Cuprocyparis leylandii</i>)	Group	Height (m): 3 Stem Diam(mm): 100 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 20+ Years	N:0.5 E:0.5 S:0.5 W:0.5	Tight clipped off-site hedge.	C2	Area: 84 sq m.	Physiological Condition: Good Structural Condition: Unknown Public Amenity Value: Low Inspection Limitations: Access
G002	Chinese juniper x11 (<i>Juniperus chinensis</i>)	Group 11 trees	Height (m): 3.5 11 stems, avg.(mm): 100 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 20+ Years	N:0.5 E:0.5 S:0.5 W:0.5	Off-site hedge. Poor form. Browning on west side where previously suppressed by dense vegetation.	C1	Area: 38 sq m.	Physiological Condition: Poor Structural Condition: Fair Public Amenity Value: Low
G003	Mixed species	Group	Height (m): 9 Stem Diam(mm): 100 Crown Clearance (m): 0 Life Stage: Young Rem. Contrib.: 40+ Years	N:2 E:2 S:2 W:2	Younger sapling understory. All trees under 100mm diameter.	C2	Area: 118 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
G004	Birch (<i>Betula pendula</i>), Oak (<i>Quercus robur</i>) Rowan (<i>Sorbus aucuparia</i>)	Group	Height (m): 12 Stem Diam(mm): 100 Crown Clearance (m): 2 Life Stage: Semi Mature Rem. Contrib.: 20+ Years	N:3 E:3 S:3 W:3	Young trees and saplings under 100mm diameter. Dense group.	C2	Area: 181 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T001	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 16 Stem Diam(mm): 400 Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:6 S:6 W:5	Off-site tree. Ivy clad.	B2	Radius: 4.8m. Area: 72 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good Inspection Limitations: Access
T002	Turkey oak (<i>Quercus cerris</i>)	Tree	Height (m): 18 Stem Diam(mm): 400 Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: 40+ Years	N:8 E:10 S:9 W:8	Off-site tree. Broad crown.	B2	Radius: 4.8m. Area: 72 sq m.	Physiological Condition: Good Structural Condition: Unknown Public Amenity Value: High Inspection Limitations: Access
T003	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 15 Stem Diam(mm): 690 Crown Clearance (m): 7 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:3 S:4 W:4	Mature tree. Crown lifted. Needles dense and even.	B2	Radius: 8.3m. Area: 216 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate
T004	Aspen (<i>Populus tremula</i>)	Tree	Height (m): 16 Stem Diam(mm): 390 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 20+ Years	N:5.5 E:5.5 S:3 W:5.5	Slender tree, high crown.	B2	Radius: 4.7m. Area: 69 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T005	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 150 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Small tree, slender high crown.	C2	Radius: 1.8m. Area: 10 sq m.	Physiological Condition: Fair Structural Condition: Unknown Public Amenity Value: Moderate Inspection Limitations: Access
T006	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 320 Crown Clearance (m): 7 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2.5 E:3 S:2 W:4	Off-site tree, canopy in decline.	C2	Radius: 3.8m. Area: 45 sq m.	Physiological Condition: Poor Structural Condition: Unknown Public Amenity Value: Moderate Inspection Limitations: Access
T007	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 170 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Small tree, slender high crown.	C2	Radius: 1.8m. Area: 10 sq m.	Physiological Condition: Fair Structural Condition: Unknown Public Amenity Value: Moderate Inspection Limitations: Access
T008	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 150 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Small tree, slender high crown.	C2	Radius: 1.8m. Area: 10 sq m.	Physiological Condition: Fair Structural Condition: Unknown Public Amenity Value: Moderate Inspection Limitations: Access
T008	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 120 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1 E:5 S:1 W:1	Small tree in dense group. Leaning trunk over Silver Birches garage. Apical Dieback in crown.	C2	Radius: 1.4m. Area: 6 sq m.	Physiological Condition: Fair Structural Condition: Unknown Public Amenity Value: Moderate Inspection Limitations: Access
T009	Common holly (<i>Ilex aquifolium</i>)	Tree	Height (m): 8 Stem Diam(mm): 100 Crown Clearance (m): 2.5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:2 S:1.5 W:1.5	Off-site tree. Slender feathered form.	C1	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T010	Common holly (<i>Ilex aquifolium</i>)	Tree	Height (m): 8 Stem Diam(mm): 90 Crown Clearance (m): 2.5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Off-site tree. Slender feathered form.	C1	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T011	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 14 Stem Diam(mm): 460 Crown Clearance (m): 3 Life Stage: Mature Rem. Contrib.: 20+ Years	N:5 E:5 S:4 W:4.5	Off-site tree. Low crown over existing outbuilding.	B1,2	Radius: 5.5m. Area: 95 sq m.	Physiological Condition: Good Structural Condition: Unknown Public Amenity Value: Good Inspection Limitations: Access
T012	English yew (<i>Taxus baccata</i>)	Tree	Height (m): 6.5 Stem Diam(mm): 280 Crown Clearance (m): 1.5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2 E:2 S:2.5 W:1	Small off-site tree. No wider amenity value	C2	Radius: 3.4m. Area: 36 sq m.	Physiological Condition: Fair Structural Condition: Unknown Public Amenity Value: Low Inspection Limitations: Access

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T013	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 17 Stem Diam(mm): 690 Crown Clearance (m): 2 Rem. Contrib.: 40+ Years	N:3 E:4 S:8 W:7	Off-site tree. Kinked trunk. Asymmetrical crown. Deadwood.	B1	Radius: 8.3m. Area: 216 sq m.	Physiological Condition: Fair Structural Condition: Sunken Public Amenity Value: Moderate Inspection Limitations: Access
T014	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 17 Stem Diam(mm): 520 Crown Clearance (m): 2 Rem. Contrib.: 40+ Years	N:3 E:3 S:8 W:7	Off-site tree. Crown lifted. Suppressed, oval crown.	B1	Radius: 6.2m. Area: 121 sq m.	Physiological Condition: Fair Structural Condition: Sunken Public Amenity Value: Moderate Inspection Limitations: Access
T015	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 17 Stem Diam(mm): 650 Crown Clearance (m): 2 Rem. Contrib.: 40+ Years	N:8 E:6 S:7 W:6	Off-site tree. Suppressed, asymmetrical crown.	B1	Radius: 7.8m. Area: 191 sq m.	Physiological Condition: Fair Structural Condition: Sunken Public Amenity Value: Moderate Inspection Limitations: Access
T016	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 610 Crown Clearance (m): 3.5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:4 W:2	Needle density normal. Form usual for species.	B2	Radius: 7.3m. Area: 167 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T017	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 570 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2 E:7 S:3 W:1	Swept stem, kinked upper trunk. Needle density normal. Form usual for species.	B2	Radius: 6.8m. Area: 145 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T018	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 550 Crown Clearance (m): 9 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	Needle density normal. Form usual for species. Collective amenity value.	B2	Radius: 6.6m. Area: 137 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T019	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 460 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:1 E:4 S:3 W:0	Swept stem, asymmetrical crown. Needle density normal. Form usual for species. Collective amenity value.	B2	Radius: 5.5m. Area: 95 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T020	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 550 Crown Clearance (m): 9 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	Needle density normal. Form usual for species. Collective amenity value.	B2	Radius: 6.6m. Area: 137 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T020	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 380 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2 E:2 S:2 W:2	Needle density normal. Form usual for species. Collective amenity value.	B2	Radius: 4.6m. Area: 66 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T021	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 470 Crown Clearance (m): 13 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:1 S:1 W:3	Needle density normal. Asymmetrical upper crown. Collective amenity value.	B2	Radius: 5.6m. Area: 99 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T022	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 430 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:1 E:1 S:2.5 W:3	Needle density normal. Form usual for species. Collective amenity value.	B2	Radius: 5.2m. Area: 85 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T023	Norway spruce (<i>Picea abies</i>)	Tree	Height (m): 8 Stem Diam(mm): 90 Life Stage: Semi Mature Rem. Contrib.: 20+ Years	N:2 E:2 S:2.5 W:2	Small tree, low feathered crown.	C2	Radius: 1.1m. Area: 4 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Dense vegetation
T024	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 620 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3.5 E:2 S:5 W:2	Swept stem. Asymmetrical lower trunk. Needle density normal. Collective amenity value.	B2	Radius: 7.4m. Area: 172 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T025	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 460 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	Needle density normal. Collective amenity value.	B2	Radius: 5.5m. Area: 95 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T026	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 530 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4.5 E:3.5 S:3 W:2	Needle density normal. Collective amenity value.	B2	Radius: 6.4m. Area: 129 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T027	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 480 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:1 S:3 W:3	Needle density normal. Collective amenity value.	B2	Radius: 5.8m. Area: 106 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T028	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 350 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:1.5 E:1 S:1.5 W:1	Needle density normal. Collective amenity value.	B2	Radius: 4.2m. Area: 55 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T029	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 490 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4 E:2 S:3.5 W:3	Superficial bark wounds on trunk. Needle density normal. Collective amenity value.	B2	Radius: 5.9m. Area: 109 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T030	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 520 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:6 E:6 S:1.5 W:2	Asymmetrical crown. Needle density normal. Collective amenity value.	B2	Radius: 6.2m. Area: 121 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T031	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 600 Crown Clearance (m): 12 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:7 S:3 W:2	Superficial bark wounds on trunk. Needle density normal. Collective amenity value.	B2	Radius: 7.2m. Area: 163 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T032	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 16 Stem Diam(mm): 530 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4 E:1 S:3 W:3.5	Mature tree, asymmetrical crown.	B2	Radius: 6.4m. Area: 129 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate
T033	Pedunculate oak (<i>Quercus robur</i>)	Tree	1 stems Crown Clearance (m): 1.5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:7 E:8.5 S:6.5 W:5	Mature tree, asymmetrical crown. Superficial damage to buttress roots.	B2	No RPA.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T034	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 9 Stem Diam(mm): 100 Crown Clearance (m): 2 Life Stage: Early Mature Rem. Contrib.: 40+ Years	N:1.5 E:1.5 S:1.5 W:3	Slender tree kinked trunk, suppressed crown.	C2	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T035	Norway spruce (<i>Picea abies</i>)	Tree	Height (m): 9 Stem Diam(mm): 100 Crown Clearance (m): 0.5 Life Stage: Semi Mature Rem. Contrib.: 40+ Years	N:2 E:2 S:2 W:2	Young slender tree with longer term potential.	C2	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Low
T036	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 17 Stem Diam(mm): 220 Crown Clearance (m): 9 Life Stage: Mature Rem. Contrib.: 20+ Years	N:4 E:3 S:3 W:2.5	Mature tree. Swept stem. Slender high crown.	B2	Radius: 2.6m. Area: 21 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T037	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 13 Stem Diam(mm): 200 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2 E:2 S:2 W:5	Mature tree. Suppressed, asymmetrical crown.	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T038	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 13 Stem Diam(mm): 320 Crown Clearance (m): 4 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2 E:2 S:2 W:5	Mature tree. Swept stem West. Suppressed, asymmetrical crown.	B2	Radius: 3.8m. Area: 45 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T039	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 13 Stem Diam(mm): 140 Crown Clearance (m): 4 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2 E:2 S:2 W:2	Mature tree. Slender crown.	B2	Radius: 1.7m. Area: 9 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T040	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 13 Stem Diam(mm): 160 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 20+ Years	N:3 E:0 S:1 W:4.5	Mature tree. Stem wounds. Suppressed, asymmetrical crown.	C2	Radius: 1.9m. Area: 11 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T041	Norway spruce (<i>Picea abies</i>)	Tree	Height (m): 18 Stem Diam(mm): 510 Crown Clearance (m): 4.5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4 E:4 S:4 W:4	Good form and vitality.	A2	Radius: 6.1m. Area: 117 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T042	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 16 Stem Diam(mm): 300 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 20+ Years	N:3 E:3 S:3 W:3	Slender tree. Suppressed crown.	B2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T043	Norway spruce (<i>Picea abies</i>)	Tree	Height (m): 8 Stem Diam(mm): 110 Crown Clearance (m): 1 Life Stage: Young Rem. Contrib.: 40+ Years	N:2 E:2 S:2 W:2	Suppressed. Fair form and vitality.	C2	Radius: 1.3m. Area: 5 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T044	Norway spruce (<i>Picea abies</i>)	Tree	Height (m): 14 Stem Diam(mm): 300 Crown Clearance (m): 1 Life Stage: Early Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	Suppressed crown. Fair form and vitality.	B2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T045	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 7 Stem Diam(mm): 100 Crown Clearance (m): 3 Life Stage: Early Mature Rem. Contrib.: 40+ Years	N:2 E:0 S:1 W:5	Swept stem West. Suppressed, asymmetrical crown.	C2	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T046	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 200 Crown Clearance (m): 3 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2.5 E:2.5 S:2.5 W:2.5	Slender tree. Suppressed crown.	C2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T047	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 14 Stem Diam(mm): 230 Crown Clearance (m): 3 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2.5 E:4 S:3 W:2.5	Slender tree. Suppressed crown.	C2	Radius: 2.8m. Area: 25 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T048	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 130 Crown Clearance (m): 3 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2 E:2 S:2 W:2	Slender tree. Suppressed crown.	C2	Radius: 1.6m. Area: 8 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T049	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 12 Stem Diam(mm): 330 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	End tree in linear group	B2	Radius: 4.0m. Area: 50 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T050	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 200 Crown Clearance (m): 3 Life Stage: Dead	N:1 E:1 S:1 W:1	Standing dead tree	U	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Dead Structural Condition: Decaying Public Amenity Value: Low Inspection Limitations: Dense vegetation
T051	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 330 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	End tree in linear group	B2	Radius: 4.0m. Area: 50 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T052	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 330 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	End tree in linear group	B2	Radius: 4.0m. Area: 50 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T053	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 17 Stem Diam(mm): 340 Crown Clearance (m): 3 Life Stage: Mature Rem. Contrib.: 20+ Years	N:5 E:2.5 S:2.5 W:2.5	Slender tree. Swept stem. High crown.	C2	Radius: 4.1m. Area: 53 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T054	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 330 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 4.0m. Area: 50 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T055	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 200 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T056	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 150 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 4.0m. Area: 50 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T057	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 200 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T058	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 300 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T059	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 300 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T060	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 200 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T061	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree 2 stems	Height (m): 14 2 stems, avg.(mm): 80 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2 E:2 S:2 W:2	End tree in linear group	B2	Radius: 1.4m. Area: 6 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T062	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 200 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:1.5 E:1.5 S:1.5 W:1.5	End tree in linear group	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T063	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 300 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:4	End tree in linear group	B2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T064	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 200 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T065	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 450 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 4.8m. Area: 72 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T066	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 12 Stem Diam(mm): 320 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T067	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 200 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	End tree in linear group	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T068	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 350 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:4	End tree in linear group	B2	Radius: 4.2m. Area: 55 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T069	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 200 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	Linear group	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T070	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 100 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2 E:2 S:2 W:2	Linear tree group	B2	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T071	Lawson cypress (<i>Chamaecyparis lawsoniana</i>)	Tree	Height (m): 14 Stem Diam(mm): 150 Crown Clearance (m): 0 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	Linear tree group	B2	Radius: 1.8m. Area: 10 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Dense vegetation
T072	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 630 Crown Clearance (m): 7 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4.5 E:4.5 S:4.5 W:4.5	Mature tree. Good form and vitality.	B2	Radius: 7.6m. Area: 181 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate
T073	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 12 Stem Diam(mm): 350 Crown Clearance (m): 5 Life Stage: Early Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:4	Small tree. Fair form and vitality.	B2	Radius: 4.2m. Area: 55 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate
T074	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 400 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:2 S:2 W:4	Fair form and vitality.	B2	Radius: 4.8m. Area: 72 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T075	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 7 Stem Diam(mm): 300 Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:8.5	Offsite oak. Swept low trunk over garden of silver birches.	B2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T076	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 7 Stem Diam(mm): 100 Crown Clearance (m): 2 Life Stage: Early Mature Rem. Contrib.: 20+ Years	N:3 E:1 S:2 W:4.5	Small tree, suppressed low crown.	C2	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T077	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 19 Stem Diam(mm): 480 Crown Clearance (m): 7 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:5 S:5 W:5	Offsite tree.	B2	Radius: 5.8m. Area: 106 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T078	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 120 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1 E:1 S:1 W:3	Slender small tree entwined with Rowan.	C2	Radius: 1.4m. Area: 6 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T079	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 14 Stem Diam(mm): 150 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1 E:1 S:1 W:4.5	Slender small tree. Superficial bark wound on trunk.	C2	Radius: 1.8m. Area: 10 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T080	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 18 Stem Diam(mm): 200 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:3 E:3 S:4 W:3	High slender crown.	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T081	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 17 Stem Diam(mm): 120 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1 E:1 S:4 W:2	Slender tree. Wounds on lower trunk. High crown.	C2	Radius: 1.4m. Area: 6 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T082	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 19 Stem Diam(mm): 200 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2.5 E:2.5 S:2.5 W:2.5	High slender crown.	B2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T083	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 18 Stem Diam(mm): 220 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1 E:2.5 S:4 W:2	High slender crown.	B2	Radius: 2.6m. Area: 21 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T084	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 19 Stem Diam(mm): 130 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 20+ Years	N:4 E:2 S:2 W:2	High slender crown.	B2	Radius: 1.6m. Area: 8 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T085	Silver birch (<i>Betula pendula</i>)	Tree 3 stems	Height (m): 19 3 stems, avg.(mm): 300 Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: 20+ Years	N:6 E:3 S:6 W:6	Multi-stem from ground level.	B2	Radius: 6.2m. Area: 121 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Good
T086	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 520 Crown Clearance (m): 6 Rem. Contrib.: 40+ Years	N:4 E:4 S:6 W:4	Fair form and vitality	B2	Radius: 6.2m. Area: 121 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate
T087	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 480 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:6 E:4 S:4 W:2	Fair form and vitality	B2	Radius: 5.8m. Area: 106 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate
T088	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 560 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 20+ Years	N:8 E:5 S:4 W:3	Superficial bark wound on trunk. Poor form. Multiple leaders in upper crown with weak fork.	C2	Radius: 6.7m. Area: 141 sq m.	Physiological Condition: Good Structural Condition: Physical Defect Public Amenity Value: Moderate
T089	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 430 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3.5 E:2 S:3.5 W:3.5	Fair form and vitality	B2	Radius: 5.2m. Area: 85 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate
T090	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 360 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2 E:2 S:2 W:2	Known decay fungus at base Fungus: <i>Phaeolus schweinitzii</i>	C1	Radius: 4.3m. Area: 58 sq m.	Physiological Condition: Fair Structural Condition: Physical Defect Public Amenity Value: Moderate
T091	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 400 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 20+ Years	N:5 E:2 S:2 W:4	Asymmetrical crown. Foliage sparse.	C2	Radius: 4.8m. Area: 72 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T092	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 440 Crown Clearance (m): 9 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3.5 E:3.5 S:3.5 W:3.5	Fair form and vitality	B2	Radius: 5.3m. Area: 88 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T093	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 16 Stem Diam(mm): 330 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:0 E:1.5 S:4 W:1	Slender tree, asymmetrical crown.	C2	Radius: 4.0m. Area: 50 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Root collar buried
T094	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 550 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:5 S:6 W:5	Fair form and vitality. Codominant leaders in upper crown.	B2	Radius: 6.6m. Area: 137 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate
T095	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 600 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:5 S:5 W:5	Offsite tree. Kinked trunk. Multiple leaders in upper crown.	C2	Radius: 7.2m. Area: 163 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Root collar buried
T096	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 16 Stem Diam(mm): 500 Crown Clearance (m): 8 Life Stage: Dead	N:5 E:5 S:5 W:5	Standing dead tree with full crown. Retain for habitat value.	U	Radius: 6.0m. Area: 113 sq m.	Physiological Condition: Dead Structural Condition: Decaying Public Amenity Value: Low
T097	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 6 Stem Diam(mm): 70 Crown Clearance (m): 1.5 Life Stage: Young Rem. Contrib.: 40+ Years	N:2 E:2 S:2.5 W:1	Small young oak with long-term potential.	C2	Radius: 0.8m. Area: 2 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T098	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 12 Stem Diam(mm): 200 Crown Clearance (m): 7 Life Stage: Early Mature Rem. Contrib.: 40+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Slender young tree.	C2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Root collar buried
T099	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 11 Stem Diam(mm): 150 Crown Clearance (m): 7 Life Stage: Early Mature Rem. Contrib.: 40+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Slender young tree.	C2	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate Inspection Limitations: Root collar buried
T100	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 15 Stem Diam(mm): 160 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2 E:2 S:2 W:2	Offsite tree. Slender high crown.	C2	Radius: 1.9m. Area: 11 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T101	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 16 Stem Diam(mm): 600 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 40+ Years	N:7 E:5 S:3.5 W:3	Offsite tree. Needles dense.	B2	Radius: 7.2m. Area: 163 sq m.	Physiological Condition: Good Structural Condition: Not Recorded Public Amenity Value: Moderate Inspection Limitations: Access

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T102	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 10 Stem Diam(mm): 100 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 20+ Years	N:0 E:5 S:2 W:1	Offsite tree. Poor form. Elongated branches resting in crown of adjacent trees	C2	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Fair Structural Condition: Poor Public Amenity Value: Low Inspection Limitations: Access
T103	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 15 Stem Diam(mm): 220 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2.5 E:2.5 S:2.5 W:2.5	Offsite tree. Slender high crown.	C2	Radius: 2.6m. Area: 21 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T104	Goat willow (<i>Salix caprea</i>)	Tree	Height (m): 13 Stem Diam(mm): 200 Crown Clearance (m): 3 Life Stage: Mature Rem. Contrib.: <10 years	N:4.5 E:2 S:2 W:2	Swept stem. Low fork. Dieback in crown.	U	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Poor Structural Condition: Fair Public Amenity Value: Low
T105	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 12 Stem Diam(mm): 120 Crown Clearance (m): 2 Life Stage: Early Mature Rem. Contrib.: 20+ Years	N:4.5 E:2 S:2 W:2	Small tree, suppressed low branch from 1m.	C2	Radius: 1.4m. Area: 6 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T106	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 17 Stem Diam(mm): 350 Crown Clearance (m): 7 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4 E:4 S:4 W:4	Codominant leaders in upper crown.	B2	Radius: 4.2m. Area: 55 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate
T107	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 15 Stem Diam(mm): 400 Crown Clearance (m): 4 Life Stage: Mature Rem. Contrib.: 20+ Years	N:4 E:4 S:2 W:2	Offsite tree. Substantial wound on lower trunk.	C2	Radius: 4.8m. Area: 72 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T108	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 8 Stem Diam(mm): 100 Crown Clearance (m): 4 Life Stage: Mature Rem. Contrib.: 10+ Years	N:1 E:1 S:1 W:1	Offsite tree. Slender and sickly crown.	C2	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Poor Structural Condition: Poor Public Amenity Value: Low Inspection Limitations: Access
T109	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 5 Stem Diam(mm): 160 Crown Clearance (m): 1.5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2 E:7.5 S:1 W:1	Offsite tree. Low swept stem over Silver Birches.	C2	Radius: 1.9m. Area: 11 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T110	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 430 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:4 S:1 W:3	Asymmetrical crown.	B2	Radius: 5.2m. Area: 85 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T111	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 560 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5 E:6.5 S:5 W:5	Codominant leaders in upper crown.	B2	Radius: 6.7m. Area: 141 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Good
T112	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 510 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4.5 E:4.5 S:4.5 W:4.5	Kinked trunk at 7m due to past stem failure.	B2	Radius: 6.1m. Area: 117 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Good
T113	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 16 Stem Diam(mm): 350 Crown Clearance (m): 2.5 Life Stage: Early Mature Rem. Contrib.: 40+ Years	N:6 E:7 S:5 W:3	Offsite tree. Historic stem low dead branch stubs over Silver Birches.	C2	Radius: 4.2m. Area: 55 sq m.	Physiological Condition: Good Structural Condition: Physical Defect Public Amenity Value: Low Inspection Limitations: Access
T114	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 480 Crown Clearance (m): 9 Life Stage: Mature Rem. Contrib.: 20+ Years	N:9 E:7 S:3 W:5	Uneven ground at base - ground level changes or root plate movement. Poor form in upper canopy. Asymmetrical crown.	C2	Radius: 5.8m. Area: 106 sq m.	Physiological Condition: Fair Structural Condition: Physical Defect Public Amenity Value: Moderate
T115	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 560 Crown Clearance (m): 6 Life Stage: Mature Rem. Contrib.: 40+ Years	N:5.5 E:5.5 S:5 W:4	Swept stem North. Bark wounds on buttress roots. Codominant leaders in upper crown.	B2	Radius: 6.7m. Area: 141 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Good
T116	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 20 Stem Diam(mm): 600 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:8 E:4 S:2 W:6	Offsite tree. Twin stem from 8m. Poor form.	B2	Radius: 7.2m. Area: 163 sq m.	Physiological Condition: Good Structural Condition: Physical Defect Public Amenity Value: Moderate Inspection Limitations: Access
T117	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 15 Stem Diam(mm): 220 Crown Clearance (m): 3 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2 E:5 S:1 W:1	Offsite tree. Swept low trunk over Silver Birches. High slender crown.	C2	Radius: 2.6m. Area: 21 sq m.	Physiological Condition: Fair Structural Condition: Poor Public Amenity Value: Low Inspection Limitations: Access
T118	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 460 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4 E:4 S:2 W:3	Uneven ground at base - ground level changes or root plate movement.	B2	Radius: 5.5m. Area: 95 sq m.	Physiological Condition: Fair Structural Condition: Not Recorded Public Amenity Value: Moderate
T119	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 19 Stem Diam(mm): 400 Crown Clearance (m): 9 Life Stage: Mature Rem. Contrib.: 40+ Years	N:4.5 E:4.5 S:4.5 W:4.5	Offsite tree. Slender high crown	B2	Radius: 4.8m. Area: 72 sq m.	Physiological Condition: Good Structural Condition: Physical Defect Public Amenity Value: Moderate Inspection Limitations: Access

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T120	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 14 Stem Diam(mm): 100 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 20+ Years	N:2 E:4 S:2 W:2	Offsite tree. Suppressed form.	C2	Radius: 1.2m. Area: 5 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T121	Rowan (<i>Sorbus aucuparia</i>)	Tree	Height (m): 7.5 Stem Diam(mm): 90 Crown Clearance (m): 1.5 Life Stage: Young Rem. Contrib.: 40+ Years	N:3 E:1.5 S:3 W:2	Large sapling. Fair form and vitality.	C2	Radius: 1.1m. Area: 4 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Low
T122	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 300 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 40+ Years	N:1.5 E:1.5 S:1.5 W:1.5	Slender tree.	B2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate
T123	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 18 Stem Diam(mm): 300 Crown Clearance (m): 9 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	Slender tree.	B2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate
T124	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 9 Stem Diam(mm): 130 Crown Clearance (m): 2 Life Stage: Semi Mature Rem. Contrib.: 20+ Years	N:1.5 E:3.5 S:2.5 W:2	Kinked trunk, suppressed form.	C2	Radius: 1.6m. Area: 8 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low
T125	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 230 Crown Clearance (m): 8 Life Stage: Over Mature Rem. Contrib.: 10+ Years	N:1 E:1 S:1 W:1	Slender tree. Needles sparse.	C2	Radius: 2.8m. Area: 25 sq m.	Physiological Condition: Poor Structural Condition: Fair Public Amenity Value: Low
T126	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 350 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:1.5 E:1 S:1 W:1	Slender tree. High crown, needles sparse.	C2	Radius: 4.2m. Area: 55 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T127	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 470 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 40+ Years	N:8 E:3 S:0 W:4	Slender tree. Twin stem from 8m. Asymmetrical crown.	B2	Radius: 5.6m. Area: 99 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T128	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 18 Stem Diam(mm): 320 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:3.5 E:1 S:1 W:2	Slender tree. High, asymmetrical crown.	B2	Radius: 3.8m. Area: 45 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate

Ref.	Species	Structure	Measurements	Spread	General Observations	Retention Category	RPA	Summary
T129	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 360 Crown Clearance (m): 8 Life Stage: Mature Rem. Contrib.: 20+ Years	N:3.5 E:1 S:1.5 W:3	Slender tree. High, asymmetrical crown.	B2	Radius: 4.3m. Area: 58 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Moderate
T130	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 17 Stem Diam(mm): 350 Crown Clearance (m): 5 Life Stage: Mature Rem. Contrib.: 40+ Years	N:6 E:2 S:2 W:5	Slender oak. Reasonable physiological health.	B2	Radius: 4.2m. Area: 55 sq m.	Physiological Condition: Good Structural Condition: Good Public Amenity Value: Moderate Inspection Limitations: Access
T131	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 370 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3 E:3 S:3 W:3	Uneven ground at base - possible ground level changes or root plate movement.	B2	Radius: 4.4m. Area: 61 sq m.	Physiological Condition: Fair Structural Condition: Not Recorded Public Amenity Value: Moderate
T132	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 390 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:3.5 E:2.5 S:2.5 W:2.5	Soil level built up around lower trunk. Bark damage to trunk.	B2	Radius: 4.7m. Area: 69 sq m.	Physiological Condition: Fair Structural Condition: Not Recorded Public Amenity Value: Moderate
T133	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 440 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	Soil level built up around lower trunk. Bark wounds on lower trunk.	B2	Radius: 5.3m. Area: 88 sq m.	Physiological Condition: Fair Structural Condition: Not Recorded Public Amenity Value: Moderate
T134	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 620 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:6.5 E:2.5 S:3 W:3.5	Root damage from ground level changes. Asymmetrical crown.	B2	Radius: 7.4m. Area: 172 sq m.	Physiological Condition: Fair Structural Condition: Physical Defect Public Amenity Value: Moderate
T135	Scots pine (<i>Pinus sylvestris</i>)	Tree	Height (m): 19 Stem Diam(mm): 380 Crown Clearance (m): 10 Life Stage: Mature Rem. Contrib.: 40+ Years	N:2.5 E:2.5 S:2.5 W:2.5	Slender high crown. Codominant leaders in upper canopy.	B2	Radius: 4.6m. Area: 66 sq m.	Physiological Condition: Good Structural Condition: Fair Public Amenity Value: Moderate
T136	Pedunculate oak (<i>Quercus robur</i>)	Tree	Height (m): 14 Stem Diam(mm): 300 Crown Clearance (m): 1 Life Stage: Early Mature Rem. Contrib.: 40+ Years	N:2 E:3 S:6 W:2.5	Small slender tree growing offsite.	C2	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Fair Structural Condition: Fair Public Amenity Value: Low Inspection Limitations: Access
T137	Silver birch (<i>Betula pendula</i>)	Tree	Height (m): 15 Stem Diam(mm): 300 Crown Clearance (m): 3 Life Stage: Mature Rem. Contrib.: <10 years	N:4 E:3 S:2 W:3	Roots lifting, partial root plate failure.	U	Radius: 3.6m. Area: 41 sq m.	Physiological Condition: Fair Structural Condition: Physical Defect Public Amenity Value: Moderate

APPENDIX E – TREE PLANS

Attached as separate pdf documents

- Tree Protection Plan ref: [SILVER BIRCHES \(POOL\) TPP 06806 2025](#)

APPENDIX F – PHASING OF WORKS

STAGE 1 (PRE-COMMENCEMENT)

INSTALLATION TREE PROTECTION FENCING
& TEMPORARY GROUND PROTECTION



SITE MEETING TO SIGN OFF TREE PROTECTION FENCING
(NOTIFY LOCAL AUTHORITY -MIN 5 DAYS)



STAGE 2 (DEMOLITION & CONSTRUCTION)

CONSTRUCTION OF POOL HOUSE



TREE PROTECTION MEASURES TO REMAIN RIGID AND INTACT
THROUGHOUT BUILD WORKS.



STAGE 3 (POST DEVELOPMENT)

REMOVE TREE PROTECTION MEASURES
(NOTIFY LOCAL AUTHORITY -MIN 5 DAYS)



LANDSCAPING WORKS

APPENDIX G – CONTACTS

Arboricultural Consultant

Sarah Duckworth

Glebelands Bungalow
Mildenhall
Marlborough
Wiltshire
SN8 2LR

E: sarahcduckworth@hotmail.com

M: 07810 440546

Architect

The Keen Partnership
The Courtyard
Edinburgh Road
Reading
Berkshire
RG30 2UA


T: 01189 510 855

Local Planning Authority

Wokingham Borough Council

T: 0118 974 6000

APPENDIX H - TREE PROTECTION FENCING

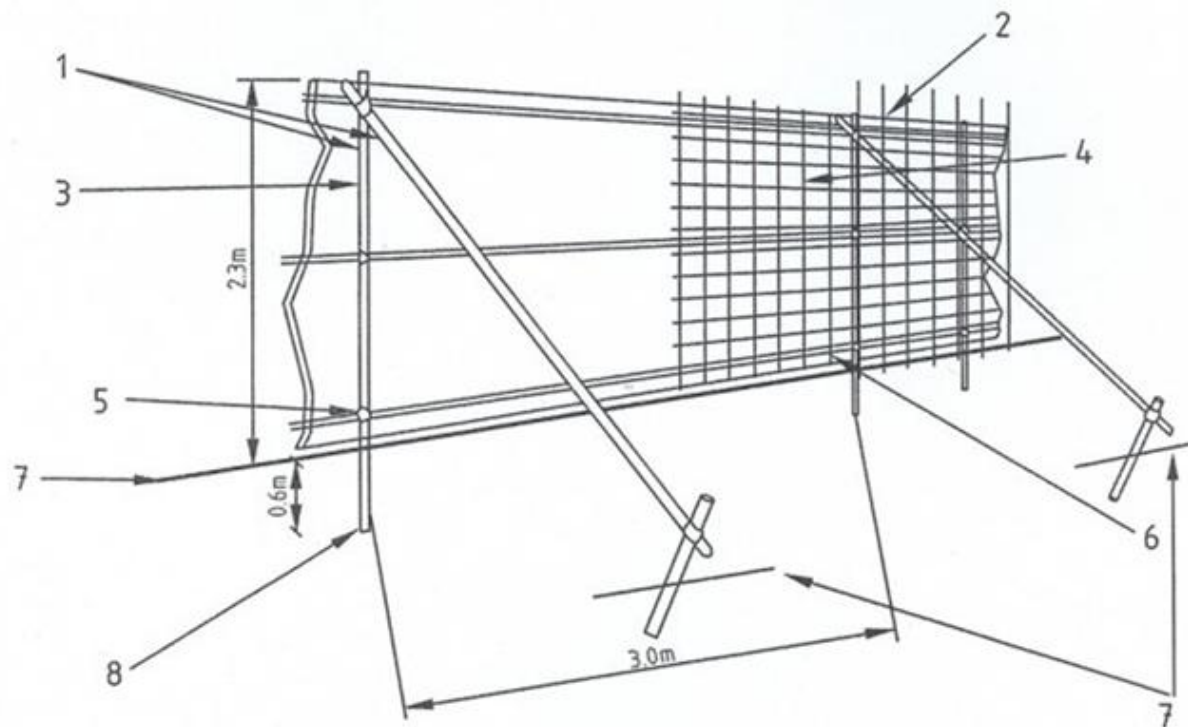

- 1 Standard scaffold poles
- 2 Uprights to be driven into the ground
- 3 Panels secured to uprights with wire ties and, where necessary, standard scaffold clamps
- 4 Weldmesh wired to the uprights and horizontals

- 5 Standard clamps
- 6 Wire twisted and secured on inside face of fencing to avoid easy dismantling
- 7 Ground level
- 8 Approx. 0.6m driven into the ground

APPENDIX I - TREE PROTECTION SIGNAGE



TREE PROTECTION AREA KEEP OUT !

**(TOWN & COUNTRY PLANNING ACT 1990)
TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY
PLANNING CONDITIONS AND/OR ARE THE SUBJECTS OF
A TREE PRESERVATION ORDER.
CONTRAVENTION OF A TREE PRESERVATION ORDER MAY
LEAD TO CRIMINAL PROSECUTION.**

**ANY INCURSION INTO THE PROTECTED AREA MUST BE
WITH THE WRITTEN PERMISSION OF THE LOCAL
PLANNING AUTHORITY.**

APPENDIX J - QUALIFICATIONS

This Arboricultural report has been prepared by Sarah Duckworth, Independent Arboricultural Consultant, trading as Duckworth's Arboriculture Limited.

I have over 20 years' experience working in the field of Arboriculture and for the past 17 years I have worked as a Local Authority Tree Officer both directly and independently providing contracted support. Since 2010 I have worked as a private consultant carrying out a range of Arboricultural Reports and Assessments for private clients.

I hold the Royal Forestry Society's Professional Diploma (Level 6) for which I received the Lockhart Garrett Award. I also hold the Arboricultural Association's Technicians Certificate (with Distinction).

I am a LANTRA qualified Professional Tree Inspector and a Professional Member of the Arboricultural Association.
