



Holt Arboriculture

TREE CONSULTANCY

ARBORICULTURAL IMPACT ASSESSMENT AND METHOD STATEMENT TO ACCOMPANY A PLANNING APPLICATION

Community Hub, School Rd, Hurst, Reading, RG10 0DR



Report by Mr Alexander Needs BA (Hons)
MICFor (Chartered) RCarborA MArborA

8 August 2025

Ref: 250808-1.0-HVCH-AIAAMS 2

Document Control Sheet

Client:	Glyn Crocombe (on behalf of Hurst Parish Council)		
Project name:	Community Hub		
Project address:	School Rd, Hurst, Reading, RG10 0DR		
Report Title:	Arboricultural Impact Assessment and Method Statement		
Report ref.:	250808-1.0-HVCH-AIAAMS 2		
Report date:	08/08/2025		
Surveyed by:	Alex Needs		
Survey date(s):	16/05/2025		
The following documents have been reviewed by Holt Arboriculture:			
Document Title	Document/Drawing number	Originator	
Topographical Survey	Not available	Not available	
Tree Constraints Plan (TCP)	250514-1.0-HVCH-TCP	Holt Arboriculture	
Proposed Layout	Site Plan Rev C	Glyn Crocombe	
Draft Utilities Plan	Not available	Not available	
Revision	Date	Description	By
1.0	08/08/2025	Submission review	AN
 Holt Arboriculture Limited Tel: 01252 280256 E mail: alex@holtarb.co.uk Website: www.holtarb.co.uk Registered in England 15381003 VAT: 478802061			
Copyright Holt Arboriculture Limited. All rights reserved. No part of this report may be copied or reproduced by any means without prior written permission from Holt Arboriculture Limited. If you have received this report in error, please destroy all copies in your possession or control and notify Holt Arboriculture Limited. This report has been prepared for the exclusive use of the commissioning party and unless otherwise agreed in writing by Holt Arboriculture Limited, no other party may use, make use of or rely on the contents of the report. No liability is accepted by Holt Arboriculture Limited for any use of this report, other than for the purposes for which it was originally prepared and provided. Opinions and information provided in the report are based on Holt Arboriculture Limited using due skill, care and diligence in the preparation of the same and no explicit warranty is provided as to their accuracy. It shall be noted, and it is expressly stated that no independent verification of any of the documents or information supplied to Holt Arboriculture Limited has been made.			

Table of Contents

1	Introduction	4
1.1	Brief and Context	4
1.2	Report Purpose	4
1.3	Executive Summary	5
1.4	The Proposal	6
1.5	The Survey	6
2	Existing Tree Population and Constraints	7
2.2	Constraints Table	7
2.3	Canopy coverage and Tree Equity	8
2.4	Statutory tree protection	8
2.5	Veteran and Ancient tree classification	8
2.6	Soil assessment	8
3	Arboricultural Impact of the Proposals	9
3.1	Tree removal and retention	9
3.2	Facilitative tree pruning works	9
3.3	Works within Root Protection Areas (RPAs)	10
3.4	Tree juxtaposition and sustainable relationships	10
3.5	Impact on the landscape and public visual amenity	10
4	Arboricultural Method Statement	11
4.2	General Principles and Administration	11
4.3	Roles and Responsibilities	11
4.4	Pre-Commencement Requirements	11
4.5	Tree Protection Barriers	12
4.6	Site Operations and Activities within or near RPAs	15
4.7	Monitoring and Compliance	16
4.8	Changes and Approvals	17
5	Conclusions	18
	Appendix A – Tree Schedule	
	Appendix B – Tree Protection Plan	
	Appendix C – Tree Constraints Plan	
	Appendix D –Tree Survey Limitations	

1 Introduction

1.1 Brief and Context

- 1.1.1 Alex Needs (the author) is a Chartered Arboriculturist (www.icf.org.uk) and Registered Consultant with the Arboricultural Association (www.trees.org.uk). He holds the Cardiff University Bond Solon Civil and Criminal Expert Witness Certificates and is an Accredited Mediator. He has a degree in Linguistics and holds both the Technician's Certificate in Arboriculture and the Royal Forestry Society Certificate in Arboriculture. He is trained to the LANTRA Professional Tree Inspection standard. He has worked in arboriculture for over 20 years and since 2007 has held principal arboricultural roles in both public and private sectors.
- 1.1.2 Holt Arboriculture was instructed to provide an Arboricultural Impact Assessment and Arboricultural Method Statement, in accordance with British Standard BS5837: 2012 *Trees in Relation to Design, Demolition and Construction – Recommendations*, of the effect of development proposals on trees.

1.2 Report Purpose

- 1.2.1 This arboricultural assessment report provides sufficient information for the Local Planning Authority (LPA) to consider the effect of the proposed development on local character from a tree perspective. It is fully compliant with the BS5837 advice relating to the planning application stage of the process and it meets national standard planning application validation requirements.
- 1.2.2 The Standard recommends a sequence of activities that starts in the initial feasibility and design phase (RIBA Stage 2 'Concept Design') with a survey to qualify and quantify the trees on site and establish the arboricultural constraints to development (above and below ground) to inform the design in an iterative process, and continues with an assessment of the arboricultural impacts of the final design and measures to mitigate such impacts should they be negative. Detailed technical specifications for mitigation and protection measures are devised in the design phase that follows (RIBA Stage 3 and 4 'Spatial Coordination' and 'Technical Design'), and the sequence ends with the 'Handover' and 'Use' phases (RIBA Stages 6 and 7), with the implementation of those measures once planning permission is granted, guided by Arboricultural Method Statements (RIBA Stage 4 and 5, 'Technical Design' and 'Manufacturing and Construction') and professional guidance where appropriate.
- 1.2.3 This report comprises of an Arboricultural Impact Assessment (AIA) which reports on the direct and indirect impacts of the proposed development on trees in terms of both the buildability of the proposals and the long-term impact of the finished scheme, and where necessary presents mitigation for these impacts. And a preliminary Arboricultural Method Statement (AMS) detailing outline methodologies to demonstrate that, in principle, retained trees can be incorporated into the new landscape.

- 1.2.4 BS 5837:2012 recommends classifying trees into four quality and value categories to determine their relative retentive worth. A summary of the relative retentive worth of the trees on site as recorded during the tree survey and expressed by their categories is given in Table 1. Appendix A explains the BS5837 tree categorisation process.

1.3 Executive Summary

- 1.3.1 Table 1 shows data for the number of trees surveyed, their classification (Tree, Group, Woodland, etc.), and their BS5837 categorisation. Full data for each is presented within the Tree Schedule at Appendix A.

Category	Trees	Groups	Total
A	0	0	0
B	2	0	2
C	12	6	18
U	0	0	0
Total	14	6	20

Table 1: Numbers of Trees/Groups in each Retention Category

- 1.3.2 Table 2 shows trees requiring removal to facilitate the scheme. Trees have been identified for removal where they come into direct conflict with structures, where construction cannot be achieved without their removal, or where their future relationship is considered unsustainable, having regard to their eventual potential size. Where high-quality trees have been found to be in conflict with the proposed design, the decision to remove such trees has been informed by an iterative process, following a review of alternative options.

Category A	Category B	Category C	Category U
None	None	T011, T012, T014	None

Table 2: Trees and groups for removal by BS Category

- 1.3.3 Table 3 shows trees that will be subject to construction within their root protection areas. Special measures are recommended to ensure that these trees are not damaged. These measures are detailed in AMS section of this report and are illustrated on the Tree Protection Plan at Appendix B.

Category A	Category B	Category C	Category U
None	None	T003, T004, G006	None

Table 3: Trees and groups for requiring special measures by BS Category

- 1.3.4 Table 4 shows retained trees that will require pruning to facilitate the development and to reduce the likelihood of their being subject to excessive pressure after the completion of the development. These works are detailed in the Tree Schedule at Appendix A.

Category A	Category B	Category C	Category U
None	None	T004, G006	None

Table 4: Trees and groups for pruning by BS Category

1.4 The Proposal

- 1.4.1 The proposed scheme is for the demolition of the existing Scout Hut and a replacement building on the existing footprint to form a new community hub for Hurst Village.

1.5 The Survey

- 1.5.1 The survey was undertaken without the benefit of a geo-referenced topographical survey. Trees were plotted onto the Ordnance Survey Master Map. Tree locations were plotted by eye to the best of our ability, however some caution should be exercised over precise locations. Further information is available at Appendix D.

2 Existing Tree Population and Constraints

- 2.1.1 A survey covering trees on site and trees on adjacent land close enough to be affected by the development was undertaken in accordance with the BS5837:2012 recommendations. Trees were measured using a diameter tape and laser clinometer. Where poor access prevented accurate measure, an estimate was made and a note made on the survey schedule. The full survey results are presented in the Tree Schedule at Appendix A and the above and below ground constraints are illustrated on the Tree Protection Plan at Appendix B. The survey method and limitations are set out in Appendix D.
- 2.1.2 The proposed development site currently houses a single storey Scout Hut building at the edge of an existing car park and access. The hut is within an area of lawn with boundary trees. The most significant tree is the large oak located on the opposite boundary.

2.2 Constraints Table

Constraint	Details	Impact
Local Planning Authority (LPA)	Wokingham Borough Council	
LPA Canopy Cover Calculation requirements	Not known	
Tree Equity Score https://uk.treeequityscore.org/	Outside of urban area – no score.	None
Tree Preservation Orders	None	None
Conservation Areas	None	None
Forestry Act (1967)	Gardens are exempt.	None
Ancient Semi-Natural Woodland (ASNW) https://magic.defra.gov.uk/	None	None
Ancient Tree Inventory https://ati.woodlandtrust.org.uk/	None	None
Obvious veteran trees	None	None
Sites of special scientific interest (SSSI) https://magic.defra.gov.uk/	None	None
Legal covenants and outstanding planning conditions	Not known	None

British Geological Survey Bedrock: https://geologyviewer.bgs.ac.uk/	London Clay Formation - Clay, silt and sand.	If site specific investigations confirm shrinkable clay then foundations should be designed with reference to the National House Building Council's Standards Chapter 4.2 Building near trees or similar guidance.
British Geological Survey Superficial Deposits: https://geologyviewer.bgs.ac.uk/	Kempton Park Gravel Member - Sand and gravel.	If site specific investigations confirm shrinkable clay then foundations should be designed with reference to the National House Building Council's Standards Chapter 4.2 Building near trees or similar guidance.

Table 5: Site specific constraints (checked at time of writing)

2.3 Canopy coverage and Tree Equity

- 2.3.1 A Tree Equity Score is a nationwide, neighbourhood-level score ranging from 0 to 100 that highlights inequitable access to trees. The score is calculated based on tree canopy cover, climate, health and socioeconomic data. The lower the score, the greater priority for tree planting. Details of site-specific score is listed below in Table 5.

2.4 Statutory tree protection

- 2.4.1 Tree Preservation Orders (TPO), Conservation Areas, ancient woodland designations, ancient or veteran trees, and Sites of Special Scientific Interest can all constrain a site. Details of site-specific constraints are listed in Table 5.
- 2.4.2 As TPO status can change, no felling or pruning of trees should be carried out until these statutory constraints have again been confirmed in writing by the appropriate authority immediately prior to the works.

2.5 Veteran and Ancient tree classification

- 2.5.1 The Ancient Tree Inventory is an online list of trees that is created in part by the public. Due to the varying experience and knowledge of public contributors, a listing does not guarantee that a tree meets a recognised criteria for veteran or ancient status.

2.6 Soil assessment

- 2.6.1 BS5837:2012 advises that soil properties should be considered as part of a tree survey report. This is necessary because trees can cause damage to structures founded on soils that shrink and swell with changes in moisture content (principally clays). Such movement is exacerbated by the influence of trees and therefore if a shrinkable soil is suspected foundations should be designed to extend below the likely zone of seasonal moisture change. Details of site-specific soil surveys are listed in Table 5.

3 Arboricultural Impact of the Proposals

3.1 Tree removal and retention

- 3.1.1 Every effort has been made to retain trees wherever possible. Where high-quality trees have been found to be in conflict with the proposed design, the decision to remove such trees has been informed by an iterative process, following a review of alternative options.
- 3.1.2 The trees and groups proposed for removal to facilitate the proposed development are summarised in Table 2. Trees have been identified for removal where they come into direct conflict with structures, where construction cannot be achieved without their removal, or where their future relationship with the development is considered unsustainable, having regard to their eventual potential size.
- 3.1.3 Where higher value trees may be in minor conflict with the proposals, pruning or special construction and protection measures have been specified, as explained in the AMS section of this report.
- 3.1.4 Three small, planted trees (**T011, T012, T014**) are proposed for removal due to their close location to the existing structure making their protection during demolition and construction impractical. The removal of these trees will have only a marginal impact on the local landscape and none on the wider landscape character. Replacement of these trees would be easily achieved within the existing soft landscape should it be required by the LPA under a landscaping condition.

3.2 Facilitative tree pruning works

- 3.2.1 Tree pruning works to trees (**T004, G006**) are required to enable the proposed development. The works are considered minimal and not likely to impact long-term tree health or public amenity value within the landscape. The specifications for facilitative tree works are given in the Tree Schedule at Appendix A.

3.2.1 Root Protection Areas and Construction Exclusion Zones

- 3.2.2 Retained trees will be protected during development by establishing a Construction Exclusion Zone (CEZ) around their Root Protection Areas. RPAs are a layout design tool, indicating the minimum area around a tree deemed to contain sufficient roots and soil to maintain the tree's viability. RPAs should be treated as a precautionary area within which activities such as ground compaction, excavation, the storing of materials, ground level changes and other construction activity are likely to cause damage to trees and should therefore be excluded. This CEZ can be achieved by the erection of barriers or temporary ground protection at the locations shown on the Tree Protection Plan at Appendix B and as detailed in the AMS at section 4 of this report.

3.2.3 Modified RPAs and likely root distribution

- 3.2.4 The British Standard recommends a notional radial root zone is plotted around trees unless there are pre-existing site conditions that indicate that rooting has occurred asymmetrically. In this instance the road and existing building may have constrained root distribution,

however, any modification of the RPA shape would be, at best, an educated guess. For this reason I have chosen to retain a radial RPA and consider that in the absence of any other evidence, this is as reasonable an estimation of root distribution as any other.

3.2.5 Temporary ground protection

3.2.6 Where it is necessary to temporarily breach the CEZ around trees (**T002, T003, T004, T005, G006**) to facilitate the development to allow construction access, storage, and mixing of materials, the roots and soil structure within the RPAs of these trees will be protected by installing ground protection. Further information on ground protection measures can be found in the AMS at section 4 of this report.

3.3 Works within RPAs

3.3.1 Works within the RPAs of trees (**T003, T004, G006**) are required to facilitate the development, however the proposed new structure will be located on the same footprint as the existing and will utilise the existing slab. If on the advice of the consulting engineer it is decided that the slab needs strengthening, this will be added above the slab rather than removal and excavating deeper. This methodology has been chosen to minimise the opportunity for tree root damage.

3.3.2 Demolition and/or removal of structures

3.3.3 The proposal requires the demolition and removal of buildings outbuildings from within the RPAs of trees (**T003, T004, G006**). I have reviewed the likely impact and consider that it can be minimised to an acceptable degree through the use of careful methodologies, details of which can be reviewed in the AMS at section 4 of this report.

3.3.4 Services installation

3.3.5 Information on the location of utility and service runs for the proposed development was not available at time of writing, however it is anticipated they will utilise existing infrastructure. In principle, traditional trench-installed utilities should be routed outside of the RPAs of retained trees to avoid root damage. Where routing utility runs within RPAs is unavoidable, all work should comply with The National Joint Utilities Volume 4 and through the use of specialist methodologies, details of which can be reviewed in the AMS at section 4 of this report.

3.4 Impact on the landscape and public visual amenity

3.4.1 If the recommendations within this report are followed, there will be no significant impact on either tree health or the value they offer to the local and wider landscape.

4 Arboricultural Method Statement

- 4.1.1 The level of site-specific detail within this Arboricultural Method Statement (AMS) is dependent on the information available at the time of writing. At the planning application and design stages this may be minimal, in which case this document will set out a series of parameters for construction activity and outline methodologies to demonstrate that, in principal, trees can be retained within the landscape. However, at the pre-construction, technical, or specialist design stage an AMS will include input from other professions (eg. structural engineers, architects, landscape architects, transport planning consultants) and offer a greater degree of specific detail.
- 4.1.2 This approach is supported by BS5837 which suggests planning applications may be accompanied by a 'heads of terms' AMS, as additional information. A detailed AMS being suggested as appropriate only for reserved matters applications or planning conditions discharge.

4.2 General Principles and Administration

- All work will be conducted under normal site risk assessment procedures and comply with wider site safety rules.
- Unauthorised damage to protected trees is a criminal offence and could lead to enforcement action.
- Operatives entering RPAs will be briefed by the supervising arboriculturist before work starts.
- A precautionary approach towards tree protection will be adopted. Operations within RPAs will be described to demonstrate a minimal risk of adverse impact.

4.3 Roles and Responsibilities

- If required by planning condition, a supervising arboriculturist will be appointed to monitor tree protection.
- The supervising arboriculturist will visit the site to check tree protection and, as necessary, advise on emerging issues.
- The supervising arboriculturist's initial role is to liaise with the developer to ensure protective measures are fit for purpose and in place before any works start. Once the site is working, the role switches to monitoring compliance with arboricultural planning conditions and advising on tree problems or necessary modifications.

4.4 Pre-Commencement Requirements

- If required by planning condition, a pre-commencement meeting will be held on site before site clearance and construction work begins. This meeting would normally include the site manager, the supervising arboriculturist, and an LPA representative (if available).

- All tree protection measures described in the arboricultural method statement will be fully discussed to ensure their implementation and sequencing are understood by all parties.
- Any agreed clarifications or modifications to consented details will be recorded and circulated in writing.
- The programme of tree protection and supervision arrangements will be agreed and finalised at this meeting if not already done so.
- All retained trees must be protected by fencing and ground protection before any demolition, development, or soil stripping starts.
- The supervising arboriculturist must confirm that tree protection has been installed as agreed before any significant site work starts.

4.5 Tree Protection Barriers

4.5.1 Retained trees will be protected during development by establishing a Construction Exclusion Zone (CEZ) around their Root Protection Areas (RPA). RPAs are a layout design tool, indicating the minimum area around a tree deemed to contain sufficient roots and soil to maintain the tree's viability. RPAs should be treated as a precautionary area within which activities such as ground compaction, excavation, the storing of materials, ground level changes and other construction activity are likely to cause damage to trees and should therefore be excluded.

4.5.2 Barrier fencing:

- Fencing will be installed at the locations shown on the tree protection plan.
- It must be fit for purpose, preventing unauthorised incursions and activities within RPAs. Examples are given below.
- Fencing must remain rigid and complete.
- Fencing locations will not be altered or removed without prior approval of the supervising arboriculturist.
- Behind the fencing (within the RPA), unauthorised activities are prohibited, including vehicular/repeated pedestrian access, fires, storage (excavated debris, building materials, chemicals, fuels), cement mixing, service installation/excavation, raising/lowering soil levels, and excessive cultivation.
- The contractor's site huts may, where appropriate, be incorporated into the protective fencing line. If this is to be the case, then their locations must be agreed in advance with the project arboriculturist and a details agreed as to how the huts are to be placed and supported without compacting the soil within the RPA of any retained tree.
- Provision must be taken to prevent exhaust fumes or hot air from generators or kitchen facilities from damaging foliage within crowns of retained trees.
- Warning signs are recommended on fencing. An example is given below.

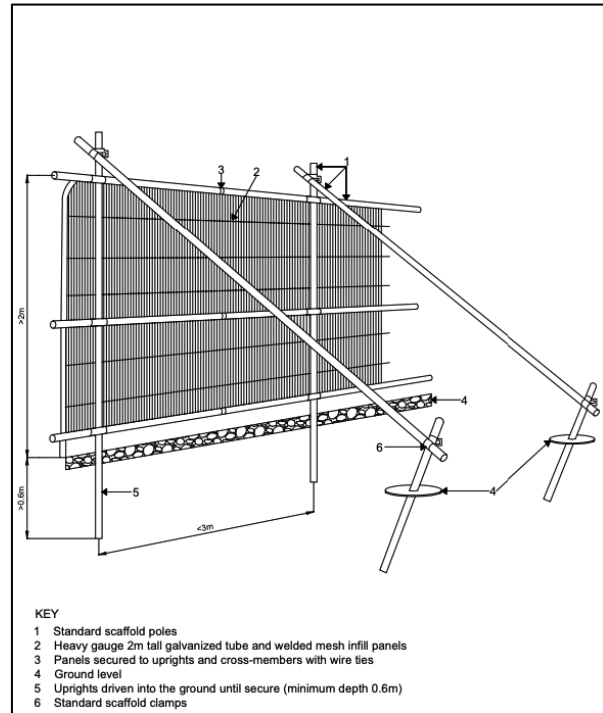


Image 1: BS5837:2012 - Figure 2 – Tree Protective Barrier

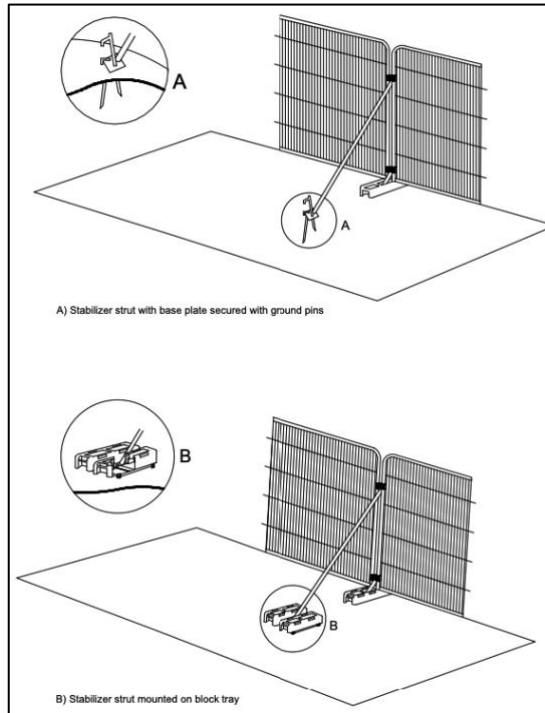


Image 2: BS5837:2012 - Figure 3 – Tree Protective Barrier



Image 3: Showing orange netlon fencing supporting by road pins.



Image 4: Example wording to be included on high visibility all-weather signage attached to protective fencing.

4.5.3 Ground protection barriers:

- Ground protection prevents damage to the underlying soil and roots in RPAs.
- It will be installed at the locations shown on the tree protection plan.
- Where feasible, existing hard standing should be retained to act as ground protection.
- New ground protection must be installed where unmade ground is exposed.
- It will remain in place until there is no risk of harm from development activity.
- Ground protection locations and removal (at the end of construction) will not be altered or removed without prior approval of the supervising arboriculturist.
- It must be fit for purpose, i.e., sufficient to prevent damage to RPAs.
- The design must support all anticipated loading and prevent compaction. The objective is to avoid soil compaction and prevent adverse impacts on root function.
- For pedestrian access ground protection shall comprise of single thickness scaffold boards or a marine grade ply, laid on a compressible layer such as woodchip, laid on a geotextile membrane. The boards should be fixed together to avoid movement.
- For vehicular or tracked machinery access ground protection shall comprise of a steel road plates, steel trackway, pre-cast reinforced concrete slabs, or a temporary access road constructed with a 3D cellular confinement system above the existing ground level, with a no fines angular aggregate infill.
- Where structures are removed from RPAs, fencing and ground protection should be installed up to the edge of the structure to protect the soil.
- All demolition plant should operate outside the RPA or on ground protection installed before demolition starts.



Image 5: Showing an example of a ply boarding above woodchip system of temporary ground protection.

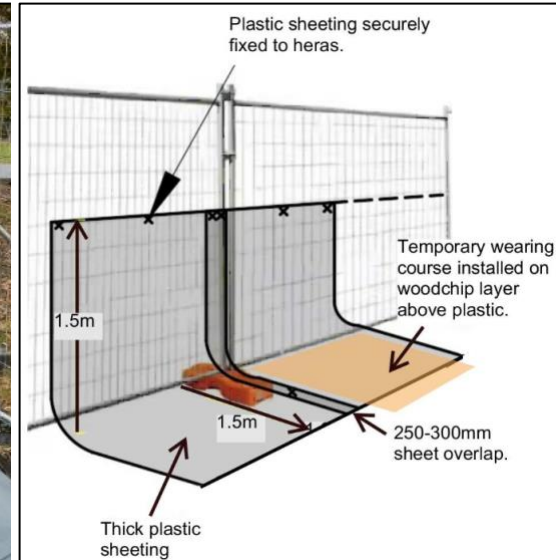


Image 6: Example system preventing liquid pollutants from moving into RPAs.

4.6 Site Operations and Activities within or near RPAs

4.6.1 Pollution Control:

- Measures will be put in place where there is a significant risk of RPA contamination. Materials that could harm trees should be stored and handled well away from RPAs.
- Spilled chemicals or toxic liquids can kill roots and prevent new root growth. Pollution control measures must include containing spillages and clean-up procedures. Provision must be made for emergency spillage clean-up.
- Cement mixing and vehicle washing points must be located outside RPAs.
- Bunding or impermeable membranes should be used to prevent liquid contaminants or leachate (from poured concrete) reaching RPAs. This could comprise impermeable plastic sheeting under wooden boards, to prevent tears, surrounded by a raised lip.
- During wet weather periods where construction on clay soils may produce a liquefied soil run off, or on sites where mixing and washing is close to RPAs, the addition of plastic sheeting to tree protection barrier fencing can prevent this. An example of this is shown above.
- Pollution control measures remain in place until there is no significant risk.

4.6.2 Removing Structures:

- Careful consideration will be given to retaining structures and surfacing if their removal will cause excessive disturbance to retained roots. For example, retaining an existing footing to build a new wall on.
- Manually break up and remove debris using appropriate hand tools.
- Remove debris from the RPA without disturbing the adjacent rooting environment (e.g., lift out with machine outside RPA or carry over ground protection).
- Machines with a long reach can be used if working from outside RPAs or protected areas, not encroaching onto unprotected soil.
- If structures are firmly incorporated into roots, it may be best to leave them in place.
- No vehicular or repeated pedestrian access is permitted unless existing ground protection is retained or new measures are installed.
- All exposed RPAs must be protected until no further risk of damage.
- Demolition of buildings near retained trees should be done inwards within the footprint of the existing building.
- Existing surfacing should be removed with care; machines should work backwards over the area to prevent damage to exposed RPAs. It is preferable to leave existing sub-base if new surfacing is to be laid.

4.6.3 Landscaping in Root Protection Areas:

- Soft landscaping includes re-profiling soil levels and covering with plants or mulch. Hard landscaping is installed according to above.
- No heavy mechanical cultivation such as ploughing or rotavation is permitted.
- Do not fill above original ground levels within RPAs without the precise depth of fill being agreed and authorised by the supervising arboriculturist.
- Never raise soil levels to leave soil touching a trunk that was previously exposed to air. Level changes within 1m of the trunk require input from the supervising arboriculturist.
- Avoid soil compaction. If compaction has occurred, seek arboricultural advice on mitigation methods (eg. forking, spiking, soil augering, radial trenching).

4.7 Monitoring and Compliance

- If required by planning condition, the supervising arboriculturist will monitor works in RPAs.
- Visits will occur at an interval agreed at the pre-commencement meeting (normally every 4-6 weeks for general supervision, but flexible for sensitive works).
- An auditable system of site monitoring for retained trees should be in place.
- Written records of monitoring will be prepared for the client and will not be forwarded directly to the Local Planning Authority.

4.8 Changes and Approvals

- The locations of fencing and ground protection, and precautionary areas, will not be altered without prior approval of the supervising arboriculturist.
- Fencing and ground protection will not be removed at the end of construction without prior approval of the supervising arboriculturist.
- Any variations to the restrictions behind fencing must be agreed by the supervising arboriculturist.

5 Conclusions

- 5.1.1 A BS5837:2012 survey of 20 trees has been carried out on land at School Rd, Hurst, Reading RG10 0DR. This report demonstrates that the proposal has been fully considered in accordance with Arboricultural and Planning best practice.
- 5.1.2 Two trees are considered to be category B and of moderate value, and the remainder are considered to be category C and are of low value.
- 5.1.3 The proposed development requires the removal of three small low-quality Category C trees.
- 5.1.4 The trees to be retained will be protected during development and methods for ensuring their protection have been described.
- 5.1.5 It is considered that the proposed development will pose no threat to trees to be retained and will have no significant impact on the public visual amenity offered by the trees to the local or wider area.

Appendix A

Tree Schedule

Ref.	Species	Measurements	RPA	Condition	General Observations	Work Recs.	Retention Category
T001	English yew (<i>Taxus baccata</i>)	Height (m): 9 2 stems, avg.(mm): 500 Spread (m): 6N, 6E, 6S, 6W Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: 20+ Years	Radius: 8.5m. Area: 227 sq m.	Physiological Condition: Fair Structural Condition: Poor	Slightly sparse crown. Topographic plan unavailable at time of survey.		B
T002	Pedunculate oak (<i>Quercus robur</i>)	Height (m): 13 Stem Diam(mm): 480 Spread (m): 3N, 3E, 8S, 3W Crown Clearance (m): 2.5 Life Stage: Early Mature Rem. Contrib.: 40+ Years	Radius: 5.4m. Area: 92 sq m.	Physiological Condition: Good Structural Condition: Poor	Asymmetrical crown shape. Topographic plan unavailable at time of survey.		C
T003	Pedunculate oak (<i>Quercus robur</i>)	Height (m): 13 2 stems, avg.(mm): 350 Spread (m): 3N, 3E, 8S, 3W Crown Clearance (m): 2.5 Life Stage: Early Mature Rem. Contrib.: 40+ Years	Radius: 5.9m. Area: 109 sq m.	Physiological Condition: Good Structural Condition: Fair	Asymmetrical crown shape. Unable to access trunks. Topographic plan unavailable at time of survey.		C
T004	Pedunculate oak (<i>Quercus robur</i>)	Height (m): 13 Stem Diam(mm): 370 Spread (m): 4.5N, 4.5E, 4.5S, 4.5W Crown Clearance (m): 2.5 Life Stage: Early Mature Rem. Contrib.: 40+ Years	Radius: 4.4m. Area: 61 sq m.	Physiological Condition: Good Structural Condition: Good	Topographic plan unavailable at time of survey. Topographic plan unavailable at time of survey.	Prune back branch ends and crown lift to achieve a 2-3m clearance to allow demolition and construction access.	C
T005	Pedunculate oak (<i>Quercus robur</i>)	Height (m): 13 Stem Diam(mm): 350 Spread (m): 3N, 3E, 8S, 3W Crown Clearance (m): 2.5 Life Stage: Early Mature Rem. Contrib.: 40+ Years	Radius: 4.2m. Area: 55 sq m.	Physiological Condition: Good Structural Condition: Fair	Asymmetrical crown shape. Ivy clad trunk. Dieback. Topographic plan unavailable at time of survey.		C
G006	Mixed species x30 (<i>Mixed species</i>)	Height (m): 8 30 stems, avg.(mm): 150 Spread (m): 3N, 3E, 3S, 3W Crown Clearance (m): 1 Life Stage: Early Mature Rem. Contrib.: 40+ Years	Area: 390 sq m.	Physiological Condition: Fair Structural Condition: Fair	Mixed boundary group of predominantly field maple, sycamore, elm. Topographic plan unavailable at time of survey.	Prune back branch ends and crown lift to achieve a 2-3m clearance to allow demolition and construction access.	C

Ref.	Species	Measurements	RPA	Condition	General Observations	Work Recs.	Retention Category
G007	Mixed species x30 (Mixed species)	Height (m): 17 30 stems, avg.(mm): 350 Spread (m): 4.5N, 4.5E, 4.5S, 4.5W Crown Clearance (m): 0.5 Life Stage: Early Mature Rem. Contrib.: 40+ Years	Area: 266 sq m.	Physiological Condition: Fair Structural Condition: Fair	Mixed boundary group including understory of sycamore, field maple. elm Includes larger trees of oak and ash . Ash trees in advanced stages of decline. Growing either side of boundary ditch. Topographic plan unavailable at time of survey.	Fell ash.	C
G008	Mixed species (Mixed species)	Height (m): 11 Stem Diam(mm): 350 Spread (m): 3.5N, 3.5E, 3.5S, 3.5W Crown Clearance (m): 0.5 Life Stage: Early Mature Rem. Contrib.: 40+ Years	Area: 319 sq m.	Physiological Condition: Fair Structural Condition: Fair	Small group at corner of side consisting of 2 oak, 2 field maple, one two cherry. Topographic plan unavailable at time of survey.		C
T009	Pedunculate oak (Quercus robur)	Height (m): 20 Stem Diam(mm): 1200 Spread (m): 10N, 10E, 10S, 6W Crown Clearance (m): 4 Life Stage: Over Mature Rem. Contrib.: 40+ Years	Radius: 14.4m. Area: 651 sq m.	Physiological Condition: Fair Structural Condition: Fair	Large tree growing between boundary fence and ditch. Some dieback and deadwood in crown . Crown appears slightly sparse but maybe due to late leaf flush. Ivy clad. Lowest live section of branch approximately 5m above ground level over site. Topographic plan unavailable at time of survey.		B
G010	Mixed species x30 (Mixed species)	Height (m): 17 30 stems, avg.(mm): 30 Spread (m): 4N, 4E, 4S, 4W Crown Clearance (m): 0.5 Life Stage: Early Mature Rem. Contrib.: 40+ Years	Area: 610 sq m.	Physiological Condition: Fair Structural Condition: Fair	Boundary group consisting of predominantly field maple, with some hawthorn and sycamore. Three larger multi stem ash trees in latter stages of ash die back. Topographic plan unavailable at time of survey.	Fell ash.	C
T011	Wild cherry (Prunus avium)	Height (m): 6 Stem Diam(mm): 250 Spread (m): 3.5N, 3.5E, 3.5S, 3.5W Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: <10 years	Radius: 3.0m. Area: 28 sq m.	Physiological Condition: Fair Structural Condition: Fair	Dieback in crown. Topographic plan unavailable at time of survey.	Rel to facilitate development.	C
T012	Wild cherry (Prunus avium)	Height (m): 5 Stem Diam(mm): 200 Spread (m): 2.5N, 2.5E, 2.5S, 2.5W	Radius: 2.4m. Area: 18 sq m.	Physiological Condition: Fair Structural Condition: Fair	Topographic plan unavailable at time of survey.	Rel to facilitate development.	C

Ref.	Species	Measurements	RPA	Condition	General Observations	Work Recs.	Retention Category
		Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: <10 years					
T013	Wild cherry (<i>Prunus avium</i>)	Height (m): 6 Stem Diam(mm): 250 Spread (m): 3.5N, 3.5E, 3.5S, 3.5W Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: <10 years	Radius: 3.0m. Area: 28 sq m.	Physiological Condition: Fair Structural Condition: Fair	Ivy clad trunk. Unable to access trunk. Topographic plan unavailable at time of survey.		C
T014	Silver birch (<i>Betula pendula</i>)	Height (m): 14 Stem Diam(mm): 260 Spread (m): 4N, 4E, 4S, 4W Crown Clearance (m): 1.5 Life Stage: Mature Rem. Contrib.: 20+ Years	Radius: 3.1m. Area: 30 sq m.	Physiological Condition: Good Structural Condition: Good	Close to adjacent building. Topographic plan unavailable at time of survey.	Rel to facilitate development.	C
T015	Box elder maple (<i>Acer negundo</i>)	Height (m): 6 Stem Diam(mm): 210 Spread (m): 2N, 2E, 2S, 2W Crown Clearance (m): 2 Life Stage: Early Mature Rem. Contrib.: <10 years	Radius: 2.5m. Area: 20 sq m.	Physiological Condition: Poor Structural Condition: Good	Planted within small strip of soft landscape surrounded by car parking. Ivy clad stem. Sparse crown and dieback. Topographic plan unavailable at time of survey.		C
T016	Apple (<i>Malus sp.</i>)	Height (m): 5 2 stems, avg.(mm): 240 Spread (m): 2N, 2E, 2S, 2W Crown Clearance (m): 2 Life Stage: Over Mature Rem. Contrib.: <10 years	Radius: 4.1m. Area: 53 sq m.	Physiological Condition: Fair Structural Condition: Poor	Managed through pollard reduction. Decay evident in trunk. Topographic plan unavailable at time of survey.	Fell decayed trunk.	C
T017	Apple (<i>Malus sp.</i>)	Height (m): 4 2 stems, avg.(mm): 320 Spread (m): 2N, 2E, 2S, 2W Crown Clearance (m): 2 Life Stage: Mature Rem. Contrib.: <10 years	Radius: 5.4m. Area: 92 sq m.	Physiological Condition: Fair Structural Condition: Fair	Managed through pollard reduction. measured below crown break at 1m. Topographic plan unavailable at time of survey.		C
T018	Apple (<i>Malus sp.</i>)	Height (m): 4 2 stems, avg.(mm): 330 Spread (m): 1.5N, 1.5E, 1.5S, 1.5W Crown Clearance (m): 2	Radius: 5.6m. Area: 99 sq m.	Physiological Condition: Fair Structural Condition: Fair	Managed through pollard reduction. measured below crown break at 1m. Topographic plan unavailable at time of survey.		C



Ref.	Species	Measurements	RPA	Condition	General Observations	Work Recs.	Retention Category
		Life Stage: Mature Rem. Contrib.: <10 years					
T019	False acacia (<i>Robinia pseudoacacia</i>)	Height (m): 14 2 stems (mm): 240,200 Spread (m): 3N, 6E, 8S, 3W Crown Clearance (m): 4 Life Stage: Early Mature Rem. Contrib.: 20+ Years	Radius: 3.7m. Area: 43 sq m.	Physiological Condition: Fair Structural Condition: Fair	Twin-stemmed. Sparse crown. Topographic plan unavailable at time of survey.		C
G020	False acacia x3 (<i>Robinia pseudoacacia</i>)	Height (m): 9 3 stems, avg.(mm): 250 Spread (m): 3.5N, 3.5E, 3.5S, 3.5W Crown Clearance (m): 2 Life Stage: Early Mature Rem. Contrib.: <10 years	Area: 184 sq m.	Physiological Condition: Poor Structural Condition: Poor	Deadwood in crown. Dieback in crown. Sparse crown. Topographic plan unavailable at time of survey.	Fell predominantly dead tree at eastern end of group.	C

Table 1 Cascade chart for tree quality assessment				
Category and definition	Criteria (including subcategories where appropriate)			Identification on plan
Trees unsuitable for retention (see Note)				
Category U Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years	- Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning) - Trees that are dead or are showing signs of significant, immediate, and irreversible overall decline - Trees infected with pathogens of significance to the health and/or safety of other trees nearby, or very low quality trees suppressing adjacent trees of better quality <i>NOTE Category U trees can have existing or potential conservation value which it might be desirable to preserve; see 4.5.7.</i>			See Table 2
	1 Mainly arboricultural qualities	2 Mainly landscape qualities	3 Mainly cultural values, including conservation	
Trees to be considered for retention				
Category A Trees of high quality with an estimated remaining life expectancy of at least 40 years	Trees that are particularly good examples of their species, especially if rare or unusual; or those that are essential components of groups or formal or semi-formal arboricultural features (e.g. the dominant and/or principal trees within an avenue)	Trees, groups or woodlands of particular visual importance as arboricultural and/or landscape features	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood-pasture)	See Table 2
Category B Trees of moderate quality with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of significant though remediable defects, including unsympathetic past management and storm damage), such that they are unlikely to be suitable for retention for beyond 40 years; or trees lacking the special quality necessary to merit the category A designation	Trees present in numbers, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals; or trees occurring as collectives but situated so as to make little visual contribution to the wider locality	Trees with material conservation or other cultural value	See Table 2
Category C Trees of low quality with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150 mm	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories	Trees present in groups or woodlands, but without this conferring on them significantly greater collective landscape value; and/or trees offering low or only temporary/transient landscape benefits	Trees with no material conservation or other cultural value	See Table 2

Extract from British Standard BS5837:2012 Trees in Relation to Design, Demolition and Construction – Recommendations

Appendix B

Tree Protection Plan

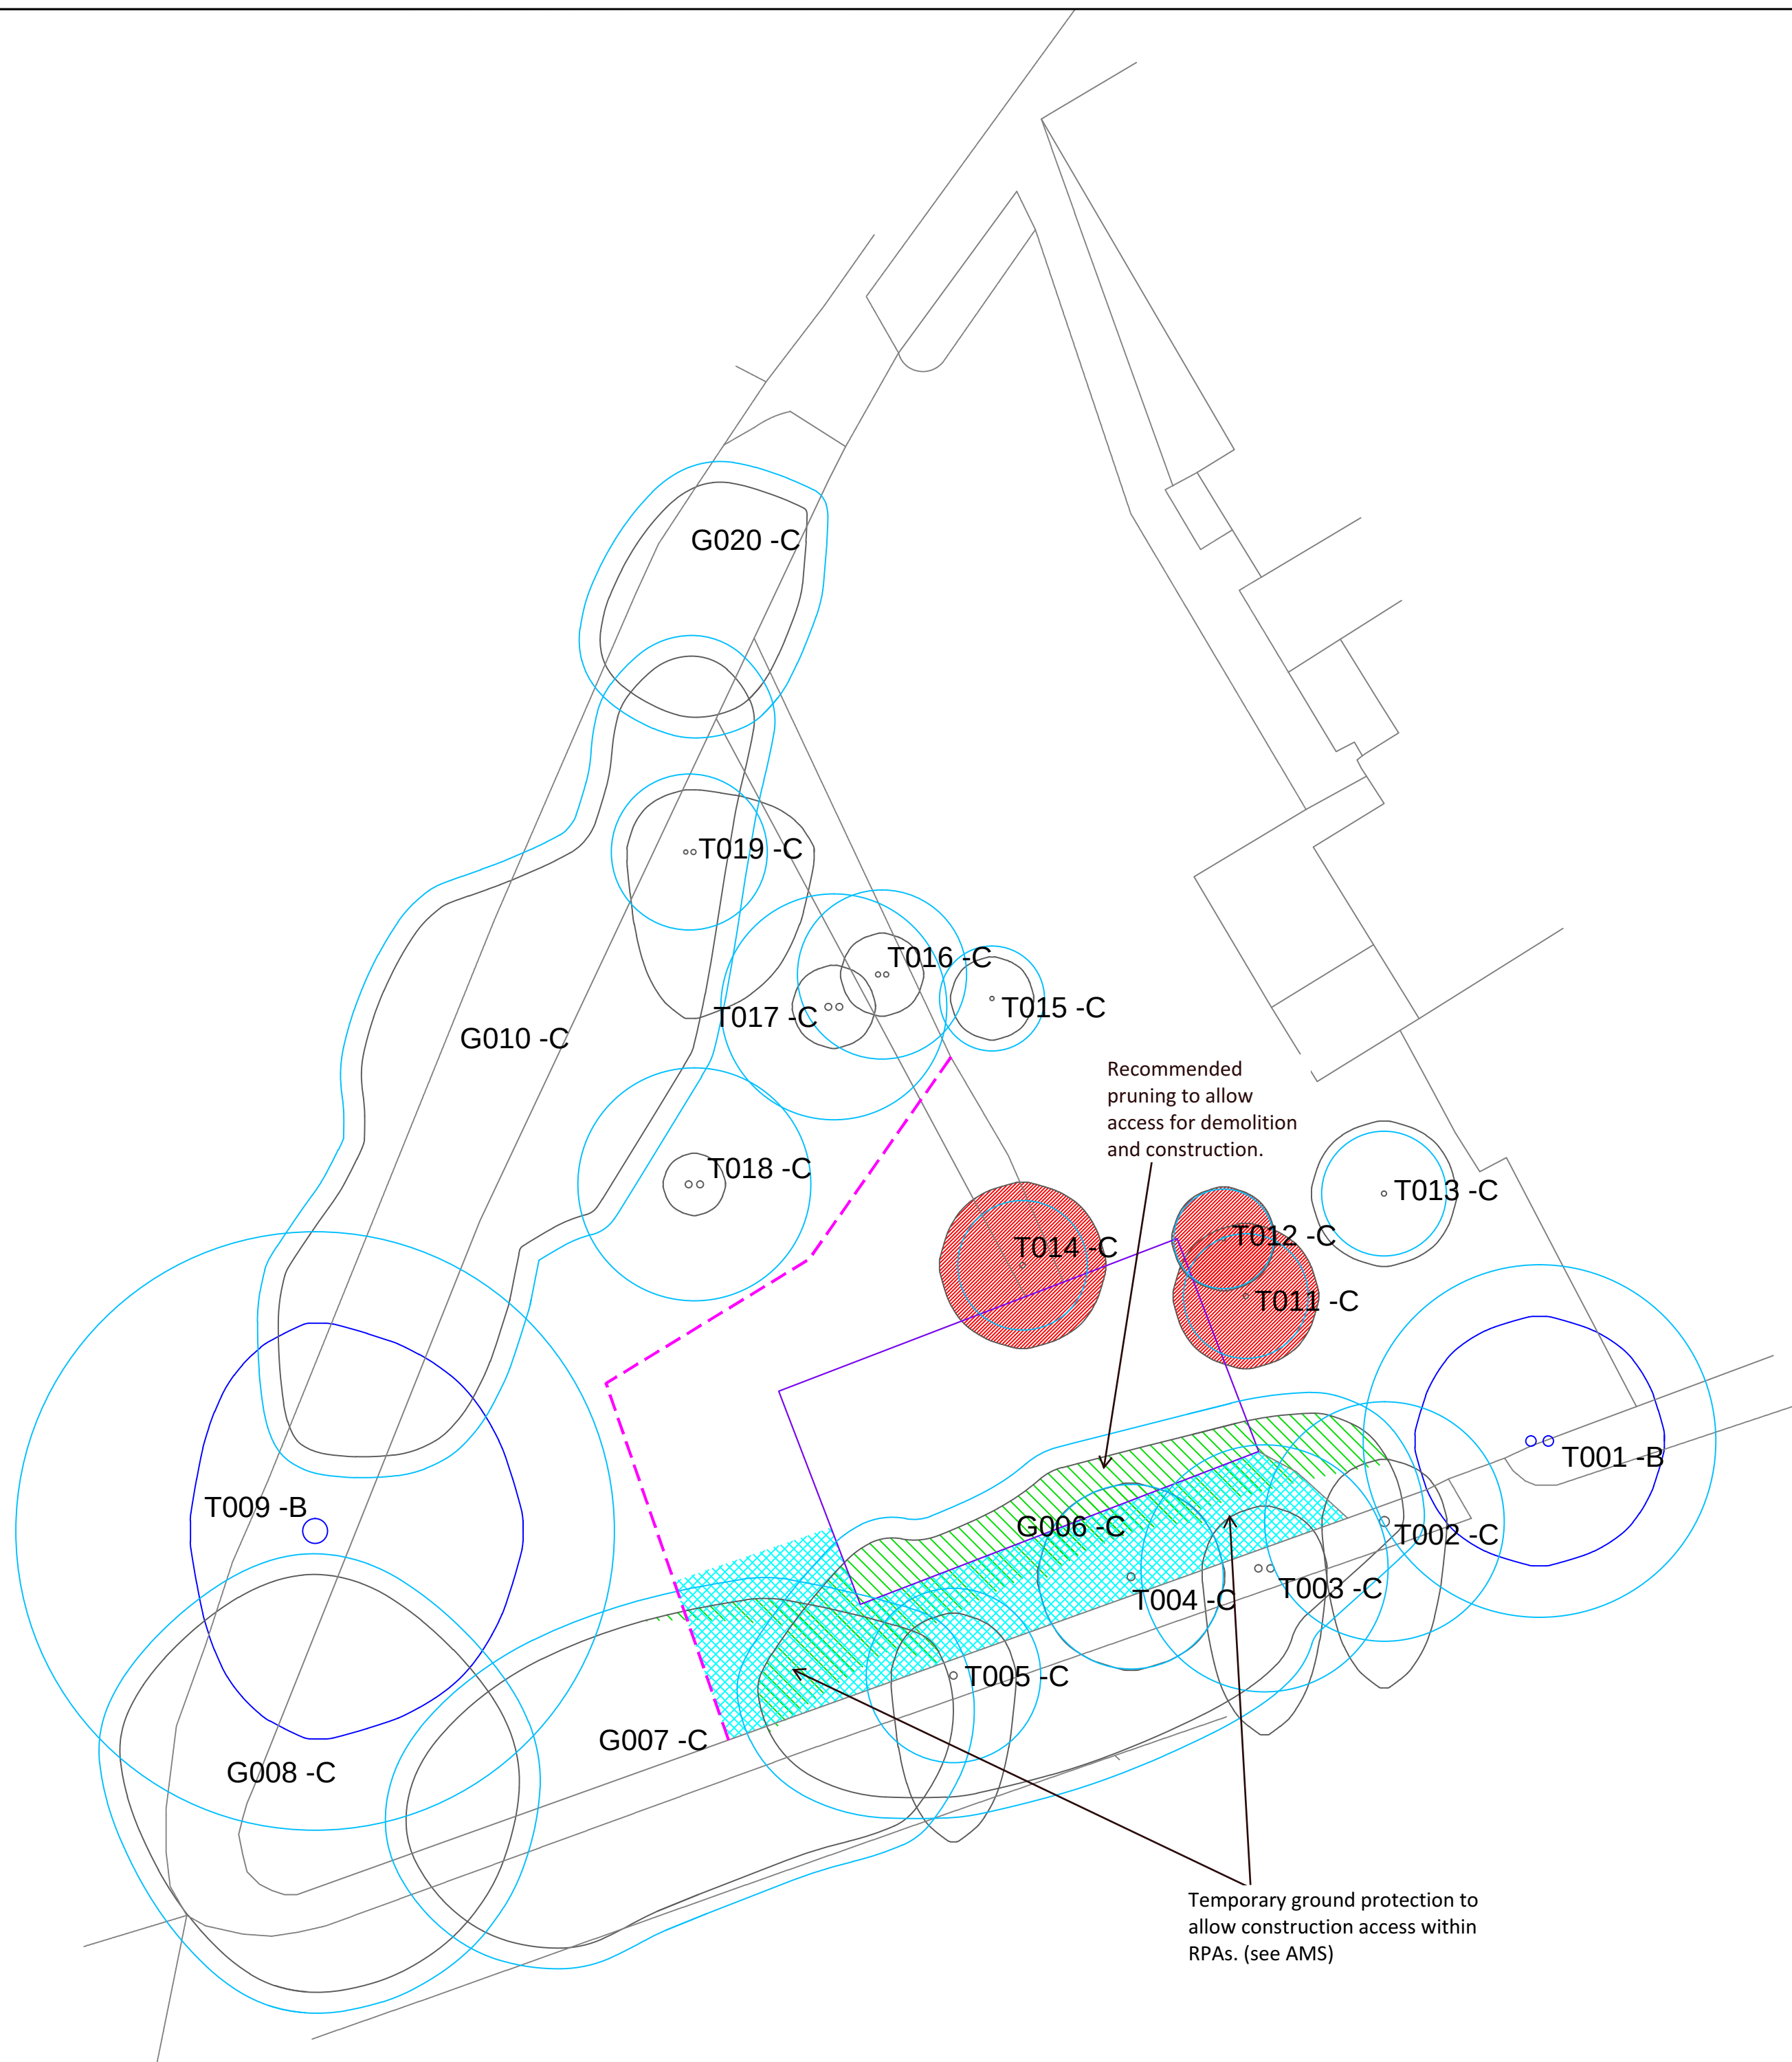

REV	DATE	DESCRIPTION

LEGEND

- Category U
- Category A
Trees of high quality
- Category B
Trees of moderate quality
- Category C
Trees of low quality
- RPA using formula in accordance with BS5837:2012
- Proposed building on same footprint as existing
- Trees to be removed
- Canopy cut back in accordance with BS3998
- Location of Protective Fencing
- Temporary ground protection

Trees categorised in accordance with BS5837:2012 "Trees in relation to design, demolition and construction - Recommendations".

The original of this drawing was supplied in colour, a monochrome copy should not be relied upon.

LOCATIONS ARE APPROXIMATE.

SITE
Hurst Village Community Hub,
School Road, Hurst, Reading, RG10 0DR

TITLE
Tree Protection

REFERENCE
250514-1.0-HVCH-TTP

CLIENT
Hurst Parish Council

DATE
04/08/25

SCALE
1:250 @ A2



Holt
Arboriculture
TREE CONSULTANCY

info@holtarb.co.uk
01252 280256
www.holtarb.co.uk

Appendix C

Tree Constraints Plan



REV	DATE	DESCRIPTION

LEGEND

- Category U
- Category A
Trees of high quality
- Category B
Trees of moderate quality
- Category C
Trees of low quality
- RPA using formula in accordance with BS5837:2012

Trees categorised in accordance with BS5837:2012 "Trees in relation to design, demolition and construction – Recommendations"

The original of this drawing was produced in colour – a monochrome copy should not be relied upon

LOCATIONS ARE APPROXIMATE.

SITE
Hurst Village Community Hub,
School Road, Hurst, Reading, RG10 0DR

TITLE
Tree Constraints

REFERENCE
250514-1.0-HVCH-TCP

CLIENT
Hurst Parish Council

DATE
14/05/25

SCALE
1:250 @ A2



Holt Arboriculture
TREE CONSULTANCY

info@holtarb.co.uk
01252 280256
www.holtarb.co.uk

Appendix D

Tree Survey Limitations

- The assessment of the trees was for the purposes relevant to planning and development and was made on the basis that they will be biennially inspected in the future to identify any changes in size and condition and review the original constraints and categorisations. For these reasons, the tree assessment advice only remains valid for two years from the date that the trees were last inspected.
- This survey is not a tree safety inspection. It is carried out in order to inform the planning process. Where clear and obvious hazards have been observed, these have been addressed in the recommendations (see Appendix A - Tree Schedule). A full assessment of the levels of risk posed by trees would need to consider site use together with tree hazards.
- All observations were of a preliminary nature and did not involve any climbing or detailed investigation beyond what was visible from accessible points at ground level. No invasive or other detailed internal decay detection devices were used in assessing trunk condition.
- The conclusions relate to conditions found at the time of survey. Any significant alteration to the site that may affect the trees that are present or have a bearing on the planning implications (including level changes, hydrological changes, extreme climatic events, or other site works) will require a re-assessment of the trees and the site.
- Each tree, hedge, and group was inspected and the numbering scheme is indicated on the plans. Where important trees were found on site that were not included on the provided plan, their approximate positions and canopy extents are indicated on the plan.
- Offsite trees within influencing distance of the site (typically those located within a distance of up to 12 times their stem diameter away from the site) were included in the survey.
- The data collection is fully compliant with the advice in subsection 4.4.2 of BS 5837.
