

**B.S. 5837 Arboricultural
Method Statement
at
145 Nash Grove Lane
Finchampstead
RG40 4HE
Rev C**

**Client: Chris Evans Consultancy Ltd
145 Nash Grove Lane
Finchampstead
RG40 4HE**

Important note for demolition and construction contractors

This document includes requirements for arboricultural supervision by a suitably qualified arboricultural consultant in certain areas and techniques that may involve a specialised input. Adherence to these requirements is necessary for this document to comply with the Town and Country Planning Act 1990

Prepared by
Simon Hawkins Dip Arb L6 (ABC) N.D Arbor M. Arbor. A.

Date
07/08/2025



Merewood.
Gregory Road, Hedgerley, Bucks. SL2 3XW
M. 07784 915944 T. 01753 647236
E. simon.hawkins@hotmail.co.uk
VAT No: 990 9313 90

1.0 Brief:

- 1.1 I am instructed by Chris Evans Consultancy Ltd to prepare an Arboricultural Method Statement (AMS) in respect of a proposed development of the site at 145 Nash Grove Lane, Finchampstead.
- 1.2 I am to provide instructions for tree retention and protection, including details of appropriate measures that are to be undertaken in order to minimize the impact of development.
- 1.3 The method statement is required to support a planning application for the demolition of the existing and the erection of a new detached dwelling and garage with associated parking and landscaping.

2.0 Arboricultural Supervision

- 2.1 An arboricultural consultant will be appointed by the developer prior to the commencement of any works on the site.
- 2.2 Prior to the commencement of works a set up meeting between the main contractor, any (relevant) sub-contractors, a representative from the LPA and the arboricultural consultant will take place. In the event the representative from the LPA is unable to attend, the arboricultural consultant will make a note of discussions and will advise the LPA in writing.
- 2.3 The meeting will establish a line of communication between the working parties and to understand the parameters of the site, underlining the importance of maintaining and respecting tree protection barriers.
- 2.4 At the meeting the Arboricultural Method Statement (AMS) is to be signed off by the person responsible for the day to day running of the site (normally the site foreman).
- 2.5 By signing off the AMS, the responsible person agrees that he/she has read and understood the method statement and agrees to adhere to it.
- 2.6 In the event of the responsible person being replaced at any time during the development it will be their responsibility to ensure the new person responsible for the site is made aware of the method statement and the need to adhere to the method statement.
- 2.7 A copy of this report will be permanently available on site for the duration of the development activity. It can also be copied for the purposes of tendering, planning the timing of operations and used as a reference as a general guide on how to protect important trees.
- 2.8 A full scale (1:200) copy of the tree protection plan is to be available at all times on site.

- 2.9 No tree work is to take place without obtaining, in writing, the express consent of the Local Authority.
- 2.10 Once the site becomes active the arboricultural consultant will visit on regular occasions to record specific stages of the development (e.g. demolition, laying of foundations, construction etc.).
- 2.11 All site visits are to be recorded on paper and with accompanying photographs. The purpose of recording the visits is to
 - (a) Provide the developer with proof of compliance in the event of any dispute
 - (b) Allow the LPA to discharge the relevant planning conditions

3.0 The development

3.1 Overview

- 3.1.1 The expected programme of site development where arboricultural input is required is as follows:

- 1. Pre commencement meeting
- 2. Installation of protective fencing
- 3. Excavation of foundations
- 4. Erection of main build
- 5. Removal of tree protection measures

3.2 Erection of fencing

- 3.2.1 The tree protection plan (appendix 1) shows the line and position of the root protection fencing to be erected prior to any other works taking place on site.
- 3.2.2 The root protection fencing installation shall be approached from within the central working zone to avoid damage within the root protection area itself, in accordance with the recommendations of BS 5837/2012, as illustrated by Fig. 1.
- 3.2.3 The fencing for the root protection zones shall be constructed of scaffold tube uprights (set at 3m intervals with diagonal braces driven securely into the ground). Thereafter 'Heras' type fencing shall be attached to the scaffold framework using either steel strapping or scaffold clamps. The fencing shall comply with the requirements of the British Standard B.S. 5837:2012 'Trees in relation to design, demolition and construction - Recommendations'.
- 3.2.4 The fenced off areas are to be regarded as a Construction Exclusion Zone (CEZ). This area is to be considered sacrosanct and strictly off limits to any construction activity including any movement of machinery, storage of materials or parking of contractors' vehicles.
- 3.2.5 The fencing protecting the RPA is not to be moved unless this has been specifically detailed in the AMS or with the written agreement of the LPA.

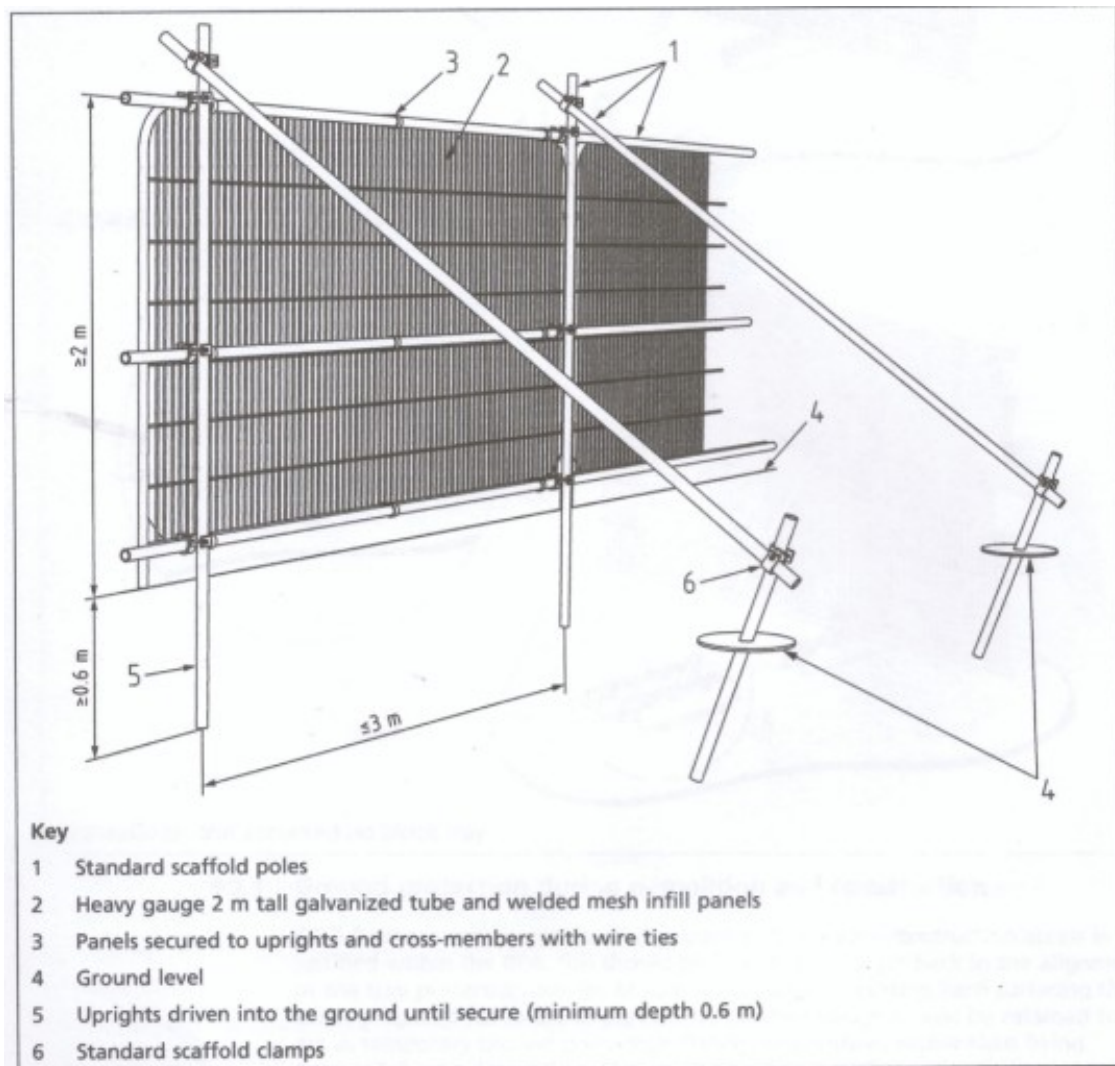


Fig. 1 Protective fencing in accordance with B.S. 5837



Fig 2. Signage attached to fencing reinforces the protection afforded by these barriers

3.2.6 There is to be no burning of any materials or substances within 10m of the root protection barriers.

3.2.7 There is to be no storage of cement bags, chemicals or any other toxic or potentially toxic substances within the CEZ.

3.2.8 Once the fencing has been properly installed, the retained arboricultural consultant will visit the site to confirm the correct installation of the fencing.

3.2.9 The installation of the fencing will be photographed and recorded and a record of this will be passed on to the arboricultural officer at the Local Authority.

3.3 Site access

3.3.1 The site is to be accessed by way of the existing driveway entrances off Nash Grove Lane.

3.4 Foundations

3.4.1 The extensions are expected to be constructed using a strip foundation.

3.4.2 The strip foundations for the exterior walls of the buildings will be excavated working from the back and moving towards the front of the site.

3.4.3 Excavated soil from the foundations will be moved by dumper trucks to the side of the site for disposal by tipper lorry.

3.5 Mortar mixing

3.5.1 Concrete and mortar (when not delivered by cement lorry) will be mixed to the side of the site in a dedicated area within the working area.

3.5.2 All mortar mixing and handling of any other hazardous materials shall take place outside the rpa's of trees. Water run-off from the cleaning of either a mortar tower or concrete mixers is to be directed away from rpa's and will take place as far from trees as possible.

3.5.3 If necessary a confinement area controlling the run-off shall be installed, incorporating an impermeable layer of strong plastic sheeting held within a raised bed. Washing of cement mixers shall take place only within the confined area.

3.6 Storage of materials

3.6.1 Materials are to be delivered by way of Nash Grove Lane to the delivery/set down area at the front of the site.

3.6.2 Materials can be moved about the site across hard surfaces either by fork lift truck, dumper truck, wheelbarrow or by hand.

4.0 Post construction

4.1 Final removal of tree protective fencing

- 4.1.1 Following the conclusion of all construction operations, site huts scaffolding, and protective fencing and ground protection measures will be removed to allow for landscaping operations to take place.
- 4.1.2 Great care is needed at this stage from ground work contractors to continue to observe tree protection requirements. No machines are to be used within rpa's which specifically includes rotovators and all new planting and soil level variations must be agreed and supervised by the arboriculturist.

4.2 Specification for tree planting

- 4.2.1 The landscaping shall include the planting of extra heavy standard trees in proximity to existing trees (to be retained). The trees shall be planted in accordance with the landscape specification prepared by ACD Environmental.
- 4.2.2 All tree pits are to be dug using hand held tools (spade, fork, mattock, etc) only. There shall be no digging by machine.
- 4.2.3 If roots are encountered and root pruning is unavoidable, cuts shall be made at the nearest suitable point in the root system, such as a root junction. Final pruning cuts are to be made at right angles to the axis of the root to leave as small a wound as possible.
- 4.2.4 All pruning cuts shall be made with sharp horticultural tools such as secateurs, pruning shears or a saw (not a spade, shovel, pickaxe or mattock) and the final cut shall be as smooth as possible free of jagged edges.

4.3 Site monitoring

- 4.3.1 The monitoring of the site shall be undertaken by an appointed arboriculturist and shall include site visits to advise and to confirm the correct installation of protective fencing and any other specialist input that may be needed.
- 4.3.2 Each visit shall be recorded and shall include photographs that are to be shared with the Local Authority. This shall take the form of email communication and if considered necessary, further site meeting with the tree officer.
- 4.3.3 The monitoring of the site shall be undertaken by an appointed arboriculturist and shall include site visits to advise and to confirm the correct installation of protective fencing and any other specialist input that may be needed.
- 4.3.4 Each visit shall be recorded and shall include photographs that are to be shared with the Local Authority. This shall take the form of email communication and if considered necessary, further site meeting with the tree officer.

Arboricultural checklist

<i>Ref</i>	<i>Work Activity</i>	<i>Schedule of Works</i>	<i>Refer</i>	<i>Recommendations</i>
General site works and tree related operations				
01	Pre-start site meeting	Pre-start site meeting with LPA tree officer, site manager, client representative and arboriculture consultant to agree scope of any works, where required		
02	Protect trees to be retained	Barriers should be fit for the purpose of excluding construction activity and should remain rigid and complete. Barriers are to be located in accordance with Merewood Tree Protection Plan	B.S. 5837:2012 Trees in relation to design, demolition and construction: Section 6.2.2 Merewood Tree Protection Plan	Ongoing monitoring by appointed person
03	Protective fencing to be inspected by LPA (if required)	Contractors to give LPA at least 2 working days' notice of the erection of the temporary protective fencing.		Appointed person to contact LPA prior to completion of fencing.
04	Maintain the temporary protective fencing	Contractors to ensure the temporary protective fencing is maintained throughout the entire construction period and record any breach of the tree protection.	B.S. 5837:2012 Trees in relation to design, demolition and construction: Merewood Tree Protection Plan	Appointed person responsible for arboricultural protection measures shall monitor fencing monthly, recording details
05	Works within the Root Protection Area (RPA)	Adopt hand dig methods for reducing levels to avoid damage to roots. Where limited root pruning is unavoidable it should be made at a suitable place within the root system, avoiding damage to surrounding tissue. Final pruning cuts shall be made at right angles to the axis of the root. The final cut wound should be smooth and as small as possible, free from ragged torn ends. Where root pruning is required to roots over 25mm in diameter, works should be	B.S. 5837:2012 Trees in relation to design, demolition and construction: Section 7.2 Merewood Tree Protection Plan	All tree work should be carried out by a suitably tree qualified tree surgeon, preferably an Arboricultural Association approved contractor.

		overseen by a suitably qualified Arboriculturist. Any root pruning should be completed in accordance with BS 3998:2010.		
--	--	---	--	--

Signatures:

I confirm that I have attended a pre-application site meeting with the contractors and have gone through the requirements of the Arboricultural Method Statement and that a copy is available in the site office.

Arboricultural Consultant

I confirm that I have attended a pre-application site meeting with the arboricultural consultant and that I am responsible for the correct procedures being followed in accordance with the Arboricultural Method Statement and that a copy is available in the site office.

Site Manager/Foreman**Contact details:**

Simon Hawkins – Arboricultural Consultant 07784 915 944

Planning Consultants – Union 4 Planning 01483 340346

Wokingham Council – Council Offices 0118 974 6000

Tree Protection Plan

