




Drawings to Support Phase 1 Construction Method Statement

Linked to Planning Application 260186
14th April 2026

Second Padel Court Installation




Current
padel court
installed in
May 2025

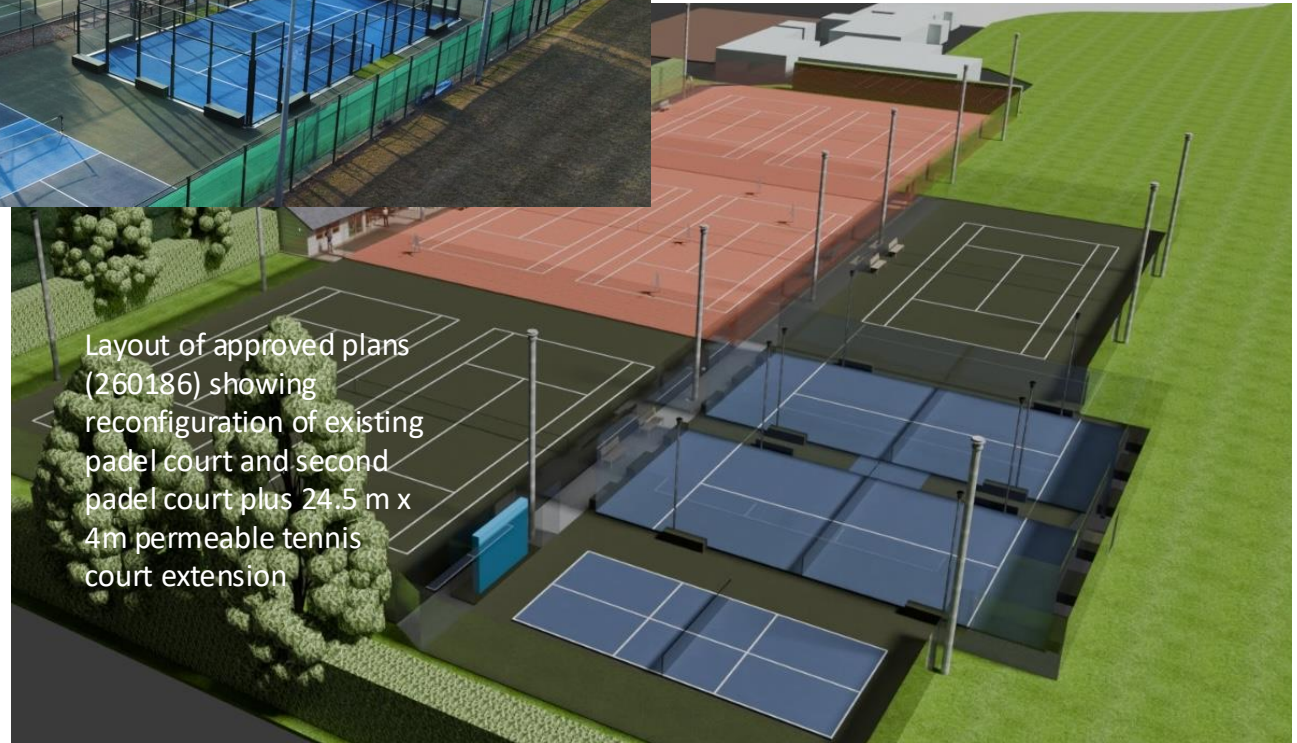

Layout of approved plans
(260186) showing
reconfiguration of existing
padel court and second
padel court plus 24.5 m x
4m permeable tennis
court extension

Second Padel Court Installation

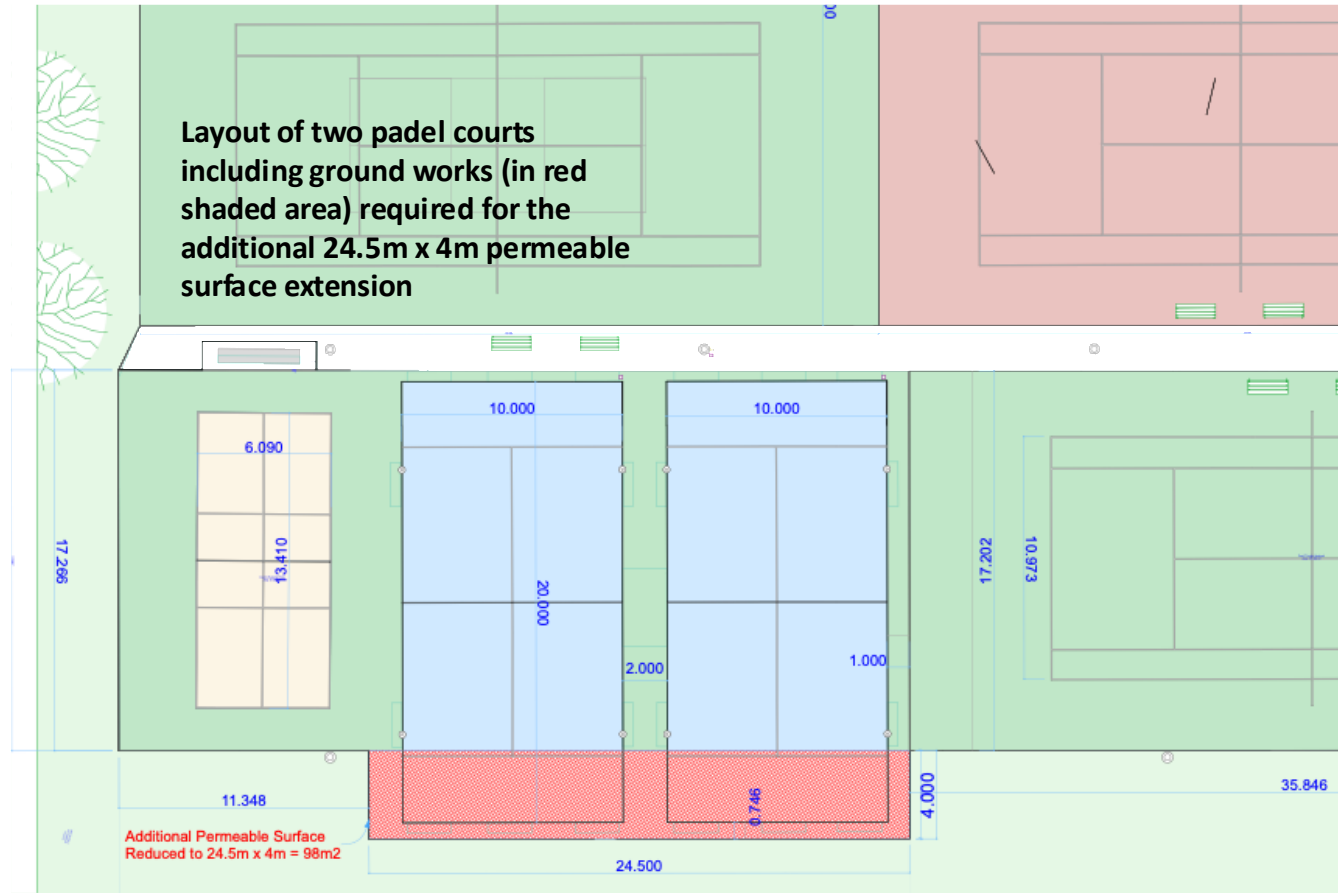

Site Access for Deliveries

Google earth image showing the main access to the site



Delivery and Construction Schedule


#	Items of Work	Start Date	End Date	Notes
1	Delivery of groundworks equipment and protective matting	22/4/26	22/4/26	Delivery on 7.5 tonne x 4 wheel lorry, no additional access requirements. Banksman will be provided to guide vehicle access into the car park area.
2	Laying of matting as per attached drawings to provide tree root protection in line with recommendation in arborist report.	22/4/26	22/4/26	
3	Main ground works to create 24.5 m x 4m permeable surface court extension (included temporary removal of tennis court fencing).	23/4/26	7/5/26	All topsoil to be kept in recreation ground for use in allotments. See attached drawings.
4	Reconfiguration works for existing padel court – uninstall and rotate by 90 degrees from N/S orientation to W/E orientation.	20/5/26	22/5/26	No delivery of equipment. Installation team to arrive in small van.
5	Delivery of 8-yard skip	20/5/26	20/5/26	Delivery on 18 tonne x 4 wheel lorry, no additional access requirements. Banksman will be provided to guide vehicle access into the car park area.
6	Delivery of second padel court	25/5/26	25/5/26	Delivery of all equipment with euro-trailer articulated lorry. Same access plan as for the delivery of our first court in 2025. Banksman will be provided to guide vehicle access into the car park area.
7	Installation of second padel court	25/5/26	29/5/26	Second pop up padel court installed adjacent to reconfigured court.
8	Reinstallation of tennis court fencing	1/6/26	10/6/26	Project complete with fencing replaced as per plan.

Detailed Construction Site Plan




Detailed Construction Site Plan

Access of small earth moving equipment and forklift vehicle for padel court delivery

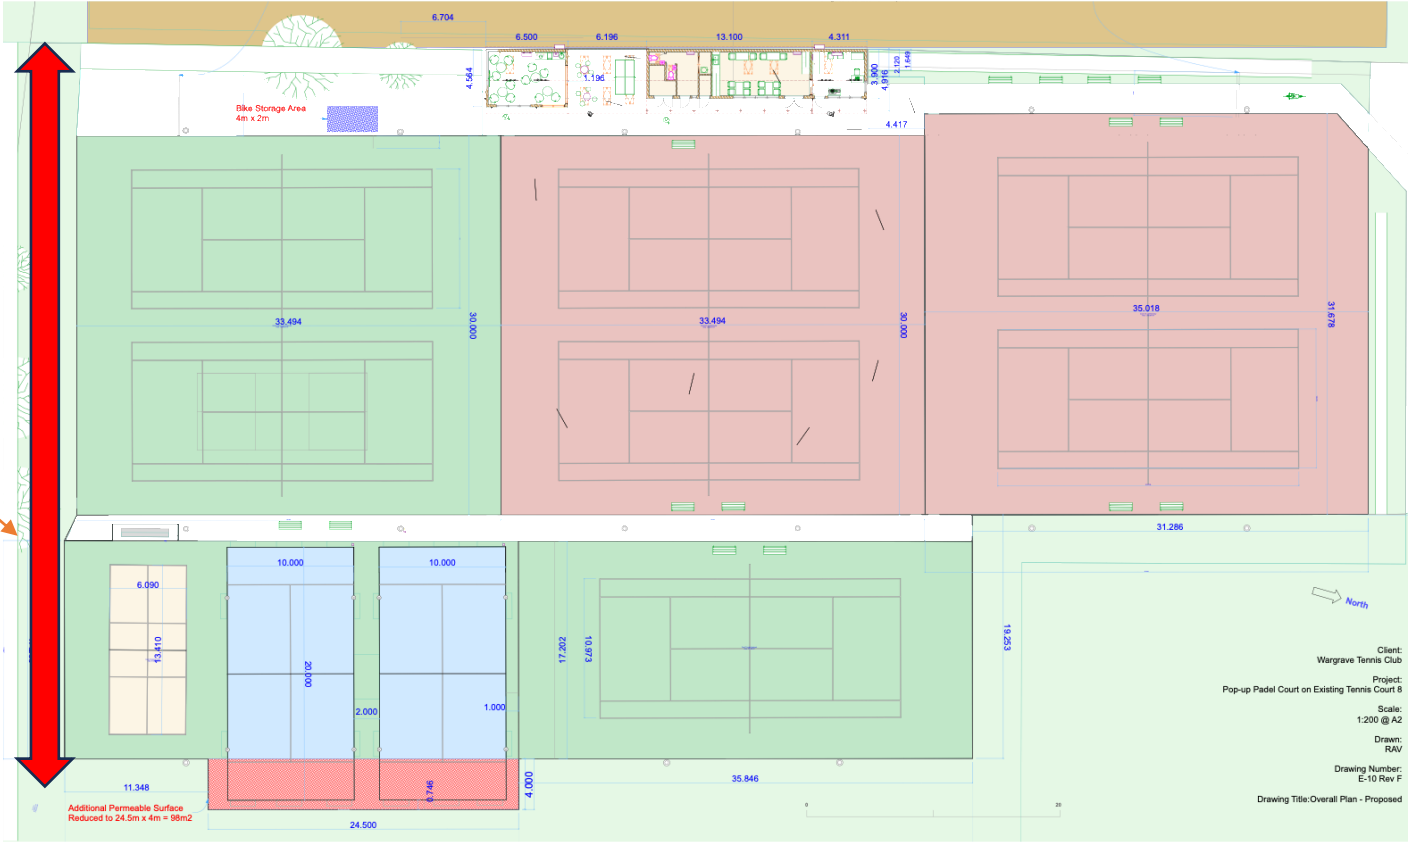

Tree Protection Plan

Tree protection measures in accordance with approved Arboricultural plan

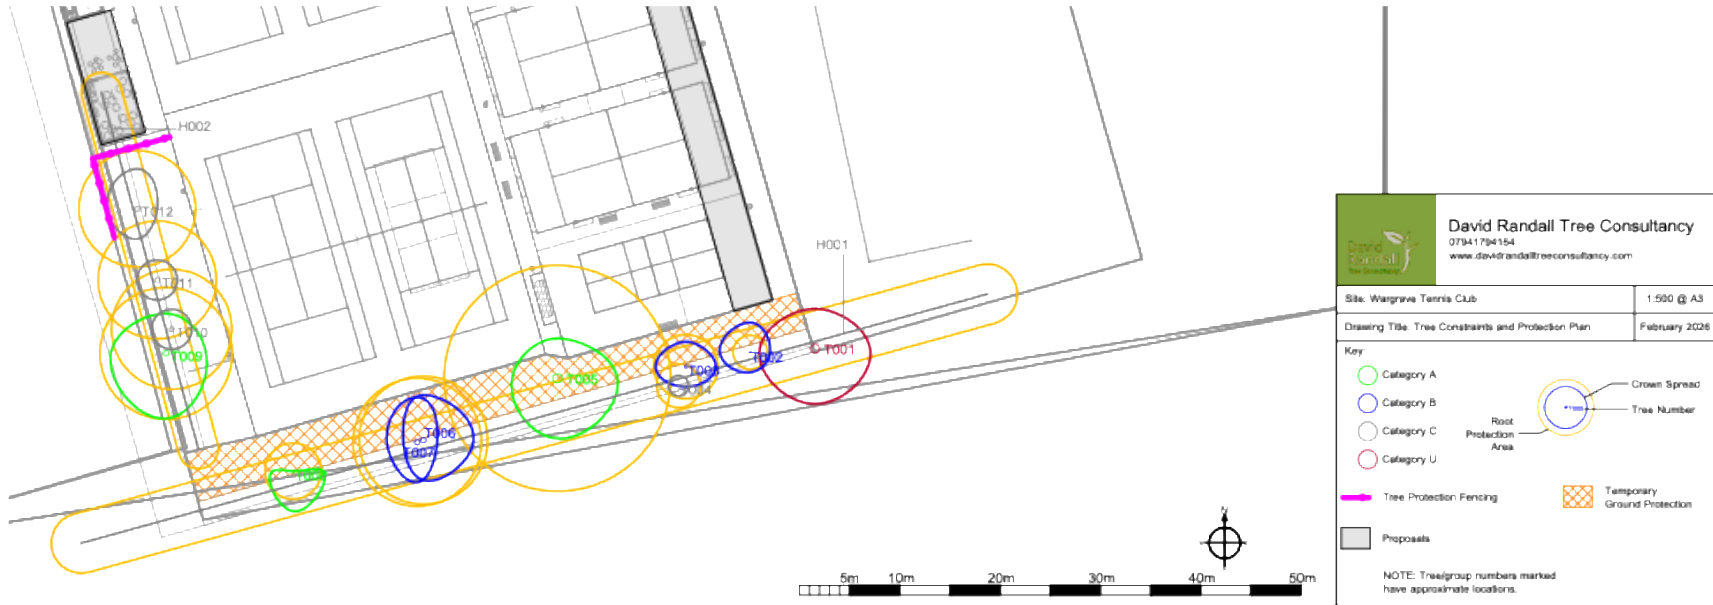

Overall Area Plan

