

ARBORICULTURAL IMPACT ASSESSMENT, PROTECTION PLAN AND METHOD STATEMENT

SITE:	42 WELLESLEY DRIVE, CROWTHORNE, RG45 6AL
SURVEY DATE:	6 FEBRUARY 2024
REPORT DATE:	12 FEBRUARY 2024
OUR REFERENCE:	517-1956-1/26/2024
ON BEHALF OF:	Liz Grierson
AUTHOR:	Mark Harrison, BSc (Hons), MarborA, NDArb




CONTENTS

1. INTRODUCTION	3
2. TERMS OF REFERENCE	3
3. DOCUMENTS SUPPLIED	6
4. PROTECTION STATUS	6
ARBORICULTURAL IMPACT ASSESSMENT	7
5. DEVELOPMENT / SITE APPRAISAL	7
6. TREE CATEGORISATION	7
7. DEVELOPMENT IMPLICATIONS	7
8. SERVICE RUNS	8
9. SITE PARKING, SITE HUTS, MIXING AND MATERIAL STORAGE AREAS	9
10. TREE PROTECTION	9
11. GROUND PROTECTION	11
12. CONSTRUCTION CONSIDERATIONS	12
13. SOFT LANDSCAPING WORKS	14
14. POST DEVELOPMENT PRESSURES	14
ARBORICULTURAL METHOD STATEMENT (PRELIMINARY)	16
15. METHOD AND PHASING OF WORKS	16
16. CONTACTS	17
17. DECLARATION	17
18. CONCLUSION	18
APPENDIX A – TREE SCHEDULE	19
APPENDIX B – GENERIC INFORMATION	24
APPENDIX C – BARRIER INFORMATION	26
REFERENCES	28
DIGITALLY APPENDED TREE PROTECTION PLAN (IN PDF FORMAT)	

ABBREVIATIONS

AIA	Arboricultural Impact Assessment	CMS	Construction Method Statement
AMS	Arboricultural Method Statement	RICS	Royal Institute of Chartered Surveyors
BRE	Building Research Establishment	RPA	Root Protection Area
BS	British Standard	TPBE	Trees and People in the Built Environment
CCS	Cellular Confinement System	TPO	Tree Preservation Order
CEZ	Construction Exclusion Zone	TPP	Tree Protection Plan



1. INTRODUCTION

- 1.1. Harrison Arboriculture Ltd. was commissioned to provide an arboricultural report to include an arboricultural impact assessment, tree protection plan and preliminary method statement for development proposals at 42 Wellesley Drive, Crowthorne, RG45 6AL by Sarah Gould, on behalf of Liz Grierson on 26 January 2024.
- 1.2. The site co-ordinates are 51°22'14.6"N 0°49'22.8"W which lies within the administrative area of Wokingham Borough Council.

2. TERMS OF REFERENCE

- 2.1. To provide an assessment of the trees on and around the site regarding their suitability for retention within the context of the development based on the details provided. It assesses which of those will either have an impact on and/or be impacted upon by the development. The report includes methods by which those impacts can be mitigated if they are available and adheres to the recommendations provided in British Standard 5837:2012 'Trees in relation to design, demolition and construction - Recommendations' (BS 5837)
- 2.2. The report includes:

An Arboricultural Survey

The survey provides a plan indicating the size and positions of the trees on and close to the site. The positions and dimensions are scaled based on the general topographical and building features indicated by the Ordnance Survey plan © Crown Copyright and database rights 2018 OS 100047474, the final plan will be at 1:500 or larger as per RICS specification, it provides:

- Identification details and assessment of the current condition of trees within and close to the red line site.
- Recommendations for remedial works necessary and available to maintain their health and/or safety within the context of the development (for trees within the ownership of the applicants).



- Categorisation as per BS 5837 : 2012.

An Impact Assessment (AIA) / Constraints Plan


Based on the tree survey and proposed layout as illustrated by drawing reference 02-01 Location plan and Block plan provided by Sarah Gould Architects. The impact assessment provides:

- Details of tree loss and works (if any) required in implementing the proposed design.
- Identification of both above and below ground activities proposed in the vicinity of retained trees which may be potentially damaging e.g. removal of existing structures, the installation of hard surfacing, services installation and the location and dimensions of all proposed excavations or changes in ground level, including those necessary for the implementation of the recommended mitigation measures.
- The practicability of the scheme regarding access, adequate working space and provision for the storage of materials.
- Theoretical Root Protection Areas (RPA's) denoted as nominal circular areas centred on the trunk for all trees categorised A and B will be listed in the tree schedule.
- The RPA's for trees categorised C will be included in the tree schedule but will only be relevant where they are not under the ownership or management of the applicant or where they are to be retained within the development.

A Tree Protection Plan (TPP)

This will provide:

- Recommendations for the construction and positioning of suitable tree protection. It includes barrier fencing and both permanent and temporary ground protection where appropriate based on the AIA.
- The report will include possible methods to mitigate the adverse impacts of the development. The TPP illustrates the areas within or close to the RPA's within which measures are necessary to protect the root areas of retained



trees.

Predicted impacts plan

- The predicted impacts are provided on plan reference 517-1956-1/26/2024 TPP and assess the expected impacts of the retained trees post development. The shade prediction is based on guidance provided by Building Research Establishment (BRE) in Site Layout Planning For Daylight and Sunlight - A guide to good practice.

An Arboricultural Method Statement

This will provide a precautionary approach appropriate to the proposals. It will describe the methods and sequence of tree protection that should be adopted in order to demonstrate that the operations can be undertaken with minimal risk of adverse impact on trees to be retained. It may require relevant information from other specialists. It will include some or all of the following:

- any operations proposed within the RPA (or crown spread where this is greater);
- removal of existing structures and hard surfacing;
- installation of temporary ground protection ;
- excavations and the requirement for specialised trenchless techniques ;
- installation of new hard surfacing including materials, design constraints and implications for levels;
- specialist foundations including installation techniques and the effect on finished floor levels and overall height;
- retaining structures to facilitate changes in ground levels;
- preparatory works for new landscaping;
- An auditable/audited system of arboricultural site monitoring, including a process by which adherence to the agreed methods and phasing within this report can be monitored;



- A schedule of specific site events requiring specialist arboricultural input or supervision; and
- A list of contact details for the relevant parties.

2.3. The scope and limitations of the report are listed in Appendix B – Generic Information.

3. DOCUMENTS SUPPLIED

Table 1 - Document summary

Document Title	Provided by	Reference
Location plan and Block plan	Sarah Gould Architects	02-01
Existing Site and parking plan	Sarah Gould Architects	03-01
Existing Ground and First floor plans	Sarah Gould Architects	03-02
Proposed Ground and First floor plans	Sarah Gould Architects	03-06
Proposed Roof and parking plans	Sarah Gould Architects	03-07

4. PROTECTION STATUS

4.1. Trees subject to constraints such as Tree Preservation Orders (TPO) and Conservation Areas are protected under the law. There are trees on or adjacent to the site which are protected by TPO 1421-2012-T11. Any works being undertaken outside the remit of an approved planning application will require a formal application for TPOs and notification of the intended works for trees within Conservation Areas tree Preservation to Wokingham Borough Council.



ARBORICULTURAL IMPACT ASSESSMENT

5. DEVELOPMENT / SITE APPRAISAL

- 5.1. The site is a residential property 42 Wellesley Drive, Crowthorne, RG45 6AL. It was surveyed on 6 February 2024.
- 5.2. The development proposal is for a front and side extension to the existing building and the alteration of the roof pitch to facilitate the installation of solar panels. There are 3 mature trees graded A/B in proximity to the proposed extension one of which is listed as tree 11 of TPO1421-2012.
- 5.3. The default root protection area of one tree lies underneath the existing building which was constructed pre 1975 and therefore is likely to have had an influence on root morphology.

6. TREE CATEGORISATION

- 6.1. The method of categorisation as provided by BS5837 can be found at Appendix A. The following is a summary of the trees present on the site and their grade (table 1). A and B category trees are a material consideration in the development process; the subcategories 1, 2 and 3 are intended to reflect arboricultural, landscape and cultural values respectively.

7. DEVELOPMENT IMPLICATIONS

- 7.1. The primary criterion, in Arboricultural terms, is the retention of as many appropriate trees as practicable, allowing development to proceed whilst providing them with space and protection both during and subsequent to the completion of the development. The following is an assessment of the likely impact of the development on trees which are worthy of retention and guidance on the type and extent of protection required to ensure their continued wellbeing within the proposed development and the future landscape.



- 7.2. Most tree roots are typically found in the upper 600mm of soil and any excavation or compaction of the ground within these areas has the potential to damage roots and impact the future health and potentially the stability of the trees. Therefore, soil structure maintained.
- 7.3. Where the building footprint lies within or close to root areas, traditional concrete filled trench foundations have the potential to remove roots extending beyond the line of the trench.
- 7.4. The area beneath the existing building is around 11.5m² and beneath the existing patio 14.5m² which equates to around 7% of the default RPA. The remaining area around the root area is unsurfaced providing a suitable growth medium for future root growth.
- 7.5. Hand dug trial pits investigating the presence of significant roots would allow the use of trench footings. Roots arising from the pine trees (T1 and T2) <25mm can be cut cleanly to the trench/pit wall without undue impact.
- 7.6. Should roots >25mm be uncovered trench footings are not viable. Pile foundations would reduce the amount of excavation required and would provide satisfactory alternative. The principles of piling close to trees are described in section 12 although it is noted that materials may differ dependent on the engineering requirements suitable for the proposed building. Pile type foundations should be used with ground beams and floor pads positioned as close to the natural ground level as possible.
- 7.7. The proposed extension to the garage and associated parking spaces lie outside of the RPAs of all trees. Barrier fence as described in section 9 will prevent access into the root areas.

8. SERVICE RUNS

- 8.1. We have not been provided with details of underground services at this stage of the project. Due to the nature of the development and the eastern extension forming living space rather than WCs or kitchen, it is assumed that the existing services can be connected to the additional rooms.
- 8.2. Should additional underground electricity, gas or foul and grey water services be



required, they will require routing well outside the protection areas of trees which are to be retained. If the route is likely to pass close to or within the RPAs of the retained trees prohibitions on excavation within the RPA's applies. A specific method statement will be required describing the method to be used to minimise any root damage. These may potentially involve hand digging within the root areas and laying pipework between any significant roots or moling from a position outside the RPA's

9. SITE PARKING, SITE HUTS, MIXING AND MATERIAL STORAGE AREAS

- 9.1. All deliveries, material storage and contractor parking shall make use of the existing access and hard surfaces. Materials must not be stored within the root protection areas indicated by the CEZ as illustrated on plan reference 517-1956-1/26/2024 TPP and marked by barrier fence on site. If additional space is required for the storage and/or mixing of building materials within or close to the RPA's of the retained trees, sufficient ground protection must be installed to prevent soil compaction and/or contamination by any spillage.
- 9.2. Site huts are not required for this site

10. TREE PROTECTION

- 10.1. Exclusion of construction activity from the unprotected recommended root protection areas from the outset will ensure those trees identified for retention are maintained in a safe and healthy condition preventing the following. They should be retained in place for the duration of the development to prevent:
- Root severance
 - Damage to the bark, branches and trunks
 - Compaction of the soil within the Construction Exclusion Zone
 - Alterations in soil level
 - Soil contamination by phytotoxic materials such as herbicides, petrol, oils, diesel, cement and concrete washings or other construction additives




Barrier Fence

- 10.2. Tree protection barriers will be erected prior to the construction process and shall remain in place until completion of the development. Signs will be attached informing all site staff that the area is to remain fenced, examples of signage can be found at the end of this document which can be laminated, or generic signs can be purchase on line.
- 10.3. The barrier fence in accordance with BS5837 2012 Section 6 Figure 3 (figure 1) is considered fit for purpose for this site given the size of the development and the degree of works taking place in proximity to the retained trees. The position of the Tree Protection Fencing is shown on the Tree Protection Plan reference is 517-1956-1/26/2024 TPP appended at the end of this document. This should be constructed with weld mesh panels, at least 2m high, securely fixed together with wire or scaffold clamps and braced with ground anchored supports at a maximum spacing of one every two Heras panels (every 6m) to brace the fence sufficiently to resist impacts. The BS figure has been reproduced at the end of this section.
- 10.4. Any adjustments or removals of the tree protection measures will only be carried out following consultation and agreement with the project arboriculturalist and/or the Local Authority tree officer.
- 10.5. The following shall apply to the areas within the tree protection area:
- No mechanical excavation and excavation by other means only with Arboricultural supervision
 - Hand digging shall only be carried out following a written method statement approved by the project arboriculturist
 - No adjustment to ground levels,
 - No storage of plant or material,
 - No storage or handling of any chemicals including cement washing,
 - No vehicular access,
 - No fires.



Figure 1 - (BS5837 Figure 3) example of fence stabilization system

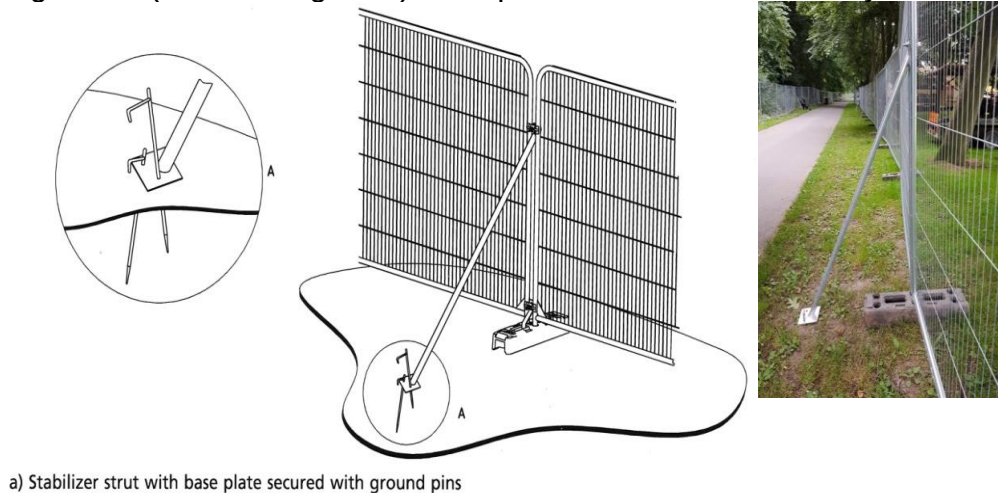

11. Ground Protection

- 11.1. Ground protection will be required where construction activity within or access across the RPA's is necessary. This is to prevent root damage and soil disturbance or compaction and is required for the duration of the development. This will be temporary where incursion is to facilitate the construction and permanent where traffic over the root area is required subsequent to the completion of the development.
- 11.2. Temporary ground protection is required to facilitate activity within the RPA's of trees no. 1 and 2. Permanent protection is not required for this site.

Temporary Ground Protection

- 11.3. The principle of ground protection is to spread the weight of anything using the area to prevent rutting or soil compaction and prevent any spillage leaching into the soil. It must be fit for purpose and designed to support the expected traffic. It should consist of a rigid surface layer over a compressible base (e.g. wood chip) laid over a separation membrane typically of geotextile.

The ground protection might comprise one of the following:

- a. for pedestrian movements only, a single thickness of scaffold boards placed either on top of a driven scaffold frame, so as to form a suspended walkway, or on top of a compression-resistant layer (e.g. 100 mm depth of*




woodchip), laid onto a geotextile membrane;

b. for pedestrian-operated plant up to a gross weight of 2 t, proprietary, inter-linked ground protection boards placed on top of a compression-resistant layer (e.g. 150 mm depth of woodchip), laid onto a geotextile membrane;

c. for wheeled or tracked construction traffic exceeding 2 t gross weight, an alternative system (e.g. proprietary systems or pre-cast reinforced concrete slabs) to an engineering specification designed in conjunction with arboricultural advice, to accommodate the likely loading to which it will be subjected. (British Standards Institute, 2015).

Figure 3: a. Diagrammatic illustration of ground protection within the RPA b. example of temporary ground protection.

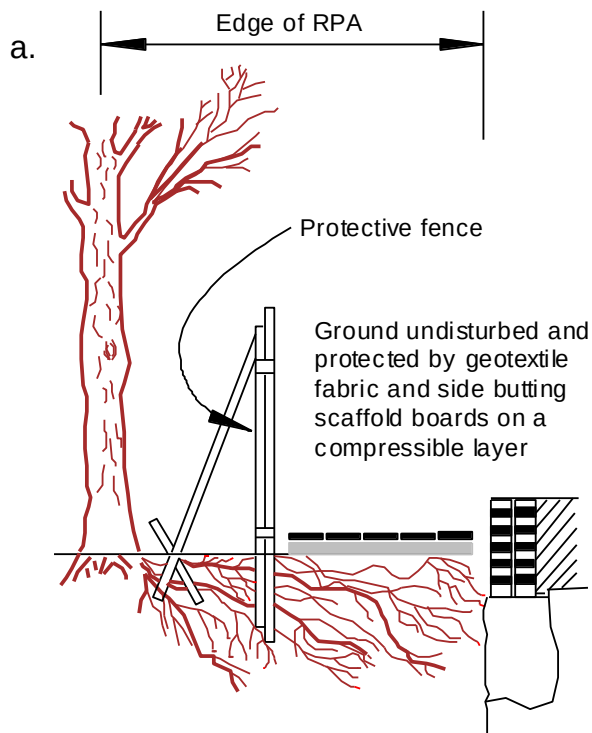

b.




12. Construction Considerations

12.1. Where significant roots (>25mm) arising from trees 1 and 2 are found to be present along the extension footprint ground beams and floor slabs will be designed so as not to require excavation of the existing ground level.




- 12.2. Where piles are to be used, these will be as small as possible to reduce the need for the use of heavy machinery within the RPA, and to minimise the risk of root damage. Pile layout will be designed to allow 150mm movement each way from their centre line, to avoid damage to any roots discovered at the time of construction.
- 12.3. Piles should be bored and poured those located within the RPA of retained trees should be sheathed to protect the soil and adjacent roots from the potential toxic effects of the concrete. piles are preferential to driven piles, as these require smaller machines which have a reduced risk of soil compaction and root disturbance.
- 12.4. Voids beneath ground beam/ floor slab may be filled with 20-40mm gravel or similar no fines material to prevent the ingress of pests.
- 12.5. Ground surface around and beneath the ground slab will be covered with fit for purpose ground protection which is maintained throughout the construction process. Ground protection beneath the proposed slab will only be removed just prior to the final formation of the floor slab.
- 12.6. Diagrams below show the principles of the various methods which are acceptable in arboricultural terms, however other designs which comply with the above performance specification may be equally acceptable.

Figure 3 - Pile and Beam principles (specific measurements to be provided by the engineer)

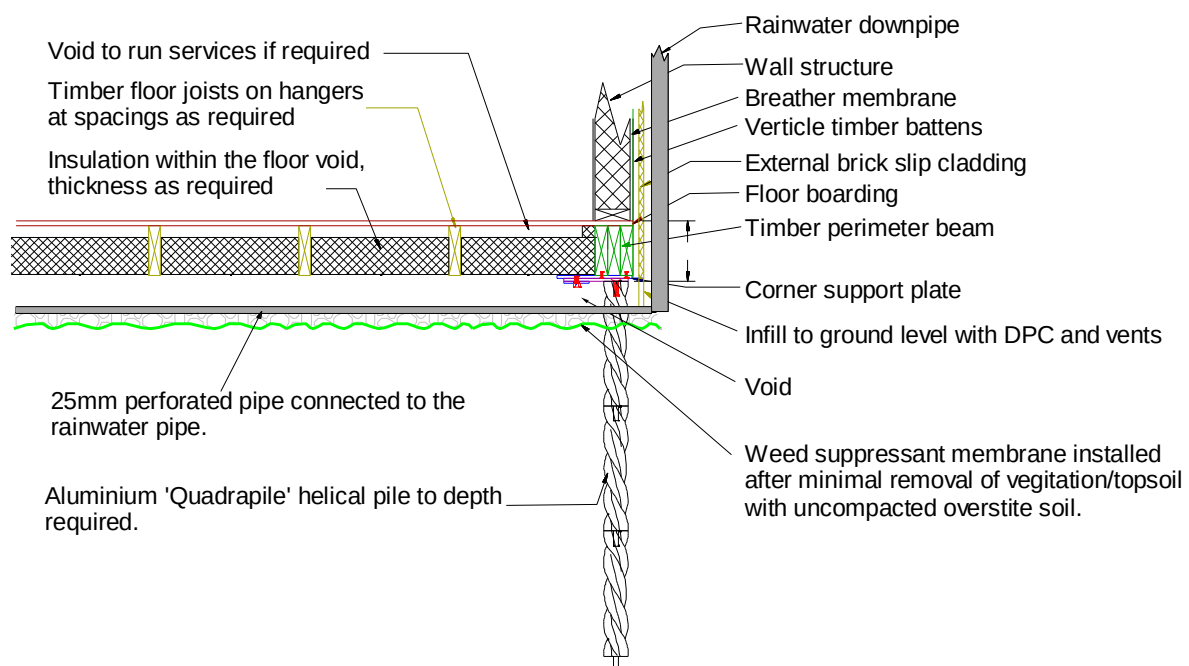

(Diagram courtesy of Quadradrill)



13. SOFT LANDSCAPING WORKS

13.1. Any soft landscaping works within the development area should be in accordance with the approved landscape plan, and any specification of such works approved by the local planning authority which should adhere to the following British Standard Specifications and Codes of Practice:

- Trees should be supplied packaged in accordance with the recommendations of BS 3936:1992 Part 1 Nursery Stock - Specification for trees and shrubs;
- BS 4428:1989 - Code of Practice for General Landscaping Operations (excluding hard surfaces);
- BS 8545:2014 Trees from Nursery to Independence in the Landscape;
- The Code of Practice for Plant Handling 2002 (Horticultural Trades Association).

13.2. The construction exclusion zone will remain off limits for all site plant and machinery unless fit for purpose ground protection is installed. Pedestrian traffic must be kept to an absolute minimum only permitted for the ground preparation and landscape installation work.

13.3. The landscaping works will need to be undertaken in such a way as to avoid level changes, deep digging or mechanical rotovation. Excavation of planting pits within the RPA can cause serious harm the root system of retained trees. Planting pits within the RPA of retained trees will be excavated by hand to avoid damage to roots greater than 25mm and masses of smaller roots.

14. POST DEVELOPMENT PRESSURES

Shading

The expected shading cast by the trees is based on guidance provided by Building Research Establishment (BRE) in Site Layout Planning for Daylight and Sunlight - A guide to good practice (BRE, 1991). The shade predictions are illustrated on the



Tree Protection Plan reference 517/1956/1/26/2024 TPP appended at the end of this document.

Buildings.

Shade predictions are not expected to have an unreasonable impact on the availability of light to living space within the proposed dwellings.

Open spaces.

The shade cast by the retained trees is minimal both at their existing sizes and future size and are not expected to have an unreasonable impact on the reasonable enjoyment of gardens.

Privacy and screening.

Not applicable

Direct damage.

There are no retained trees which are in such close proximity that would result in direct damage at their current size or resulting from future growth.

Seasonal nuisance.

The retained trees do not overhang the proposed building and leaf and debris fall is not expected to impact the dwelling over and above what can be considered typical for this type of setting.

Future pressure for removal.

The design of the site does not present any unreasonable impacts or pressures on the retained trees and no post development pressures for removal are expected.



ARBORICULTURAL METHOD STATEMENT (Preliminary)

15. METHOD AND PHASING OF WORKS

PRE CONSTRUCTION

- 15.1. Prior to the start of any construction, including material storage, protective barrier will be erected as per BS5837 figure 3 as illustrated in section 10.
- 15.2. It will be positioned as denoted on the tree protection plan reference 517/1956/1/26/2024 TPP.
- 15.3. Signage informing all site workers that the area is to remain protected for the duration of the development is to be attached to the fence. An example of signage can be found at the end of this document which can be printed, laminated and securely attached to the barrier fence if required.
- 15.4. Temporary ground protection will be installed prior to the start of construction ground works. This is to provide ground protection to the underlying ground and form a platform from which works can be undertaken. Any spoil resulting from the excavation of the footings must not be stored over the root area.
- 15.5. The project arboriculturalist will be on hand to provide advice and/or supervision if required.

CONSTRUCTION

- 15.6. All barrier fence and ground protection is to remain serviceable and in position for the duration of the development. No adjustments are to be made unless with the written agreement of the planning/arboricultural officer.
- 15.7. Excavations for all piles if required are to be excavated by hand from fit for purpose ground protection within the RPA's. The ground protection is to remain in place and only removed to allow the final installation of the floor slab.



- 15.8. Landscaping works may be necessary prior to the completion of the build. In this case prohibitions on traffic and movement over the Construction Exclusion Zones will remain in effect and activity will require additional fit for purpose temporary ground protection, no machine movements and the transport of materials into these areas will be made manually.
- 15.9. The project arboriculturalist will be on hand to provide arboricultural advice if it is needed.

POST CONSTRUCTION

- 15.10. Barrier fence and temporary ground protection is to be removed.
- 15.11. Site reinstatement and landscaping will be undertaken. Prohibitions on traffic and movement over the Construction Exclusion Zones will remain in effect and activity will require additional fit for purpose temporary ground protection, no machine movements and the transport of materials into these areas will be made manually.

16. CONTACTS

Organisation	Contact Name	Contact number	Email / online contact
Applicant	Liz Grierson	-	-
Agent	Sarah Gould, Sarah Gould Architects	07979712649	sarahgouldarchitects@gmail.com
Harrison Arboriculture	Mark Harrison	07915 847 367	mark@harrisonarboriculture.co.uk
Wokingham Borough Council	Case officer	0118 974 6000	https://www.wokingham.gov.uk/contact-us

17. DECLARATION

- 17.1. The statements in this report are based on information provided by the client. It does not take into account, the effects of extremes of climate, vandalism or accident. Harrison Arboriculture cannot accept liability in connection with these factors, nor where prescribed work is not carried out in a correct and professional manner in accordance with current good practice.



17.2. The authority of this report is effective for two years from the date of the survey or when any site conditions change, or pruning or other works unspecified in the Report are carried out to, or affecting, the subject tree(s), whichever is the sooner. It is recommended that a new survey be carried out after twelve months or following any severe weather event or change in the site.

18. CONCLUSION

- No tree removals are required to facilitate the proposals.
- Post development pressures for works on the retained trees are not expected as a result of the proposal.
- The proposed development would not have adverse impacts on the long-term vitality of the retained trees providing the methodology set out in this document are followed.



APPENDIX A – TREE SCHEDULE

Site: 42 Wellesley Drive, Crowthorne, RG45 6AL

Date: 6 February 2024

* Recommendations are provided based on the initial survey independent of the proposal by default. Recommendations in italics within parentheses relate to works required to facilitate the development as identified by the impact assessment.

Tree no	Species	Height/m	Diameter/mm	Age	Condition		Life Exp / yrs	Canopy Height/m				First Significant Branch Hgt/m	Canopy Spread/m				Comments	Recommendations	Category	Root protection	
					Physiological	Structural		N	E	S	W		N	E	S	W				Radius/m	Area/sqm
T1	Pinus sylvestris (Pine)	22	630	Mature	Fair	Fair	10+	12	15	17	15	10(W)	6.5	5	5	4.5	Broken/lost leader. Major dead wood >50mm. Minor dead wood <50mm.	Remove major deadwood.	B2/C1	7.56	179.58
T2	Pinus sylvestris (Pine)	22	890	Mature	Fair	Fair	10+	10	20	18	10	10(W)	6.5	5.5	2	8	Minor dead wood <50mm.	None required at time of inspection.	B1/A2	10.68	358.38
T3	Pinus sylvestris (Pine)	26	840	Mature	Fair	Fair	10+	20	20	16	16	17(S)	4	6	5	3.5	Bulges / swelling trunk. Minor dead wood <50mm.	Remove major deadwood.	B1/A2	10.08	319.25



Key

1. Tree Ref No:

This relates to the numbers on the plan. Where trees have been tagged, the tag number will be used as the tree reference number. Individual trees are not prefixed and prefixed with a G, W or H represent a group, woodland or hedge respectively.

2. Species:

The name given is the Latin name by default. Where common names are given they are shown in parentheses.

3. DBH (Diameter at breast height):

This is the stem diameter at 1.5 metres (breast height) above ground level, given in millimetres. Where trees are multi-stemmed trees the square root of the combined stem diameter is calculated.

4. H (Height):

The height of the tree measured where possible or estimated and recorded in metres.

5. Canopy Spread (Crown radius):

The average crown spread taken from the centre of the trunk to the tips of the live lateral branches given in metres. Measurements following the compass points North, East, South and West.

6. Canopy height:

Ave - Average Crown Height Clearance: (HaB Height above ground) — ground clearance of the canopy for each cardinal point given in metres.

7. First significant branch

The height of the first significant branch the direction of which is shown in parentheses.

8. Age:

Age assessment is based on growth stages rather than actual age in years and are recorded as follows

Y Young



SM Semi Mature – having reached up to 1/3 life expectancy

EM Early mature - having reached 1/3 of the expected life expectancy and is transitioning into maturity.

M Mature - over 2/3 life expectancy

OM Over-mature - fully mature, past peak condition and beginning to decline

V Veteran - trees of interest biologically, aesthetically or culturally because of significant age.

9. Condition

Physiological – Assessment of the overall health and vigour of the tree compared to what would normally be considered typical of a healthy tree of the species.

Condition categories are given as good, fair, poor or dead.

Structural – Assessment of the structural stability of the tree based on visible signs of decay, damage, genetic weaknesses or faults. Structural categories are given as good, fair, poor or dead

10. Life Expectancy:

An estimate of the potential worthwhile remaining contribution – future life expectancy of the tree(s) in the present setting given normal circumstances, given in years (< = less than > = greater than) categorised <10 years, 10 – 20 years, 20 – 40 years and > 40 years.

11. Category:

A quality assessment of the trees based on criteria detailed in BS5837:2012 Table 1

U: Trees unsuitable for retention

A: Those of high quality and value

B: Those of moderate quality and value

C: Those of low quality and value

Assessments are based on their condition on the day of inspection and cannot account for future changes in circumstances.

12. Recommendations:

Preliminary management recommendations in relation to the proposed



development are made where appropriate. These may include remedial tree works that are deemed necessary to improve the quality of the tree or for safety reasons. Recommended tree works will be required to be in accordance with British Standard 3998:2010 Tree Work.

13. Root Protection

Radius – nominal circle centred at the stem centre providing the recommended radius of a circular area necessary for the continue wellbeing of the tree based on recommendations provided in British Standard 5837:2012

Area – The area necessary for the continue wellbeing of the tree based on recommendations provided in British Standard 5837:2012



Table 1

Category and definition	Criteria			Identification on plan
Category U Those in such a condition that cannot realistically be retained as living trees in the context of the current land use for longer than 10 years	• Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning) • Trees that are dead or are showing signs of significant, immediate, and irreversible overall decline • Trees infected with pathogens of significance to the health and/or safety of other trees nearby or very low quality trees suppressing adjacent trees of better quality NOTE Category U trees can have existing or potential conservation value which it might be desirable to preserve			DARK RED
TREES TO BE CONSIDERED FOR RETENTION				
Category and definition	Criteria — Subcategories			Identification on plan
	1 Mainly arboricultural values	2 Mainly landscape values	3 Mainly cultural values, including conservation	
Category A Tree of high quality with an estimated remaining life expectancy of at least 40 years	Trees that are particularly good examples of their species, especially if rare or unusual, or essential components of groups, or of formal or semi-formal arboricultural features (e.g. the dominant and/or principal trees within an avenue)	Trees, groups or woodlands of particular visual importance as arboricultural and/or landscape features	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood-pasture)	LIGHT GREEN
Category B. Trees of moderate quality with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of remediable defects including unsympathetic past management and minor storm damage) such that they are unlikely to be suitable for retention beyond 40 years; of trees lacking the special quality necessary to merit A categorisation	Trees present in numbers, usually as groups or woodlands, such that they form distinct landscape features, thereby attracting a higher collective rating than they might as individuals but which are not, individually, essential components of formal or semi-formal arboricultural features (e.g. trees of moderate quality within an avenue that includes better, A category specimens), or trees situated mainly internally to the site, therefore individually having little visual impact on the wider locality	Trees with material conservation or other cultural benefits	MID BLUE
Category C. Trees of low quality with an estimated life expectancy of at least 10 years, or younger trees with a stem diameter below 150 mm	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories	Trees present in groups or woodlands, but without this conferring on them significantly greater landscape value, and/or trees offering low or only temporary screening benefit	Trees with very limited conservation or other cultural benefits	GREY
	NOTE Whilst C category trees will usually not be retained where they would impose a significant constraint on development, young trees with a stem diameter of less than 150 mm should be considered for relocation			



Appendix B – Generic information

TREE SURVEY

Scope and Limitations of Survey

1. This survey and report are concerned with the arboricultural aspects of the site only.
2. Only trees of significant stature were surveyed. Trees with a stem diameter of less than 75mm when measured at 1.5m above ground level (DBH) have been excluded unless they have particular merit that warrants comment.
3. The survey is restricted to trees that will be affected by the development within and adjacent to the site in accordance with guidelines detailed in British Standard 5837:2012 and with good practice as promoted by the Arboricultural Association and Arboricultural and Forestry Advisory Group (AFAG).
4. This survey is based on a ground level tree assessment and examination of external features only — described as the 'Visual Tree Assessment' (Mattheck and Breloer, The Body Language of Trees, DoE booklet Research for Amenity Trees No. 4, 1994). Although the structural conditions of the trees are considered and remedial action may be recommended it does not constitute a comprehensive Health and Safety report and if one is required it should be commissioned separately. No tissue samples were taken or internal investigations carried out.
5. No soil samples were taken or soil analyses carried out and the risk of tree-related subsidence to structures has not been assessed.
6. Consideration should be given to the timing of the proposed tree works to avoid the active growing period of trees. Tree work should ideally be carried out during the dormant period from November through to February and then again from June to August.
7. Although considered and wildlife habitat potential highlighted, no specific wildlife assessment has been carried out. It should be noted that The Wildlife and Countryside Act 1981, as amended by the Countryside Rights of Way Act 2000 and Conservation - Natural Habitats -Regulations 1994 provides statutory



protection to birds, bats and other species that inhabit trees.

8. This report should be read in conjunction with the Tree Protection Plan. The position of all trees and existing or proposed features are based on the plans provided by the client or other instructed professionals. Where trees have been omitted from the plans provided their position has been estimated or where possible plotted by triangulation.

Survey Method

1. In order to provide a systematic and consistent evaluation of the trees situated on the site, the following methodology was used in accordance with BS 5837: 2012.
2. The stem diameters of single stemmed trees were measured in millimetres at 1.5m above ground level (DBH). Multi-stemmed trees were measured at 1.5m above ground level and the RPA arrived at as per section 4.6a BS 5837:2012.
3. The height of visible trees was measured using a clinometer and estimated visually where view to the upper canopy obstructed.
4. The crown radii were measured where possible or estimated where access is restricted and are given for each cardinal point.
5. Where access to trees was obstructed or obscured, dimensions have been estimated.
6. Each tree has been assessed in terms of its arboricultural, landscape, cultural and conservation values in accordance with BS 5837: 2012 which are detailed in the Tree Schedule.



CONSTRUCTION EXCLUSION ZONE

BARRIER FENCE MUST NOT BE MOVED

**THE FOLLOWING IS PROHIBITED WITHIN THE
PROTECTED AREA**

No excavation, mechanical or otherwise

No adjustment to ground levels

No storage of plant or material

No storage or handling of any chemicals

No vehicular access

No fires



Additional examples of suitable signage





REFERENCES

- BRE. (1991). *Site Layout Planning For Daylight and Sunlight - A guide to good practice*. Construction Research Communications Ltd.
- British Standards Institute. (2015). Surveying for Bats in Trees and Woodland. *BS 8596*. British Standards Institute.
- Countryside Rights of Way Act . (2000). London: HMSO.
- H., M. C. (1994). *The body language of trees, Research for Amenity Trees no. 4*. HMSO.
- K. Rogers, V. L. (2014). Trees and People in the Built Environment II. *Determining Tree Growth in the Urban Forest*, (p. 84).
- Lonsdale, D. (2001). *Principles of Tree Hazard Assessment and Management*. London: HMSO.
- Rogers et al. (2014). TPBE II paper - Determining tree growth in the urban forest. Institute of Chartered Foresters.
- Technical Committee B/213, Trees and tree work. (2010). *Tree work - Recommendations*. London: BSI Standards Limited.
- Technical Committee B/213, Trees and tree work. (2012). *Trees in relation to design, demolition and construction - Recommendations*. London: BSI Standards Limited.
- Wildlife and Countryside Act. (1981). London: HMSO.



Legend

- Category A trees - Trees of high quality and value such that they make a substantial existing and future contribution for an expected 40 years or more.
- Category B trees - Trees of moderate quality and value such that they make a significant future contribution for an expected 20 years or more.
- Category C trees - Trees of low quality and value which might be expected to remain for around 10 years or less or with stems of less than 150 mm diameter.
- Category U trees - Trees of low quality and value which are considered to have little or no potential due to disease or defects.

Number suffixes relate to the subcategories 1, 2 and 3 which are intended to reflect arboricultural, landscape and cultural values respectively

Direction of the first significant branch

The root protection area is the theoretical area considered necessary to provide sufficient room for the root growth required to support the tree - activity impacting the soil should be avoided.

The construction exclusion zone (CEZ) is the area within the root protection area. Access into this area should be prohibited for the duration of the project unless suitably protected to prevent any construction activities including storage.


Barrier fence to be installed as per BS5837, section 6, Figure 3.

The shade prediction is based on guidance provided by Building Research Establishment (BRE) in Site Layout Planning for Daylight and Sunlight - A guide to good practice (BRE, 1991)

Proposals

Temporary ground protection provides protection to roots and underlying soil within the RPA's of retained trees during the development to provide work space.

Figure 3 BS 5837 : 2012 - Default Specification for Protective Barrier



CLIENT	Liz Grierson									
SITE	42 Wlesley Drive, Crowthorn.									
DRAWING	Title	Tree Protection Plan								
	Version	0.1				Revision	A			
	Base plan ref.	02-01 Location plan and Block plan								
DRAWING NO.	517-1956-1/26/2024 TPP									
SCALE	1:200 @ A3									
DATE	10 February 2024									
DRAWN BY	M.Harrison									
Harrison Arboriculture Ltd.  Telephone - 07915 847 367 email: admin@harrisonarboriculture.co.uk										
