



ALLARBORICULTURE

23 Southernhay Avenue, Bristol, BS8 4TJ

07375110399 | 0800 107 3652

e – info@allarboriculture.co.uk

ARBORICULTURAL IMPACT ASSESSMENT AND METHOD STATEMENT

BS5837:2012

On behalf of:

Alex Smith

Site address:

20 Rotherfield
Avenue,
Wokingham,
Berkshire,
RG41 2EX

Prepared by:

Kristian
Chesterman BSc
(Hons)

Report

reference:

AAAIA20RO

Report date:

3rd May 2024

Contents

Chapters	Content	Page no.
1.0	Instruction	3
2.0	Statement Of Purpose	3
3.0	Associated Documents	3
4.0	Site Description	3
5.0	Vegetation Description	3
6.0	Arboricultural Impact Assessment	4
7.0	Method Statement	5
Appendix 1	Tree Survey Schedule	
Appendix 2	Protection	
Appendix 3	Tree Protection Plan	

1.0 Instruction

All Arboriculture has been instructed by Alex Smith to undertake a tree survey in accordance with BS5837:2012 *Trees In relation to design, demolition and construction – Recommendations*, and to produce an Arboricultural Impact Assessment, Arboricultural Method Statement and Tree Protection Plan. The instruction was received on the 27th March 2024. The tree survey was carried out on the 1st May 2024.

2.0 Statement of purpose

The purpose of this report is to provide local planning authorities with sufficient arboricultural information to consider the effect of the proposed development on nearby trees, and to demonstrate that trees have been carefully considered throughout the development process. The report includes an arboricultural method statement that describes how work will be undertaken to provide adequate protection of retained trees.

3.0 Associated documents and drawings

This report should be read in conjunction with the following documents and drawings:

1. 08 Existing and Proposed Block Plans
2. British Standards Institute - BS5837:2012 *Trees in relation to design, demolition and construction – Recommendations*
3. Tree Protection Plan – AATPP20RO

4.0 Site description

The site is in the urban area of Wokingham and is a detached residential dwelling. The proposal is the erection of rear and side extension. The site falls under the jurisdiction of Wokingham Council who have advised the property is not within a Conservation Area and there are no Tree Preservation Orders present onsite.

5.0 Vegetation description

The vegetation consists of 5 Category C trees. Some tree protection measures and working methodology (in accordance with BS 5837:2012) will ensure they are not detrimentally affected during construction.

6.0 Arboricultural impact assessment

Table 1: Summary of impacts	
Tree removal	None
Facilitation pruning	None
Demolition within RPA	None
New surfacing within RPA	None
New structures within RPA	None

Building construction in relation to tree roots: No tree removal or facilitation pruning is required for the implementation of the proposed. The RPA of T2 is close to the proposed but due to the change in level and the proposed being within the existing footprint traditional foundations may be used and will not impact on any of the retained trees.

Building construction in relation to tree crowns: It is important that sufficient growing space is allowed between the mature crown extent of each tree and the roof edge of the proposed structures. This is to reduce conflicts of interest in the future and to reduce the pressure to prune trees to keep them clear of roofs which is the case for this proposal.

Tree root and canopy protection: The RPA (Root protection area) of the retained trees should be protected during the development phase with heras fencing to ensure heavy machinery is not operated, or materials stored within the rooting area. This can be detrimental to the trees, causing soil compaction and root die back. The protection of the RPA and canopy spread is detailed in the Arboricultural Method Statement below.

Special surfacing: I do not consider special surfacing to be warranted.

Materials delivery, storage and handling: Materials should not be handled or stored within the RPAs of retained trees; the load exerted can result in soil compaction and leachate from spills can be toxic to trees.

Surface drains, soakaways and services: It is important that services, surface drains and soakaways avoid the RPAs of retained trees as roots can be damaged during trench excavations. The location of services should therefore be agreed with the local planning authority prior to the development phase commencing.

Shading: The shading effects of trees should be taken into consideration when locating fenestration. Where structures are located too close to trees and to the north of them, the shade cast by the trees may prompt requests to fell or prune in the future and is therefore not encouraged by local planning authorities.

7.0 Arboricultural Method Statement

Implementation and phasing of the proposed development: Prior to any building work commencing on site, a meeting will be held with the tree consultant and site manager present. During the meeting details regarding the location of heras fencing will be discussed and a time to reconvene in order to assess the heras fencing and ground protection will be agreed. The schedule of events during the development phase will be as follows:

Heras fencing will be installed as indicated in plan AATPP20RO.

During the development phase, the arboricultural consultant will be notified and asked to supervise any excavating within the RPA of retained trees.

Tree protection barriers: Protective fencing will be installed prior to the commencement of any development activity and will be retained in the positions shown on the tree protection plan (AATPP20RO). The fencing will be to the BS 5837:2012 'Trees in relation to design, demolition and construction – recommendations' (section 6.2) i.e. preformed galvanised steel mesh panels ('Heras') or similar facings on a driven braced scaffold pole framework. It will be retained at the locations shown until construction is completed. It may be moved or removed only with notice to and consent from the local planning authority.

Ground protection: Temporary ground protection will not be required.

Storage and handling of materials: This site has sufficient space for materials to be stored and handled.

Contractors parking: There is sufficient space on Rotherfield Avenue for parking.

Welfare facilities: Toilets and hand washing facilities shall be made available within the property.

Surface drains, soakaways and services: RPAs will be avoided in the drainage design however, in the unlikely event that existing cables need to be unearthed within an RPA, the method for doing so will accord with the recommendations in the NJUG Publication: Volume 4: Issue 2: 16/11/2007: Guidelines for the planning, installation and maintenance of utility apparatus in proximity to trees. Trenches will be dug by hand and any roots over 2.5cm in diameter will be retained undamaged. Smaller roots may be cut back to the proximal face with a clean, sharp pair of secateurs. The trench backfill around the roots shall be a granular material that can be compacted to the point where it can bear the new surfacing without subsiding but without abrasion of tree roots and without raising the soil bulk density to the point where root growth cannot take place. Should it be necessary, this operation will be overseen by the project arboriculturist.

Supervision: Supervision will not be required.

Tree works: No tree works are required.

Tree planting: It is respectfully suggested that if additional tree planting is required then this should be secured through an appropriately worded planning condition.

Sequencing of works

Site clearance of a light nature
Main construction phase
Removal of all non-essential equipment
Landscaping hard and soft (if required)
Completion

Contacts

Architect and Agent:

Name:

Tel:

E:

Arboricultural Consultant:

Name: K Chesterman

Tel: 07375110399

E: info@allarboriculture.co.uk

Tree No	Species	Height (m)	Trunk Diameter (cm)	Crown spread (m)		Crown height above ground (m)	Life stage	General observations	BS 5837 cat	Root protection area (m)
1	Cherry <i>Prunus avium</i>	3	23	2	2	1	Early Mature	Previously reduced.	C	2.7
				2	2					
2	Ash <i>Fraxinus excelsior</i>	16	58	5	3	5	Early Mature	Side reduced to boundary. Off site tree.	C	6.9
				5	5					
3	Pear <i>Pyrus communis</i>	3	29	2	2	1	Early Mature	Co dominant. Previously reduced.	C	3.4
				2	2					
4	Apple <i>Malus domestica</i>	4	42	3	3	1	Early Mature	Previously reduced.	C	5.0
				3	3					
5	Apple <i>Malus domestica</i>	4	50	2	2	1	Early Mature	Previously reduced.	C	6.0
				2	2					

APPENDIX 1 - Tree Schedule Schedule

Survey Key

Diameter (mm)

Stem diameter in millimetres measured at 1.5m above ground level. Where the stem is divided below 1.5m, measurement is taken as directed by BS:5837 Annex C.

RPA - Root Protection Area

RPA circle radius is determined from Annex D of BS:5837. R- Radius

A – Area

Branch Spread (m)

Radial crown spread in metres, measured for each of the four cardinal points of the compass from the centre of the trunk.

N E
W S

Low branches

Height above ground in metres of the lowest branch and use of the 4 cardinal points of the compass.

Age class

(NP) Newly planted – a tree within 3 years after planting

(Y) Young – a tree within its first one third of life expectancy

(EM) Early Mature – a tree within its second third of life expectancy

(M) Mature – a tree in its final one third of life expectancy

(OM) Over Mature – a tree having reached its maximum life span and is declining in health and size due to old age

(V) Veteran – a tree in the second or mature stage of its life and has important wildlife and habitat features including; hollowing or associated decay fungi, holes, wounds and large dead branches.

(A) Ancient – a tree in the ancient or third and final stage of their life that is of interest biologically, aesthetically or culturally because of its age, size and condition

Physiological Condition

GOOD – a tree in a healthy condition with no significant problems

FAIR – a tree generally in good health with some problems that can be remediated POOR – a tree in poor health with significant problems that can't be remediated DEAD – a tree without sufficient live material to sustain life

Structural Condition

An assessment of the structural/safe condition of the tree categorised into:

GOOD – a tree in a safe condition with no significant defects

FAIR – a tree in a safe condition at present but with defects or with significant defects that can be remediated POOR – a tree with significant defects that can't be remediated.

EC - Estimated remaining contribution in years (based on the species and its current condition)

<10 Up to 10 years

10+ 10 years or more

20+ 20 years or more

40+ 40 years or more

Category (Tree quality assessment)

Category U – Tree in poor condition that cannot realistically be retained for longer than 10 years

Category A – Trees of high quality

Category B – Trees of moderate quality Category


C – Trees of low quality

APPENDIX 2 – Protective fencing


Protective fencing should be erected before any construction commences on site. It should also be in position to protect important trees prior to demolition.

Protective fencing should stay in position until all construction activity has finished.


‘Fencing should be established at the minimum distance set out in British Standard 5837:2012 *‘Trees in relation to design, demolition and construction - Recommendations’*. Excavations should not encroach into the fence position and it is appropriate to keep at least 0.5m between the fence and any changes in level.

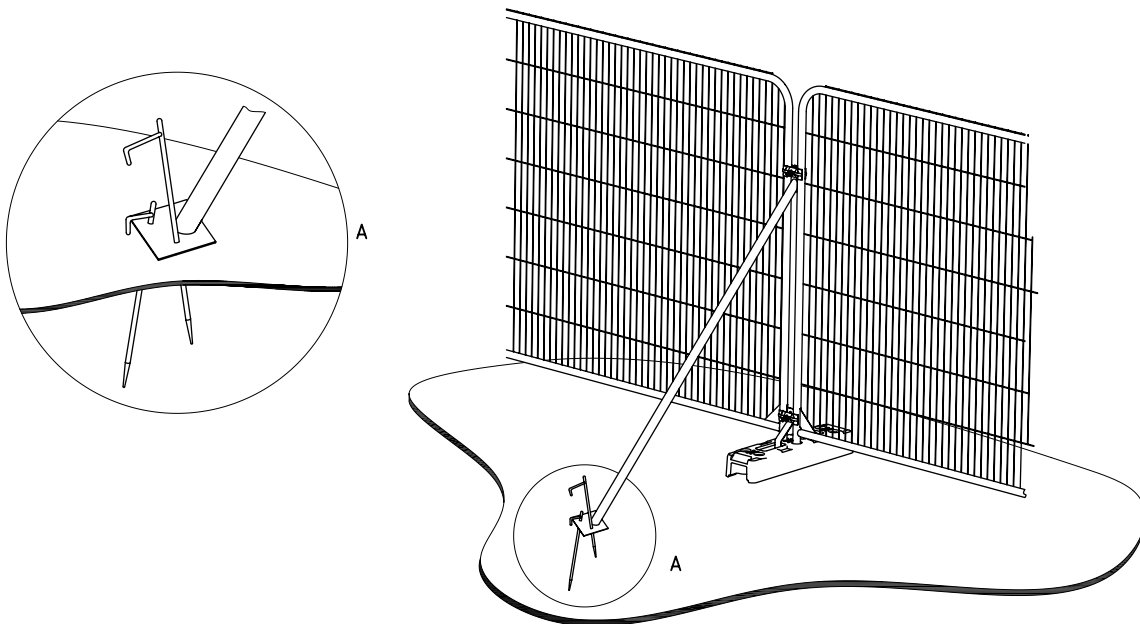

a) Stabilizer strut with base plate secured with ground pins

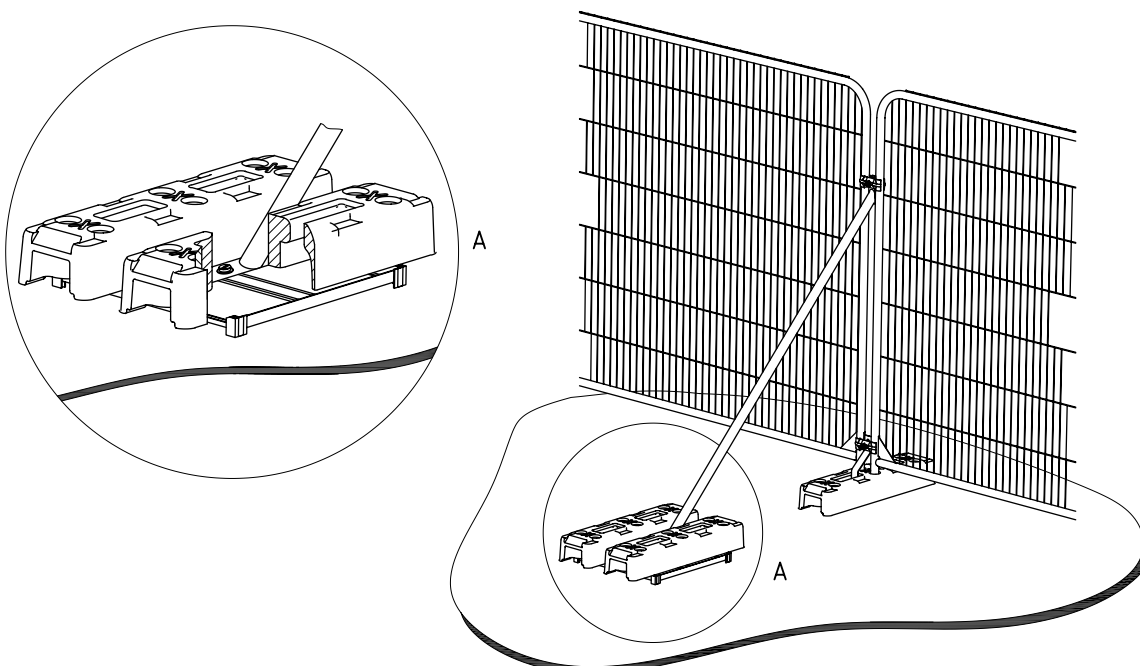

b) Stabilizer strut mounted on block tray



RPA for Cat A* tree

RPA for Cat B* tree

RPA for Cat C* tree

RPA for Cat U* tree

Tree Canopy

Heras Fencing

Ground Protection

All Arboriculture

23 Southernhay Avenue

Bristol

BS8 4TJ



ALLARBORICULTURE

Client:

Alex Smith

Consultant:

Kristian Chesterman

Site:

20 Rotherfield Avenue,
Wokingham, RG41 2EX

Title:

Tree Protection Plan

Scale at A3:

1:500

Date:

02/05/2024

Document Ref.

AATPP20RO
