

PHASE 2B OF THE SOUTH WOKINGHAM SDL PHASE 2B SANG, SOUTH WOKINGHAM

Landscape and Ecological Management Plan

August 2026 | P19-0052_06E

PEGASUS
GROUP





33 Sheep Street, Cirencester, GL7 1RQ
www.pegasusgroup.co.uk | T 01285 641717 | F 01285 642348

Prepared by Pegasus Landscape Design. Pegasus Landscape Design is part of Pegasus Planning Group Ltd
 Prepared in conjunction with Ecosa on behalf of Kier Ventures Ltd, Kingacre Estates Ltd and Miller Homes Limited.
 Date: August 2026
 Project code: P19-0052_06
 Contact: Pegasus Landscape Design – Alice Skinner

Copyright Pegasus Planning Group Ltd. © Crown copyright and database rights 2025 Ordnance Survey – Emapi License number 0100031673/AC0000808122. Promap License number 100020449/AC0000813445

First Issue	28/03/2019	ASK/TH
A	08/04/2019	ASK/TH – Amended to arboricultural comments
B	12/06/2020	NHA/TH – Plans updated
C	26/08/2020	NHA – Plans updated
D	16/10/2025	ASK
E	12/08/2026	ASK – updated to LPA comments

CONTENTS

1.0	Introduction	4			
	Introduction	4			
	Approach	5			
	Objective for the SANG	6			
	Ecological trends and constraints	6			
	Managing Risk and Competencies	6			
	Landscape Auditing	6			
	Replacement Planting	6			
2.0	Scheme description and objectives	9			
	Scheme and phasing description	9			
	Landscape summary	9			
	Ecology summary	10			
	Management objectives	10			
3.0	Environmental Considerations	12			
4.0	Maintenance Specification	14			
	4.1 General Management works	14			
	4.2 Retained Trees, Tree Groups and Woodland	14			
	4.3 Existing Hedgerow	15			
	4.4 Scattered Trees	16			
	4.5 Orchard	17			
	4.6 New Species Rich Native Hedgerow Planting	18			
	4.7 Other Woodland; Broadleaved	19			
	4.8 Mixed Scrub	20			
	4.9 Other Neutral Grassland and Purple Moor Grass and Rush Pastures	21			
	4.10 Introduced Shrub	22			
	4.11 Play Equipment	22			
	4.12 Ecological Enhancements to the Emm Brook	23			
	4.13 Hard landscape	24			
	4.14 Ecological Habitats	24			
	4.15 WBC SUDS Basins	25			
	Summary	25			
5.0	Schedule of Management and Maintenance	26			
	5.1 Establishment Years 0–5	26			
	5.2 Landscape Management Review	34			
6.0	Responsibilities	35			
	SANG Creation	35			
	Post–SANG Creation	35			
7.0	Appendices	36			
	Appendix 1	37			

1.0 INTRODUCTION

INTRODUCTION

- 1.1 Pegasus Planning Group were commissioned in 2020 by Kier Ventures Ltd and Miller Homes to produce a Landscape and Ecological Management Plan (LEMP) for the proposed Phase 2b Suitable Alternative Natural Greenspace (SANG) at Phase 2 of the South Wokingham Strategic Development Location.
- 1.2 The document reference P19-0052_06C was approved as part of the Hybrid Planning application 191068 in July 2024.
- 1.3 As part of the discharge of conditions for the Hybrid planning application condition 16 states:

“Prior to the commencement of each Phase of the development a Landscape and Ecological Management Plan (LEMP), including long term design objectives, management responsibilities, timescales and maintenance schedules for all landscape areas, other than privately owned, domestic gardens, shall be submitted to and approved in writing by the local planning authority. The Landscape and Ecological Management Plan shall be carried out as approved.

Reason: In order to ensure that provision is made for satisfactory maintenance of the landscaping hereby approved in accordance with Core Strategy policies CP1, CP3, CP7 & CP21; Managing Development Delivery Local Plan policies CCO3, TB21 & TB23; and the South Wokingham SDL SPD. Details are required before commencement because then need to be assessed in conjunction with the landscaping proposals.”

Condition 15 also states

“iii) No development shall take place in each phase of the development until details of quality control measures, including supervision of landscape contract(s) by a suitably qualified landscape specialist and annual landscape audits for the five-year period from completion of the landscaping for the Landscape Phase or until adoption (whichever is longer) have been submitted to and approved in writing

by the Local Planning Authority. The annual Landscape Audit shall be submitted to the Local Planning Authority for information prior to the next planting season and replacement planting undertaken in accordance with the landscape audit and iv) below.

iv) Any trees or plants which, within a period of five years after planting, are removed, die or become seriously damaged or defective, shall be replaced in the next planting season with others of species, size and number as originally approved and permanently retained.”

- 1.4 The original LEMP has therefore been updated to include the necessary points required within the conditions and any design evolution that has occurred in the time that has lapsed since the LEMP was written.
- 1.5 An overview of the SANG proposals are shown on page 8. The proposals have been designed in accordance with the objectives set out within this LEMP. Full details of the landscape proposals can be seen in Appendix 1.
- 1.6 A detailed soft landscaping specification has been produced and includes ground preparation, planting, seeding and 12-month after care. Refer to P19-0052_EN_063.

APPROACH

- 1.7 This LEMP should be read in conjunction with:
 - Detailed hard and soft Landscape Proposals P19-0052_EN_139
 - Landscape Specification P19-0052_EN_063
 - ECOSA (2026), Holme Park SANG, South Wokingham – Ecological Mitigation Strategy.
 - Woodland management Report PRI24132 by ACD Environmental
 - South Wokingham Distributor Road LEMP by Landpro dated July 2025

APPROACH

1.8 The aim of this LEMP is to:

- Outline the design of the proposed SANG and demonstrate it meets Natural England's SANG criteria;
- Provide management objectives to demonstrate that the SANG can be sustainably managed in perpetuity;
- Provide details on the status of current woodland and provide detailed management recommendations to ensure the woodland area continues to function as part of the SANG;
- Provide details on the status of the Emm Brook and provide detailed management recommendations to ensure the watercourse continues to function as part of the SANG;
- Provide details of the management recommendations to ensure successful establishment and continued function of proposed habitats including woodland, wetland, hedgerows and grassland; and
- To inform capital and revenue costs associated with the SANG.

1.9 Landscape and ecological objectives and their related management prescription are discussed within Section 2.0. These objectives have been derived from landscape surveys and an ecological surveys of the site (Carried out by ECOSA Ltd between 2013 and 2017).

1.10 Key features of existing and proposed value are;

- A proposed 2.68km circular walking route around the SANG with connections into the existing Public Right of Way (PRoW) network.
- The Emm Brook, which runs broadly from south-east to north-west across the site and provides an ecological corridor. The stream is a Habitat of Principal Importance in England (Priority Habitat) and a Wokingham Biodiversity Action Plan (BAP) Habitat;
- Existing Ancient Woodland, a Local Wildlife Site, close to Ludgrove School with further proposed woodland planting along the boundaries of the site and along the wetland corridor to provide a buffer and habitat enhancement. This is a Priority Habitat and Wokingham BAP Habitat;
- These existing landscape features, together with the proposed tree, shrub and grassland planting create a diverse environment that has visual amenity value for visitors and ecological benefits.

- Existing and proposed hedgerow planting which will provide an ecological network that provides connection within the site and beyond to the existing landscape framework. These features are a Priority Habitat;
- A series of meadows created by a variety of grassland types including wetland meadow grass, flowering lawns and wildflower meadow, which is a Priority Habitat and Wokingham BAP Habitat;
- The proposed wetland corridor creates a focal point within the southern half of the site whilst the Local Landscape Area for Play (LLAP) creates a focal point within the northern half of the site;
- The LLAP provides play and informal recreation opportunities for children visiting the site;
- Dog proof fencing and dog beaches encourages owners to exercise their dogs within the SANG, reducing pressure on the Thames Basin Heaths SPA.

1.11 This LEMP provides management actions for the pre-creation and creation phase of the GI within the Phase 2b SANG development and for a five-year period following completion of construction. After the initial five year period the LEMP would be reviewed and updated in agreement with Wokingham Borough Council.

1.12 A monitoring scheme would also be carried out during the pre-creation, creation and post-creation of the proposed green infrastructure development. This monitoring scheme would inform the on-going informal review of this LEMP.

1.13 Responsibilities for the delivery of management actions has also been discussed within Section 7.0.

OBJECTIVE FOR THE SANG

- 1.14 The broad objective for the SANG is to provide mitigation for the potential impact of residential development within the Thames Basin Heaths planning zones on the Thames Basin Heaths Special Protection Area (SPA). The provision of a suitable alternative natural greenspace is intended to prevent an increase in visitor pressure on the SPA from the additional households provided within the Phase 2 of the South Wokingham SDL.

ECOLOGICAL TRENDS AND CONSTRAINTS

- 1.15 This LEMP is to be seen as an operational guide subject to review to incorporate landscape and ecological trends that may impact on the landscape management aims, objectives and maintenance regime. The review process would also allow future constraints such as Natural England licenses, working method and conservation targets to be included as the LEMP evolves. Changes to management practice for ecological trends for habitat and species which may be updated to local policy and biodiversity targets would be incorporated as necessary. This would help to ensure that the LEMP remains fit for purpose in the evolving dynamic of landscape and help to ensure resilience to the effects of climate change and social pressure.

MANAGING RISK AND COMPETENCIES

- 1.16 It is assumed that a competent contractor shall have the necessary PPE, training and skills to undertake the management and maintenance tasks as set out within this LEMP.
- 1.17 The landscape management company shall be responsible to undertake a written risk assessment in relation to the landscape, arboricultural and ecological management and maintenance prescriptions detailed within this LEMP (in additional to any other site risks). This shall be provided to the clients prior to the start of works.

LANDSCAPE AUDITING

- 1.18 For the first years following completing or until adoption (whichever is longer) a landscaping audit shall be carried out annually by a suitably qualified Landscape Architect and will include details of the condition of landscaping features within the scheme. The audit will also note any works required to rectify defaults or known issues that require on-going monitoring prior to the next annual report. The report will be made available to the Local Planning Authority

REPLACEMENT PLANTING


- 1.19 Any trees or plants which, within a period of five years after planting, are removed, die or become seriously damaged or defective, shall be replaced in the next planting season with others of species, size and number as originally approved and permanently retained.
- 1.20 If a particular species develops a disease or known issue and requires replacement, a suitable alternative will be selected and approved with the local planning authority.

SANG PHASING

- 1.21 The SANG is to be delivered over five phases (as shown on the plan overleaf). A summary of the landscape and ecological features within each phase has been included below. When moving on to a new phase the maintenance works for the previous phase(s) will continue as required.

MAINTENANCE SPECIFICATION (refer to section 4.0)	PHASE				
	1	2	3	4	5
General Management Works	X	X	X	X	X
Retained trees, tree groups and woodland	X	X	X	X	
Existing Hedgerow					
Scattered Trees	X	X		X	
Orchard				X	
Species rich hedgerows	X	X		X	
Other woodland;broadleaved	X	X	X	X	
Mixed scrub	X	X			
Grassland and Purple Moor Grass	X	X	X	X	
Introduced shrub				X	
Play Equipment				X	
Ecological Enhancements to the Emm Brook		X			
Hard Landscape	X	X			X
Ecological Habitats	X	X	X	X	

FIGURE 1: SANG Phasing Plan

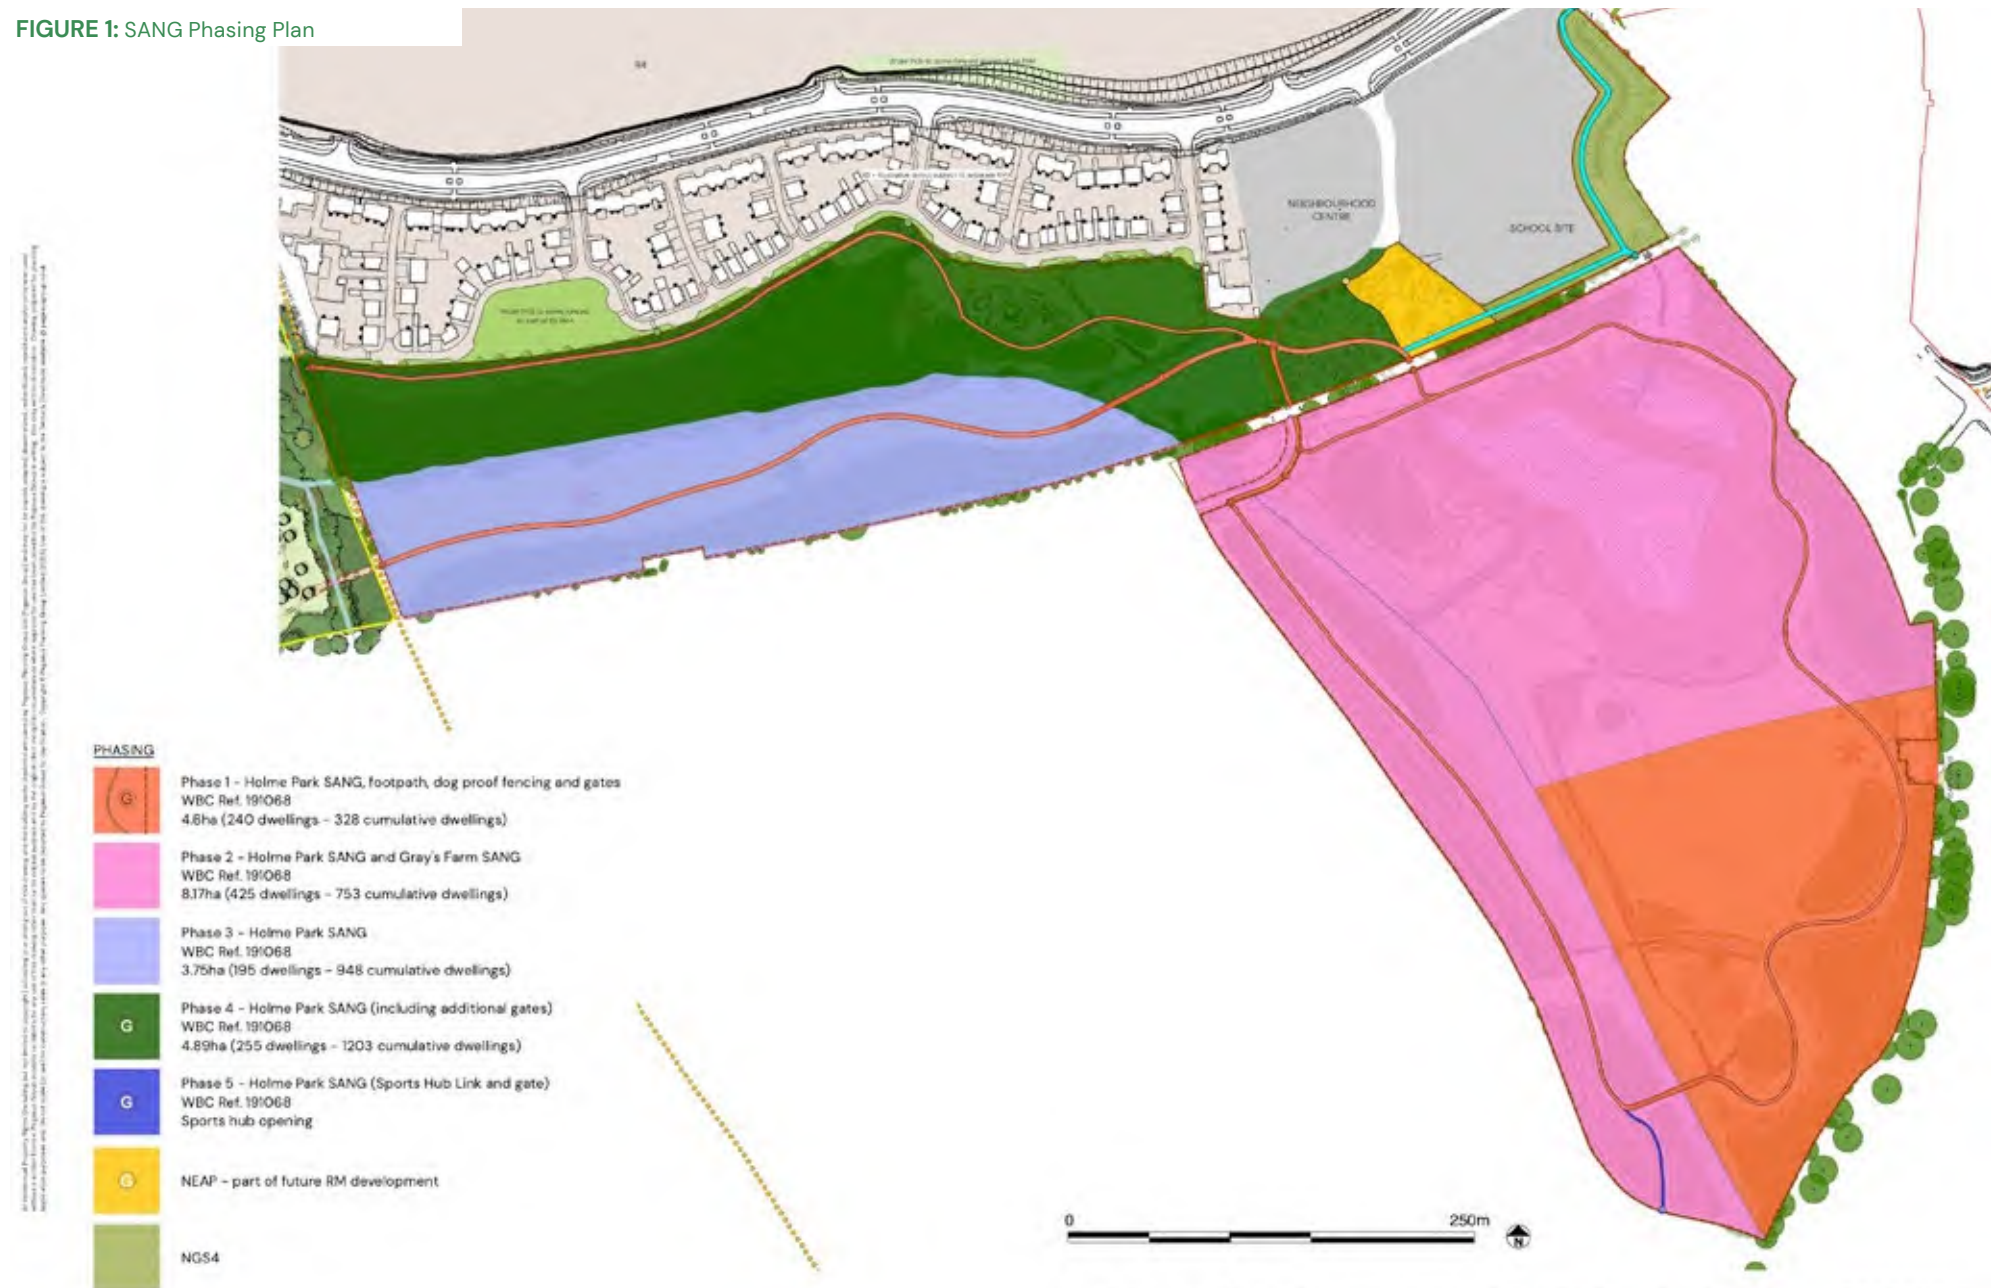

2.0 SCHEME DESCRIPTION AND OBJECTIVES

SCHEME AND PHASING DESCRIPTION

- 2.1 The proposed SANG comprises the following, refer to Figure 2: Holme park SANG General Arrangement
- Open space for informal recreation including a 2.54km circular walking route with additional secondary footpaths;
 - Woodland planting, including the retention of existing ancient woodland near Ludgrove School;
 - Native tree, shrub and hedgerow planting;
 - A mosaic of grasslands including wildflower meadow, wetland meadow grassland and areas of flowering lawn with wildflower plugs and bulb planting to create high floristic value;
 - Wetland corridor along a series of detention basins and swales that contribute to the wider SuDS strategy of Phase 2b of the South Wokingham SDL;
 - Emm Brook corridor with wetland meadow grass and footbridges to allow for access across the watercourse;
 - Primary access from the Strategic Development Road (SDR), with additional access points from Public Right of Ways (PRoW) and into the neighbouring sports hub;
 - A temporary car park to provide 8 spaces off Heathlands Road; and
 - Local Landscape Area for Play (LLAP).
- 2.2 Time-scales for the creation of the SANG are anticipated to be from 2025 to 2026. Changes to this time-scale would be revised within the LEMP and agreed with Wokingham Borough Council.

LANDSCAPE SUMMARY

Site Description

- 2.3 The proposed 24.71 hectares Phase 2b SANG site will be located within existing agricultural fields broadly to west of East Hampstead Road. The site is divided into two areas by the access road to Ludgrove School.
- 2.4 The space to the north of the access road is predominantly occupied by a pastoral field and an area of woodland, some of which is classified as Ancient Woodland, and forms part of the 'Woodland near Ludgrove School' Local Wildlife Site. There is also an area of game pens to the east of this northern section of the SANG.
- 2.5 The northern boundary will run adjacent to the proposed residential area in the west and the local centre and primary school in the east that form part of the wider Phase 2b of the South Wokingham SDL development.
- 2.6 The north-western boundary follows the existing field boundary that is adjacent to the Public Right of Way WOKW FP10.
- 2.7 The space to the south of the access road is predominantly occupied by agricultural fields containing game pens.
- 2.8 The eastern boundary abuts the existing residential properties along Easthampstead Road and extends south to run along Heathlands Road. Whilst the western boundary is currently partially undefined as it runs through an agricultural field.

ECOLOGY SUMMARY

Habitats

- 2.9 An area of woodland (Semi-natural alder and drier oak/hazel woodland) within the site is classified as Ancient Woodland in addition to being a Local Wildlife Site (Woodland north of Ludgrove School). Beyond the area of woodland, the site is predominantly formed of arable or grassland ley with hedgerows, tree belts, scattered trees and the Emm Brook and tributaries.

Species

- 2.10 The following notable and protected species are considered likely to be making use of habitats currently present within the Phase 2b SANG
- Bats (common pipistrelle *Pipistrellus pipistrellus*, soprano pipistrelle *Pipistrellus pygmaeus*, Nathusius' pipistrelle *Pipistrellus nathusii*, long-eared bat *Plecotus* species, Myotis species, serotine *Eptesicus serotinus*, barbastelle *Barbastella barbastellus*, Leisler's bat *Nyctalus leisleri* and noctule *Nyctalus noctula*);
 - Badger *Meles meles*;
 - European hedgehog *Erinaceus europaeus*;
 - Birds (all species of which are protected while nesting);
 - Reptiles (slow-worm *Anguis fragilis*, grass snake *Natrix natrix* and common lizard *Zootoca vivipara*);
 - Amphibians (including common toad *Bufo bufo*)

MANAGEMENT OBJECTIVES

Landscape Objectives

- 2.11 Existing Vegetation

The existing vegetation comprises grassland enclosed by hedgerows, tree belts along the access road to Ludgrove School, trees along the Emm Brook and an area of woodland.

The principal hedgerow species include; Blackthorn (*Prunus spinosa*), Hawthorn (*Crataegus monogyna*) and other mixed native species.

The principal tree species include; Alder (*Alnus glutinosa*), Ash (*Fraxinus*

excelsior), Field Maple (*Acer campestre*), Hawthorn (*Crataegus monogyna*), Oak (*Quercus robur*), Wild service-tree (*Sorbus torminalis*) and Willow (*Salix* species).

It is proposed to retain and manage the existing vegetation structure with the following objectives:

1. To protect and maintain the existing area of ancient woodland to ensure its long term visual amenity and ecological benefit;
2. To retain vegetation along the Emm Brook where appropriate to maintain this ecological corridor;

It is proposed to remove the existing Himalayan Balsam with the following objectives:

3. To remove existing Himalayan Balsam from the Emm Brook through annual pulling by hand.
4. To annually monitor the Emm Brook for presence of Himalayan Balsam.

New Planting

- 2.12 To enhance the landscape character of the GI, the following objectives are proposed:

5. To create new areas of woodland planting along the site boundaries to enhance the sense of enclosure within the site. Further pockets of woodland within the site would provide additional habitat opportunities;
6. To create and maintain a wetland corridor that contributes to the SuDS management on site in addition to creating a feature within the landscape and providing ecological interest;
7. To create an area of orchard tree planting to provide opportunities for communal growing and create seasonal interest through blossom and fruit;
8. To create a diverse environment through the use of a range of native shrub and tree planting. Species, suitable for their context within the site, would provide structure and an

element of screening to create a sense of discovery; and

9. To enhance areas of existing grassland by creating a rich mosaic of grassland habitats including wildflower meadow, wetland meadow and flowering lawn. Cultivation and/or management methods will be used to provide ecological and visual interest;

Hardworks

2.13 The following objectives are proposed for the on site hardworks:

10. To create a series of pathways, pedestrian and maintenance gates, footbridges and appropriate fencing that integrates and enhances with the character of the site; and
11. To deliver hardworks in the form of benches, signage, play equipment and public art.

Ecology Objectives

2.14 The following ecological objectives are proposed:

1. To incorporate high value habitats including a variety of grasslands, wetland vegetation, species rich hedgerows, woodland and wooded boundaries. Species are to be native or wildlife friendly species wherever possible. Species within 8m of the Emm Brook are to be native only. ;
2. To establish green corridors across the site, comprising of tree lines and hedgerows with wide margins where vegetation can be left more unmanaged;
3. To design and manage SuDS sympathetically to wildlife with native marginal and emergence species planted where possible to provide enhancement for potential colonisation by great crested newts;
4. To establish areas of wildflower and wetland grassland within the site, with minimal management (wildflower and wetland grasslands are to be managed through annual/biannual hay cuts. Management should always respond to the location and should not prevent access and/or safe use of the space where required or appropriate) to provide enhancement for reptiles and amphibians; and
5. To provide areas of scrub within the site to create nesting

opportunities for a range of birds. Flowering species should be chosen within the scrub mix to provide nectar and seed resource for insects, birds and mammals. The threshold between the grassland and scrub aim to create refuge for small mammals and nesting opportunities for ground nesting birds.

6. To provide bird and bat boxes as well as hibernacula for reptile and amphibians.

3.0 ENVIRONMENTAL CONSIDERATIONS

Horticultural Peat

- 3.1 Horticultural peat is not to be used as mulch on any planting areas or as a soil conditioner, and wherever possible plants grown without peat will be preferred to those grown using peat.

Recycled Materials

- 3.2 Where appropriate, use should be made of materials made from recycled components, eg wood chip mulch.

Pesticides/Herbicides

- 3.3 Weed control of transplant areas is to be achieved by using mulch mats and hand weeding. The control of invasive and pernicious weeds can be carried out with targeted applications of glyphosate based herbicides.

Water Management

- 3.4 Where necessary, maintenance staff are to water plants at appropriate times of the day to ensure minimum water evaporation. It is anticipated that watering will only be necessary during the establishment period.

Habitat Management

- 3.5 Opportunities for the creation of additional micro-habitats and habitat enhancement should be taken wherever possible. Where appropriate habitat creation could include working with the Wildlife Trust and local wildlife groups to create log/habitat piles.
- 3.6 Allow deadwood, jagged stumps, splits, fungal growths/fruiting bodies and holes in tree trunks to remain unless they are creating a safety hazard.
- 3.7 Trees should not be felled unless they are classified as dangerous. Where a tree poses as a health and safety hazard, advice shall be sought immediately from an arborist. Ivy should only be severed where it is growing into tree canopies and is likely to create a fall hazard.
- 3.8 The retention, as far as possible, of the existing vegetation is considered an important part of the development. Such areas will be managed appropriately to maintain and develop their value.

General Maintenance

- 3.9 Maintenance operations are to be carried out with regard to BS 4428: Code of Practice for General Landscape Operations. Maintenance of soft landscaping (other than amenity turf) to have regard to BS 7370-4: Grounds Maintenance. Recommendations for Maintenance of Soft Landscape.

Tree Works

- 3.10 No pruning works to trees, hedgerows or structural planting are to be undertaken during the general bird nesting season of 1st March to 31st August inclusive. Works outside of this time period should be subject to checks by an ecologist to ensure there are no nesting birds present.
- 3.11 All tree surgery work is to be carried out to BS 3998:2010 Tree Work–Recommendations, and should be undertaken by a suitably qualified operative. Any trees with bat potential to be inspected by a qualified bat specialist prior to any tree works commencing.
- 3.12 Hygiene works will be avoided, for example fungal fruiting bodies should not be removed nor trees felled because they have bracket fungi on them unless classified as dangerous by an arborist. Where possible, trees will be allowed to age naturally and dying trees will be allowed to decay in-situ. Where a tree poses a health and safety hazard, advice will be sought from an arboriculturist.

Watering

- 3.13 Care should be taken not to over-water plants. Until well established all shrubs/trees are to be watered during the growing season. Following any dry periods of 7–10 days soil water content should be assessed and watering undertaken as necessary. Planting areas are to be brought up to field capacity at each visit and each tree is to receive 40 litres or as required. If trees are showing signs of drought stress the watering regime should be reviewed and increase as required. Care should be taken to ensure applied water is absorbed into the root-zone and does not run off the surface.

Failure to Thrive

- 3.14 Any shrubs, hedges or trees which fail to thrive in the first five years shall be replaced with the same species and variety at the size specified on the original landscape planting plan. Trees and shrubs should be checked in September and marked with paint, or noted on a plan, as necessary. Replacements will be planted during the following planting season. No substitutes will be planted without written approval from the local planning authority.
- 3.15 If a particular species fails to establish successfully then an alternative, comparable species should be considered as replacement, in agreement with the landscape consultant. Replacement planting of container plants to be undertaken as required, root-ball/bare root planting to be undertaken November to March. Planting of new trees to have regard to Section 10 of BS 8545:2014 Trees: from nursery to independence in the landscape. All plants to conform to BS 3936 and be in accordance with the National Plant Specification.

Litter and Arisings

- 3.16 Litter and debris shall be cleared by hand from all open space areas and removed from site on a monthly basis, and prior to mowing amenity grassland, tussocky grassland, wildflower meadow, wildflower meadow for shade, damp grassland and retained lowland meadow. Arisings from tree works are to remain on site and be used to create habitat piles in areas of the SANG with longer grass or close the shrub and woodland planting. An ecologist should review locations as part of their annual walk over to ensure habitat is suitable for reptiles and invertebrates.
- 3.17 All other green arisings from landscape works will be removed from site and disposed of at a registered facility, recycling or composting of arisings should be prioritised.

Weed Management

- 3.18 A minimum intervention approach will be used in terms of weed control. In areas of transplant tree/shrub or ornamental shrub planting this is to be achieved by using mulch mats and hand-weeding. Weed killer and other chemicals will be used as little as possible on site and limited to hard surfaces where possible. Spot removal of weeds will be carried out by hand removal as necessary. Where mulch is used around plants, this is to be kept topped up to 75mm to minimise weed growth.

4.0 MAINTENANCE SPECIFICATION

4.1 GENERAL MANAGEMENT WORKS

Site supervision by a landscape architect would be undertaken to monitor the following:

- Setting out of planting areas;
- Tree pit excavations;
- Delivery and storage of trees and shrubs;
- Tree and shrub planting; and
- Stock protection.

Ecological Clerk of Works

An Ecological Clerk of Works (ECoW) would be appointed to oversee all ecological matters during creation. An Ecological Tool Box Talk would be provided to contractors at the start of on site works by the ECoW. The talk would identify all ecological site management issues, particularly specific management measures for reptiles, amphibians, bats and nesting birds. In conjunction with the landscape architect, the ECoW would review the planting proposals and supervise planting as required

Himalayan Balsam

Himalayan Balsam is to be pulled by hand before seed pods have developed to prevent further spread. This should take place fortnightly during May and June to allow the plants to be tall enough to be spotted amongst other vegetation, but prior to seed pods developing. Plants are not to be pulled if seed pods are present. Removal is likely required for at least 2–3 years until the seed bank has been exhausted. The riverbank should be monitored in late spring (April–May) annually for presence of any growth and removal should continue until all Himalayan Balsam plants are removed.

Himalayan balsam are listed on Schedule 9 of the Wildlife and Countryside Act 1981 (as amended). This makes it illegal to plant or otherwise cause the species to grow in the wild. It is also classed as a 'controlled waste' under the Environmental Protection Act 1990 (EPA). As such it must be removed by a suitably qualified professional and disposed of safely at a licensed landfill site according to the EPA (Duty of Care) Regulations 1991.

4.2 RETAINED TREES, TREE GROUPS AND WOODLAND

Areas and landscape elements included

Refer to ACD Arboricultural Impact Assessment for full location and schedule of retained trees and woodland on site ref: ACD Tree Protection Plan PRI24132–03

Management Aim

- To prolong the life and enhance the aesthetic and wildlife value of the existing trees and woodland across the site and along the site's boundaries

Management Objectives

- To maintain the health and visual amenity of the retained trees, tree groups and woodland;
- To enhance their ecological/ biodiversity value; and
- To maintain the varied age and structure of the trees.

A detailed condition survey of all trees will be carried out by a qualified arborist at least once every two years. Any necessary remedial works will be carried out as soon as possible.

There will be no regular pruning of trees to retain at least 75% of the expected canopy for their age range and height.

Note: deadwood resulting from tree management works will be used on the site to create wood piles as and when required following the completion of the public open space areas. The wood at the bottom of the pile is to be set 1/3rd into the ground. Piles are not to be located in areas of green space with high public usage.

An arboricultural contractor will be employed under the supervision of the ecologist to undertake the initial woodland management works as follows:

- The ecologist will brief the arboricultural contractor prior to any works commencing;
- The setting out and construction of all footpath routes directly adjacent to areas of existing woodland must be carried out under the supervision of an arborist and will comply with the requirements of the appropriate British Standard (BS 5837:2012);

- Vegetation will be removed with due diligence for all wildlife and ecological requirements and should be undertaken outside of the bird nesting season (March to August inclusive). Works outside of this time period will be subject to checks by an Ecologist to ensure there are no nesting birds present;
- All vegetation planned for removal in accordance with the woodland management plan will be subject to further surveys by an arboriculturist in conjunction with an ecologist and clearly marked out on-site;
- Habitat enhancement works such as the creation of log piles and hibernacula will be created.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.3 EXISTING HEDGEROW

Areas and landscape elements included

Refer to ACD Arboricultural Impact Assessment for full location and schedule of retained trees on site ref: ACD Tree Protection Plan PRI24132-O3

Management Aim

- To strengthen the commuting routes for wildlife to provide enhanced foraging, resting and nesting habitats for birds, bats, reptiles and invertebrates.

Management Objectives

- To maintain the health and visual amenity of the retained hedgerow;
- To maintain dense, bushy, continuous hedge lines with a good species mix and no gaps;
- To enhance the ecological and biodiversity value of the existing hedgerow;
- To take care due care during maintenance operations near existing hedgerow; and
- To maintain a varied structure of hedgerow through rotational cutting.

Hedgerows shall be cut on a 3 year rotation as the abundance of berries increases from one year to two years after cutting and then slowly declines, cutting annually reduces the availability of food for wildlife.

Existing hedgerows are to be maintained at a minimum height of 1.5m and minimum width of 1.5m.

1/3 of the retained hedgerows shall be trimmed per year, leaving the remaining 2/3 untrimmed, this will prevent encroachment into open space whilst promoting growth of fruiting plants. The untrimmed growth of the hedgerows will allow wildlife to migrate and re-colonise before the next trim, and also allow development of mature fruiting stems.

Any gaps in hedgerows on the site are to be in-filled using native species as soon as identified to prevent short-cuts developing. These will be planted as tall whips and will comprise a similar native species mix to those present within the hedgerow. To ensure that the plants establish new planting will be protected from trampling with appropriate guards and fencing until they are well established.

A 1m width of grassland is to be maintained unmown on either side of the hedge (where practical and at least to one side where it is not practical on both sides) Natural regeneration of herbaceous species is to be encouraged. Areas of bare ground should be sown with a semi-shade tolerant grassland mix to be approved by the project ecologist.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.4 SCATTERED TREES

Areas and Landscape Elements Included

Individual trees located within the SANG as shown on P19-0052_EN_139

Management Aim

- To successfully establish new tree planting;
- To maintain new tree planting to establish a diverse treed environment with a high quality visual appearance; and
- To provide enhanced opportunities for foraging and sheltering for a range of wildlife including birds, bats and invertebrates.

Management Objectives

- To maintain newly planted trees to ensure good survival rate and development;
- To minimise competition from grass and weeds around newly planted trees;
- To maintain appropriate form of trees for future growth; and
- To ensure trees do not present a hazard to site users;

Any necessary remedial works will be carried out as soon as possible. All tree work should be carried out in accordance with BS 3998 (2010) (or any subsequent updates).

Tree stakes and ties will be regularly checked during the establishment period and adjusted as necessary to ensure that the developing trees are not damaged. Stakes and ties will be removed from site (to a legal disposal facility) by the landscape maintenance contractor at the earliest opportunity (between year 3 and year 5) when it is considered that the trees are self supporting.

There will be a minimal pruning policy for trees as pruning wounds can provide a source of infection. Formative pruning of new trees will be carried out to remove dead and diseased wood and to create a well balanced tree with a single leader.

If trees die the reason for death shall be investigated and addressed before replanting a replacement. If death is due to the planting conditions these shall be ameliorated. If death is due to pests or disease and likely to be present in the future a resistant species of an alternative similar native tree shall be selected.

Where trees have become moribund due to compaction or lack of nutrients then soil aeration techniques and/or the use of inoculants shall be considered.

During the first two to three years, all trees are to be watered weekly (it is recommended newly planted trees are given 50 litres of water per week) from May to the end of September unless unnecessary due to heavy rain. Ideally watering should be carried out in the early morning or evening. Trees should be visually monitored for signs of water stress from year 3 onwards and action taken if required. If the water supply is likely to be restricted, e.g. due to emergency drought legislation, obtain instructions on watering.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.5 ORCHARD

Areas and Landscape Elements Included

Proposed fruiting trees within the orchard area of the SANG as shown on P19-0052_EN_139

Management Aim

- To successfully establish new orchard tree planting;
- To provide opportunities for residents and community groups to be able to pick fruit from orchard trees.

Management Objectives

- To ensure orchard trees are maintained to promote annual fruit cropping opportunities for residents and community groups;
- To minimise competition from grass and weeds around newly planted trees;
- To maintain appropriate form of trees for future growth; and
- To ensure trees do not present a hazard to site users.

Any necessary remedial works will be carried out as soon as possible. All tree work should be carried out in accordance with BS 3998 (2010) (or any subsequent updates).

Tree stakes and ties will be regularly checked during the establishment period and adjusted as necessary to ensure that the developing trees are not damaged. Stakes and ties will be removed from site (to a legal disposal facility) by the landscape maintenance contractor at the earliest opportunity (between year 3 and year 5) when it is considered that the trees are self supporting.

Orchard Tree planting should be carried out in line with Natural England guidance (Traditional Orchards; formative pruning of young trees (TIN016))

Signage should be provided close to orchard trees to inform residents and community groups of species, origins, cropping seasons and providing tasting or use notes. There should also be seasonal signs to inform residents, community groups and allotment users when fruit can be picked.

Pruning of trees will ensure continued fruit production and ensure trees retain at least 75% of the expected canopy for their age range and height.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.6 NEW SPECIES RICH NATIVE HEDGEROW PLANTING (WITH AND WITHOUT TREES)

Areas and landscape elements included

Proposed species rich native hedgerow planting with and without trees located within the SANG as shown on P19-0052_EN_139

Management Aim

- To assist the establishment of new native species rich hedgerow and native species rich hedgerow with trees to enhance and create green corridors throughout the site.
- To strengthen the commuting routes for wildlife and provide enhanced foraging, resting and nesting habitats for birds, bats, reptiles and invertebrates

Management Objectives

- To help establish and maintain a dense continuous hedge line with no gaps;
- To maintain the health, visual amenity and species diversity of the proposed native hedgerow; and
- To take due care during maintenance operations near new hedgerows.

New hedgerows will be planted such that there is a minimum of 5 native woody species in every 30 meters of hedgerow.

Hedgerow cutting will take place between November and January inclusive, outside of the bird nesting season, unless works are essential for public safety.

Hedgerow plants will be trimmed to create a healthy solid hedge. The frequency of cutting will depend upon growth rates and weather conditions; the requirement for cutting will therefore be assessed annually.

Hedgerow planting will be maintained by weeding, pest & disease control and appropriate guards and fencing until it is well established.

From year 4 the proposed native hedgerow will be pruned/shaped as part of a rotational management regime whereby hedgerows are cut on a 3 year rotation to allow for an abundance of berries from one to two years after cutting

Hedgerows will be maintained at a minimum height of 1.5m and a minimum width of 1.5m.

1/3 of the hedgerows shall be trimmed per year, leaving the remaining 2/3 untrimmed. This will prevent encroachment into the open space whilst promoting growth of fruiting plants.

Any gaps in hedgerows on site are to be in-filled using like-for-like species as soon as identified to prevent short-cuts developing.

A 1m width of grassland is to be maintained unmown on either side of the hedge (where practical and at least to one side where it is not practical on both sides) Natural regeneration of herbaceous species is to be encouraged. Areas of bare ground should be sown with a semi-shade tolerant grassland mix to be approved by the project ecologist.

Trees planted within hedgerows should be managed according to the management prescriptions set out for trees under section 5.3 scattered trees

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.7 OTHER WOODLAND; BROADLEAVED

Areas and landscape elements included

Proposed woodland within the SANG as shown on P19-0052_EN_139

Management Aim

- To assist the establishment of woodland habitat through the provision of woodland trees and shrubs.

Management Objectives

- To establish and maintain a two storey area of woodland planting with a mix of native trees and shrubs.
- To maintain ground cover of semi-shade tolerant grassland with areas of open space within the woodland
- To allow natural regeneration of the woodland over time to create a diverse wood

No rhododendron or laurel to be present and any other invasive species would be less than 10% of overall coverage within the woodland.

Woodland is to be maintained to have five or more native trees or shrub species across the area of woodland.

Natural regeneration is allowed to occur within the woodland with a minimum of two storeys of vegetation across the area of woodland should be maintained at all times.

Note: deadwood resulting from tree management works will be used on the site to create wood piles as and when required following the completion of the public open space areas. The wood at the bottom of the pile is to be set 1/3rd into the ground. Piles are not to be located in areas of green space with high public usage.

Report any evidence of excessive or inappropriate use of the woodland so measure to deter access can be reviewed to ensure an appropriate level of disturbance is maintained throughout the woodland area.

Tree Canopy Level Maintenance

Any necessary remedial works will be carried out as soon as possible. All tree work should be carried out in accordance with BS 3998 (2010) (or any subsequent updates).

Tree stakes and ties will be regularly checked during the establishment period and adjusted as necessary to ensure that the developing trees are not damaged. Stakes and ties will be removed from site (to a legal disposal facility) by the landscape maintenance contractor at the earliest opportunity (between year 3 and year 5) when it is considered that the trees are self supporting.

There will be a minimal pruning policy for trees as pruning wounds can provide a source of infection. If trees die the reason for death shall be investigated and addressed before replanting a replacement. If death is due to the planting conditions these shall be ameliorated. If death is due to pests or disease and likely to be present in the future a resistant species of an alternative similar native tree shall be selected.

Where trees have become moribund due to compaction or lack of nutrients then soil aeration techniques and/or the use of inoculants shall be considered.

Care should be taken not to over-water trees. Until well established trees are to be watered during the growing season following any dry periods of 7 days. Watering is unlikely to be required after year one of the management plan, but trees should be visually monitored for signs of water stress from year 2 onwards and action taken if required.

Understorey Shrub Maintenance

Shrubs should be allowed to grow dense where it does not encroach on grassland or amenity areas.

Undesirable plant growth within the woodland planting, such as scrub, dock, thistle, nettles and ragwort, should be controlled by strimming undertaken in the winter months, to avoid the bird nesting season. Trimmer guards must be in place on trimmers to prevent damage to bark of young trees and shrubs. Care must be taken to control sweeping motions to maintain a suitable distance away from tree and shrub planting. Any undesirable encroaching vegetation in close proximity to newly planted shrubs shall be removed by hand picking/weeding, undertaken in the winter months to avoid bird nesting season.

Semi-Shade Tolerant Grassland Maintenance

Mowing regimes for all grasslands can be found in 5.1.6.

Arisings shall be swept from hard surfaces adjacent grass/wildflower areas after each maintenance visit.

Junctions between grass/wildflower areas and plant beds/hard surfaces shall be regularly edged and trimmed to maintain a neat and tidy appearance. In order to avoid damage to trees no mower or strimmer will be allowed within 400mm of a tree trunk.

Areas of greater than 5% failed grass shall be prepared and re-sown with the specified seed mix either in April or September. **No fertiliser or grass growth regulator will be permitted on these grassland mixes.**

Litter shall be hand picked and bagged from all grass areas prior to cutting. Bags shall be removed from site and legally disposed of.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.8 MIXED SCRUB

Areas and landscape elements included

Proposed mixed scrub including defensible shrub within the SUDs and native scrub planting – wet and woodland edge planting within the SANG as shown on P19-0052_EN_139

Management Aim

- To establish new areas of mixed scrub planting

Management Objectives

- To maintain newly planted scrub to ensure successful establishment; and
- To minimise competition from grass and weeds from around newly planted scrub.

Mixed scrub is to be maintained to have a minimum of three wood species with no one species comprising more than 75% of the cover. There is to be an absence of invasive non-native species (includes species listed on Schedule 9 of the Wildlife and Country Act) and species indicative of sub-optimal condition make up less than 5% of the ground cover.

Undesirable plant growth within the sward, such as scrub, dock, thistle, nettles and ragwort, should be controlled by strimming undertaken in the winter months, to avoid the bird nesting season. Trimmer guards must be in place on trimmers to prevent damage to bark of young trees and shrubs. Care must be taken to control sweeping motions to maintain a suitable distance away from tree and shrub planting. Any undesirable encroaching vegetation in close proximity to newly planted shrubs shall be removed by hand picking/weeding, undertaken in the winter months to avoid bird nesting season.

Where possible (in line with maintained edges required to hard standing – see grassland maintenance within 5.9 and 5.10) a 1m edge of tall grassland should be maintained to the edge of proposed native shrub planting to help a well-developed edge and provide an ecological transition between habitat areas.

Shrubs should be allowed to grow dense where it does not encroach on grassland or amenity areas.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.9 OTHER NEUTRAL GRASSLAND AND PURPLE MOOR GRASS AND RUSH PASTURES

Areas and landscape elements included

Proposed other neutral grassland habitat includes Long Mown Grassland, Wildflower Meadow Mix, Wetland meadow grassland and Flowering Lawn within the SANG as shown on P19-0052_EN_139

Management Aim

- For grassed areas to present and maintain high quality visual appearance.

Management Objectives

- To ensure grassland areas successfully establish;
- To keep grass areas free from weeds, litter and rubbish; and
- To maintain grass areas in good condition that is reflective of the character they are within.

Mowing regimes for all grasslands can be found in 5.1.6.

Arising shall be swept from hard surfaces adjacent grass/wildflower areas after each maintenance visit.

Junctions between grass/wildflower areas and plant beds/hard surfaces shall be regularly edged and trimmed to maintain a neat and tidy appearance. In order to avoid damage to trees no mower or strimmer will be allowed within 400mm of a tree trunk.

Areas of greater than 5% failed grass shall be prepared and re-sown with the specified seed mix either in April or September. No fertiliser or grass growth regulator will be permitted on these grassland mixes.

A 1m maintenance strip adjacent to areas of hard standing is to be regular mown to a height of 15cm to minimise encroachment onto hard standing and provide cues to care within all areas of the public open space.

Flowering lawn is to be maintained through regular mowing. Mowing can be relaxed during June and July to allow flowering only in areas away from maintenance edges to hardstanding as stated above.

Undesirable plant growth within the sward, such as scrub, dock, thistle, nettles and ragwort, should be controlled by hand excavation /pulling. Any encroaching scrub vegetation shall be removed by hand picking/weeding, this should be undertaken in the winter months, to avoid the bird nesting season.

Litter shall be hand picked and bagged from all grass areas prior to cutting. Bags shall be removed from site and legally disposed of.

Areas of grassland that fail to establish and thrive should be reported to the project landscape architect and ecologist to establish reason for failure such as unsuitable site conditions or ground compaction.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.10 INTRODUCED SHRUB

Areas and landscape elements included

Proposed planting around the LLAP as shown on P19-0052_EN_139

Management Aim

- To successfully establish areas of new ornamental planting; and
- To present and maintain high quality visual appearance of planting.

Management Objectives

- To maintain newly planted shrubs and herbaceous plants to ensure a good survival rate and development;
- To minimise competition from grass and weeds; and
- To keep planted areas free from litter, rubbish, garden waste and dog faeces.

Formative pruning will be kept to a minimum, where necessary diseased and damaged plant material will be removed. Where shrubs overhang path edges they will be neatly clipped back in order to maintain the full width of pedestrian access routes.

Planting beds will be checked regularly throughout the growing season for pests and diseases and treated as necessary. Plant losses should be monitored and recorded. If a particular plant becomes subject to a fatal pest or disease it shall be replaced by an alternative resistant plant with a similar form and habit (refer to note on plant substitution in general maintenance guidance paragraph 4.7).

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.11 PLAY EQUIPMENT

Areas and landscape elements included

Proposed play equipment within the LLAP as shown on P19-0052_EN_139

Management Aim

- To regularly inspect and maintain play area to comply with current legislation and regulations.

Management Objective

- To maintain the recreational equipment in a safe and viable state which ensures freedom from unacceptable risk.

All play equipment (informal and formal) will be regularly inspected to identify any obvious hazards, this includes a post installation inspection, weekly, monthly and annual inspections. The high quality appearance of the equipment will be maintained through maintenance inspections with work undertaken as required.

Post installation inspections (carried out by a ROSPA consultant) will ensure that the play space meets the required standards and has been installed correctly. The inspection will check the site on completion including equipment, surfacing, any ancillary items and undertake a disability and risk assessment with a report produced to confirm the findings.

Weekly and monthly inspections – regular checks will ensure the play space and its equipment is functional, and will help to identify any faults or dangers arising from vandalism or breakage. The weekly inspection will check the site, surfacing and equipment and record any faults within the log book. Should a fault be found on a piece of play equipment or the play area be found unsafe and cannot be immediately corrected the equipment should be removed or immobilised and the piece/space be cordoned off with a warning noticed attached.

Annual inspections are required to ensure the play equipment and ancillary items are compliant to EN 1176 and EN 1177 and should be undertaken by an independent, suitably qualified specialist. The annual inspection will look at the site design safety, ancillary item safety, equipment and surfacing safety. The condition of the equipment is assessed and any repair or refurbishment requirements noted. Where necessary the inspector would make suggestions where the quality of the site could be improved. The annual inspections will be non-dismantling, however, where dismantling work is required, this will be recommended.

After each annual inspection, a written report is to be supplied to the client covering site safety and condition, equipment, surfacing, and ancillary item safety and condition, and compliance with EN1176 where relevant.

Recommendations for any remedial action required are given together with risk ratings for each item. The report will note compliance with standards and notifications of failures/faults where necessary and an assessment of risk, notification of faults and suggested remedial action.

Whilst annual inspection is not mandatory law under Section 3 of the Health and Safety at Work Act 1974 requires a risk assessment to be undertaken as part of the inspection process for play equipment.

4.12 ECOLOGICAL ENHANCEMENTS TO THE EMM BROOK

Areas and landscape elements included

Proposed pre-planted coir rolls located within the Emm Brook as shown on P19-0052_EN_139

Management Aim

- To enhance the bankside habitat of the Emm Brook to contribute to biodiversity net gain of the site.

Management Objectives

- To ensure pre-planted coir logs are secure; and
- To maintain newly planted coir logs to ensure a good survival rate and development

Pre-planted coir rolls will only include native species and will not contain plastic.

During the first year after installation, coir rolls are to be inspected at regular intervals to ensure they haven't worked loose and to ensure the plants have successfully established

During the first three years no management is to be carried out on the plants, other than to check for successful establishment and to report any plant failures.

From year four onwards a four year cutting cycle should be carried out with an annual winter cut to a height of 100mm.

Eventually the coir will decompose with the plants living on and becoming part of the bank edge soil.

The wider 8m wide wildlife zone is to be sown with purple moor grass and rush pastures and should therefore be managed in line with the maintenance requirements set out 4.9.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.13 HARD LANDSCAPE – INCLUDING FOOTPATHS, STREET FURNITURE, FENCING, GATES AND PUBLIC ART

Areas and landscape elements included

Proposed hard landscaping including footpaths, street furniture, fencing, gates and public art located within the SANG as shown on P19-0052_EN_139

Management Aim

- To present the visible indication of high quality, regular site maintenance.

Management Objectives

- To keep hard landscaped areas free of debris, litter, graffiti & dog faeces;
- To keep weed colonisation at a minimum and acceptable level;
- To maintain fences to ensure a secure boundary is maintained to support the use of the SANG for off-lead dog exercising;
- To maintain gates to ensure suitable access for pedestrians and maintenance vehicles;
- To maintain hard landscaped areas in safe condition;
- To maintain public art in a safe condition; and
- To maintain street furniture, including litter bins and seats and replace if necessary.

Fences, dog proof mesh and gates are to be checked fortnightly for damage including vandalism, wildlife digging or structural issues. Any reports of damage to fencing and gates should be repaired at the earliest opportunity with damaged areas cordoned off to reduce risk of dogs escaping.

Hard areas and elements will be regularly checked for subsidence and damage and will be repaired at the earliest opportunity using the original specified material. Areas where damage poses a hazard to pedestrians shall be cordoned off with bollards and high visibility tape until repair can be organised.

A “no tolerance” policy will apply to graffiti which shall be removed as soon as it appears and where necessary specialist contractors shall be employed to carry out this work.

4.14 ECOLOGICAL HABITATS

Areas and landscape elements included

Proposed ecological habitat includes the retained habitats and proposed grassland, hedgerow and woodland planting will provide opportunities for a range of protected species including bats, badger, breeding birds, reptiles, great crested newt and invertebrates.

Management Aim

- To establish habitats that provide benefits to protected species

Management Objectives

- To avoid harm and disturbance to protected species during habitat management

Bird and Bat Roost Boxes

Bird and bat boxes will be installed on site in accordance with the Bird and Bat Box Plan. A barn owl box will be installed within a retained tree within Holme Park SANG

Reptile and amphibian habitat

Habitat management objectives for grassland and scrub will ensure suitable habitats are present on site for reptiles and great crested newt. Arisings from tree works are to be used to create habitat piles in areas of long grass or close to shrub and tree planting to minimise disturbance.

Refer to ECOSA (2026), Holme Park SANG, South Wokingham – Ecological Mitigation Strategy. ECOSA for further information on habitats and locations of features.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.15 WBC SUDS BASIN

Areas and landscape elements included

Proposed grassland, shrub and tree planting associated with the WBC SUDS basin. Maintenance to be carried out in accordance with LEMP produced by Lanpro July 2025.

Management Aim

- To maintain the SuDS basin as a successful on site water management system;
- To maintain the SuDS basin as a habitat feature to provide foraging area for wildlife and as an attractive landscape feature;
- To create a scrape habitats within the SuDS basin; and
- To avoid dense shading of the margins around the SuDS basin.

Management Objectives

- To ensure the design water management capacity for the basins are achieved through viable equipment associated with the basin;
- To ensure grassland areas within the basin successfully establishes;
- To ensure planting within the scrape habitats within the basin successfully establishes
- To ensure tree planting within the basin successfully establishes; and
- To control weeds / scrub invasion detrimental to appearance or usage.

The SuDS basin should be maintained according to best practice as set out in The SuDS Manual (C753) and in line with the LEMP produced by Lanpro July 2025. Areas of tree and shrub planting and grassland within the basin will be managed and maintained as per tree and shrub planting and grassland elsewhere within the areas of public open space.

Inspect scrape margins in winter (November/December), spring (March/April), and summer (July/August) to assess vegetation establishment and ensure that levels are appropriate to support emergent macrophytes. Monitor water depth within the scrape in winter (November/December), spring (March/April) and summer (July/August). Adjust levels to improve water retention to ensure scrapes remain damp or seasonally wet, where necessary. Levels should be lowered in August year one. Levels should be reassessed in year 5.

If the waterbody should become heavily shaded (more than 50% at 1m from the pond margins) management will include cutting back overhanging trees

and shrubs to reduce shading and leaf fall into the waterbody.

Due care will be taken when carrying out management and maintenance operations in and around the SuDS detention basin. In line with the CIRIA SuDS Manual C753 2015 (Section 32 Operation and Maintenance), slopes have been designed to comply with maximum gradient of 1:3. Maintenance of the grass within the main body of the attenuation feature is to be carried out using hand machinery such as push mowers, with grass around the inlet and outlet infrastructure being strimmed closely to reduce risks to system performance. Appropriate training should be provided to encourage safe working practices on side slopes by water and should not take place during or immediately following periods of excessively wet weather.

These management measures will achieve the targeted conditions as set out in the Biodiversity Net Gain Assessment produced by ECOSA

4.16 SUMMARY

Management Action	Landscape Objective(s)	Ecological Objective(s)
Management of soft landscape in accordance with the landscape management plan	1 – 7	
Inspection and maintenance of hard landscape items	8 – 9	
Management and maintenance of bird and bat boxes, in addition to reptile hibernacula		6
Undertake planting and seeding in accordance with the Landscape Specification	3 – 7	
Undertake landscape hardworks in accordance with the Landscape Hardworks Specification	8 – 9	
Undertake woodland management		1 – 2
Undertake hedgerow management	1, 3, 6	1 – 2
Undertake grassland management	7	4
Protection and management of Emm Brook in accordance with the SANG CEMP	2 – 4	3
Undertake Environmental Tool Box Talk		1 – 6
Undertake provision of bird and bat boxes and reptile hibernaculas		6

5.0 SCHEDULE OF MANAGEMENT AND MAINTENANCE

5.1 ESTABLISHMENT YEARS 0-5

The below table sets out how the maintenance tasks for the management aims and objectives will be achieved for the establishment period of years 0-5:

Establishment Years 0-5			
Ref	Management Categories	Timing	Maintenance Task and Method
5.1.1	All planting areas	Every Visit	Ensure continued health of all landscaping – water and fertilise as required to ensure that the planting continues to establish successfully. Investigate any failed growth and take remedial action as necessary.
		Monthly	- Removal of rubbish and debris – clear litter and fly-tipped rubbish by hand and remove from site. Remove rubbish and debris from grass/wildflower areas before mowing. - Inspect for vandalism – visual inspection of all landscaping for vandalism, report to client. On instruction from client replace any landscaping damaged by vandalism.
		Annually	- Monitor and record any plant losses and report to client – on instruction from client remove dead plant and replace as per original approved specification, unless otherwise agreed to plant alternative species. Maintain to ensure survival. Re-planting to be undertaken in November/December. - Remove exotic plant species that do not belong in each type of habitat/the general environment – check all landscaped areas for exotic species, clear by strimming and remove from site - Control vigorous and exotic plant species that do not belong in each type of habitat/the general are out competing less vigorous species – check all landscaped areas for invasive species e.g. self seeded sycamore, brambles, ground ivy and nettles. Reduce/clear by strimming undertaken in the winter months, to avoid the bird nesting season. Trimmer guards must be in place on trimmers to prevent damage to bark of young trees and shrubs. Care must be taken to control sweeping motions to maintain a suitable distance away from tree and shrub planting. Any undesirable encroaching vegetation in close proximity to newly planted shrubs shall be removed by hand picking/weeding, undertaken in the winter months to avoid bird nesting season.
5.1.2	Trees/tree groups/existing woodland/woodland buffer/new woodland areas/structural shrubs – retained and newly planted	Immediately prior to implementation of landscaping	An assessment of trees suitable to support bat roots should be undertaken by an ecologist prior to any tree works. Where possible trees or features within suitability for roosting bats should be retained, if this is not possible, additional surveys should be undertaken and a licence gained for the tree works as appropriate.
		Monthly	- Ensure trees/shrubs are stable – visually inspect tree/shrub guards/shelters to check for signs of bark damage or damage. Check that stakes, ties and guards are not too loose, too tight or broken. Check underground anchors. On instruction from client, replace or upgrade guards/shelters as necessary. - Where trees have become moribund due to compaction or lack of nutrients soil aeration techniques are to be used and the use of inoculants shall be considered. - Monitor transplants to ensure developing healthily – visual inspection of plants, if not stable/upright rectify by replanting in an upright position and re-firm, if plant remains unstable remove by hand and replace. Undertake for the first two years. - Visual inspection for fungal activity (for trees this is to be performed by a qualified arboriculturist) – remove diseased wood or treat as appropriate. Keep use of pesticides to a minimum. Inspection to be undertaken March to October when trees/shrubs are still in leaf.

Establishment Years 0–5			
Ref	Management Categories	Timing	Maintenance Task and Method
	Trees/tree groups/ woodland buffer/structural shrubs – retained and newly planted (continued)	2 times per annum	Visually inspect bark mulch areas around trees and top up to 75mm depth, if required. Visually inspect structural shrub surrounds for grass/weeds – remove by strimmers (see notes in 5.1.1 for the use of strimmers around planting) to be undertaken outside of bird nesting season.
		Annually	- Establishment survey for new trees – to be undertaken by a qualified arborist, any recommendations to assist with establishment must be undertaken as soon as possible. - Keep paths/highway/parking clear from branches/vegetation – pruning/cut back any tree branches/vegetation encroaching. Trees shall be pruned to a height of 5m if overhanging highways and 3m if over paths. - Remove dead, damaged or dying branches as appropriate. Deadwood is to be retained in a number of piles within the woodland area, to provide additional habitat areas for wildlife. Piles are to be no more than 600mm high, with the wood at the bottom of the pile set 1/3rd into the ground. - Formative pruning of new trees – to create a well balanced tree with a single leader and, by rubbing off any shoots, creating a clear stem of 2m. When the trees reach 5–6m in height, lower branches will be removed to give a canopy height of approximately 2.4m.
		Biennial (or as recommended)	A detailed condition survey of all trees will be carried out by a qualified arborist at least once every two years to check tree safety – identify hazards and carry out necessary maintenance works. A visual tree assessment is to be undertaken by a qualified arboriculturist of all new and existing tree planting, with instrumental back up where necessary. Any resulting tree works are to be carried out to BS 3998:2010. Keep records up to date.
		3 to 5 years after planting	Confirm root growth is well established and remove shelters, stakes, guards and ties from trees/transplants – to avoid damage cut shelters away then remove stakes.
5.1.3	Orchard tree	Annually	- Pruning should be carried out in winter, when the leaves are off the tree. - Best practice should be followed and work is to be undertaken by a qualified arborist. - Prune between 10–20% of the overall canopy off in any one winter – focus on removing branches which are crossing, weak or diseased. Pruning should remove old wood to stimulate new growth and create an open centre to the tree to allow light into the canopy to ripen fruit and improve air movement to discourage disease. - Signage is to be used to inform visitors when fruit trees can be cropped. - Rotting fruit is to be removed from the ground surrounding the tree and disposed of responsibly. - Remove dead, damaged or dying branches as appropriate. Deadwood is to be retained in a number of piles within the woodland area, to provide additional habitat areas for wildlife. Piles are to be no more than 600mm high, with the wood at the bottom of the pile set 1/3rd into the ground.
		Biennial (or as recommended)	A detailed condition survey of all trees will be carried out by a qualified arborist at least once every two years to check tree safety – identify hazards and carry out necessary maintenance works. A visual tree assessment is to be undertaken by a qualified arboriculturist of all new and existing tree planting, with instrumental back up where necessary. Any resulting tree works are to be carried out to BS 3998:2010. Keep records up to date.

Establishment Years 0–5			
Ref	Management Categories	Timing	Maintenance Task and Method
5.1.4	Existing Woodland – Including Ancient Woodland (to be in accordance with PRI24132 Woodland Management Plan by ACD Environmental	Fortnightly	Maintain the woodland to ensure it remains free of rubbish and harmful pollutants Remove litter by hand as required. Bin emptying to be carried out in lines with 5.1.11
		Monthly	- Footpath is to be walked once a month (or after significant storm events) to identify any hazardous trees and/or other tree hazards adjacent the edges of the woodland. Any trees identified as hazardous are to be made safe/removed as necessary. - Any arisings from tree works will be used to create habitat features including creation of standing deadwood where possible, log piles and hibernacula. Log piles are to be no more than 600mm high, with the wood at the bottom of the pile set 1/3rd into the ground. Log piles are not to be located in high use areas and should be located in areas of long grass or close to shrub and tree planting to minimise disturbance.
		Annually	- Monitor woodland following the above works to assess natural regeneration. Management/works to be amended as and where necessary to achieve the objectives of the Woodland Management Plan. - Remove dead, storm damaged or dying branches as appropriate. Deadwood is to be retained in log piles within the woodland area, to provide additional habitat for wildlife and improve biodiversity. - Inspect woodland to identify non-native invasive species (including but not limited to Japanese knotweed, rhododendron and Himalayan balsam). Any non-native invasive species found to be within the woodland are to be removed by a suitably qualified professional and disposed of safely at a licensed landfill site according to the EPA (Duty of Care) Regulations 1991.
		Biennial (or as recommended)	A detailed condition survey of all trees will be carried out by a qualified arborist at least once every two years to check tree safety – identify hazards and carry out necessary maintenance works. A visual tree assessment is to be undertaken by a qualified arboriculturist of all new and existing tree planting, with instrumental back up where necessary. Any resulting tree works are to be carried out to BS 3998:2010. Keep records up to date.
5.1.5	Hedgerows – New and Existing	Monthly	- Check hedgerows for gaps, record and infill during late October to March. Plant replacement tall whips, of a species mix to match the hedgerow or to increase native diversity, in a suitably prepared soil bed. Ensure successful establishment and protect from trampling/use as a short cut using a temporary fence/guards. - Keep hedgerow planting free from weeds – visually inspect bark mulch areas around planting and top up to 75mm depth, if required. Remove any weeds within the mulch by hand, hoe or fork. Take care not to disturb shrub roots and excessive treading of bed surface. Do not use strimmers or herbicides in these areas – March to October.

Establishment Years 0-5			
Ref	Management Categories	Timing	Maintenance Task and Method
	Hedgerows – New and Existing cont.	Annually	- Prune retained hedgerows to ensure a good shape and healthy growth – prune to maintain an ‘A’ shape and control future growth. Management to be undertaken in January/February. To be maintained at 3m height. - Identify suitable growth in retained hedgerows to develop into frequent standard trees, maintain as per tree maintenance and management. - All hedgerow trees will be monitored for any signs of defects or poor health on a yearly basis, or after severe weather by a suitably qualified arborist. Any signs of damage or ill health will require action to be taken immediately. Prior to any works consultation will be undertaken with an experienced ecologist in respect to bats. Where possible, trees will be allowed to age naturally and dying trees allowed to decay in-situ. - Prune/shape new hedgerow planting to a shape and form appropriate to the species with formative and seasonal pruning to create and maintain a natural ‘A’ shape hedgerow, pruning dead foliage and extension growth as necessary. Proposed hedgerow to be maintained at 1.5m height. - Re-plant in an upright position and re-firm plants that suffer from wind-rock – January/February. - Feed instant hedgerows – as per suppliers recommendations, feed in spring with a good quality nutrient blend fertiliser.
		3 to 5 years after planting	Confirm root growth is well established and remove shelters, stakes, guards and ties from hedgerow transplants – to avoid damage cut shelters away then remove stakes.
5.1.6	Grasslands – Flowering Lawn, Wildflower Meadow, Semi-shade tolerant grassland, purple moor grass and rush, and Wetland Grassland Meadow.	General	- Do not cut grass in drought conditions. Mow with suitable machinery – no mower or strimmer will be allowed within 400mm of a tree trunk. Edge and trim junctions between grassland / wildflower and hard surfaces to maintain a neat and tidy appearance. For all areas of grassland, remove arisings from site and dispose of responsibly. Clean adjoining path areas after mowing. - Keep grass areas/wildflower free from weeds – remove weeds and encroaching scrub by hand, hoe or fork, or mowing, as appropriate. Undertake monthly from March to October, or as required. Scrub removal from long grass/wildflower to be undertaken outside of the bird nesting season.
		Cutting Regime – Year 1	Newly sown meadows and grassland are to be unmaintained until summer. Annual weeds arising after sowing will provide shelter to the sown seedlings. Grassland is to be cut in August, with cuttings removed and disposed of off site.
		Cutting Regime – Year 2 onwards	<u>Wildflower meadow, semi-shade tolerant grassland and wetland grassland:</u> To be cut through an annual hay cut – typically in August. Cuttings should be left on site for 7 days to allow seeds to shed. Once seeds have shed, cuttings are to be collected and removed from site. Areas of semi-shade tolerant grassland can be cut on a rational basis, with areas cut every 2 – 3 years so that no more than 50% of grassland is cut in one year.. <u>Purple Moor Grass and Rush:</u> Annual hay cut to 100mm height should be carried out in August. Ground conditions should be reviewed prior to cutting, if ground conditions are unsuitable the hay cut should be carried out by hand or delayed until ground conditions improve. This is to prevent compaction of the soil. Cuttings should be left on site for 7 days to allow seeds to shed. Once seeds have shed, cuttings are to be collected and removed from site. Areas of purple moor grass and rush can be cut on a rational basis, with areas cut every 2 – 3 years so that no more than 50% of grassland is cut in one year. <u>Areas of flowering lawn with wildflower plugs and bulbs:</u> once established the planting the grassland with wildflower plugs and bulbs should be managed with through regular mowing (every three weeks) mowing is to be relaxed from late June for 4-8 weeks to allow flowering. Cuttings should be collected and removed from site.

Establishment Years 0–5			
Ref	Management Categories	Timing	Maintenance Task and Method
	Grasslands – Flowering Lawn, Wildflower Meadow, Semi-shade tolerant grassland, purple moor grass and rush, and Wetland Grassland Meadow.continued	Annually	Keep grassland areas in good condition – check and report to client on damaged areas. On instruction from client repair damaged/failed areas and re-sow seed. If required, apply feed treatment to amenity grass only, do not apply feed to wildflower or wetland meadow grass. Undertake aeration and thatch removal if required. April or September.
5.1.7	Pre-Planted Coir Rolls	Monthly (first two years)	Ensure coir logs are secure
		Every 4 years	Annual winter cut to 100mm of planting within coir-logs
5.1.8	Introduced Shrubs	Monthly	- Keep planting beds free from weeds – visually inspect bark mulch areas around planting and top up to 75mm depth, if required. Remove any weeds within the mulch by hand, hoe or fork. Take care not to disturb shrub roots and excessive treading of bed surface. Do not use strimmers or herbicides in these areas – March to October. - Keep paths and parking bays clear from vegetation – prune back ornamental planting which has encroached. As required from March to October. - Keep ornamental planting in prime condition and appearance – qualified horticultural staff to inspect and check on condition of ornamental planting. Prune dead foliage, flowers and extension growth as necessary. Divide perennials as necessary. Formative and seasonal pruning to shrubs to create a natural shape – do not routinely clip shrub. Apply organic fertiliser if required. Re-plant in an upright position and re-firm plants that suffer from wind-rock. Management to be undertaken as required depending on species. - Check on health of ornamental planting – qualified horticultural staff to inspect planting and deal with individual problems as they arise. Keep pesticide use to a minimum – March to October.
		2 times per annum	Removal of excessive leaf litter and fallen twigs and branches – use leaf blower and leaf litter collection equipment – November to December

Establishment Years 0-5			
Ref	Management Categories	Timing	Maintenance Task and Method
5.1.9	Playground Equipment *play spaces are to be fenced off (with appropriate signage to tell users not to enter) until the post installation inspection is completed and the play space is fit for purpose/use	Post Installation*	- Post installation inspections are to be carried out by a ROSPA consultant and will ensure that the play space (equipment, safety surfacing and any ancillary items including gates, fences, seats etc.) meet the required standards and has been installed correctly. - The inspection will include a disability and risk assessment with a report (including photographs) produced to confirm the findings including the quality of the installation and equipment finish. The report will be sent to the client
		Weekly	- Routine visual inspection of all play areas to identify obvious hazards or respond to complaints by public. Check for signs of vandalism and remove any litter, glass etc. Check safety surface for faults. If parts are found to be unsafe and cannot be immediately repaired the equipment should be immobilised or cordoned off with a warning noticed attached. - Check each item against a checklist (as provided by manufacturer for play equipment item) and record each visit on a spreadsheet, including any actions. - Note – Inspection to be undertaken by suitably qualified/competent professional.
		Monthly	- Perform operational inspection of all items of equipment, fences and gates to check the operation and stability. Checks to include: - all working parts and oil and grease bearings as necessary; - all ropes, chains and shackles; - anti slip surfaces e.g. on step treads; - that structures and foundations are secure; - for trip hazards and obstructions in surrounding area; - finger traps; - wooden items for splinters and cracks; - metal items for corrosion and sharp edges; - plastic/polythene items for brittleness and sharp edges. - If parts found to be unsafe and cannot be immediately corrected the equipment should be removed or immobilised and cordoned off with a warning noticed attached. Check each item against a check list and record each visit and required actions on a spreadsheet. - Inspect superficial appearance of equipment and street furniture – as required, sand down and re-paint or re-stain equipment, seats, bins and fences to specification provided by supplier.

Establishment Years 0–5			
Ref	Management Categories	Timing	Maintenance Task and Method
	Playground Equipment Continued	Annual	- Annual technical inspection of all play areas to establish overall level of safety of the equipment (whilst an annual inspection is not mandatory a risk assessment is required by law under the Health and Safety Regulations) – to be carried out by RPII (Register of Play Inspectors International) trained and certified inspectors or manufacturers inspection engineers. - Ensure the play space meets the relevant standards (EN1176) and will note any faults or failures and suggest appropriate remedial action and identify risks. - Assess all elements of site design safety, ancillary items, equipment and surfacing including an operational inspection of all to check the operation and stability. Checks to include: - all working parts and oil and grease bearings as necessary; - all ropes, chains and shackles; - anti slip surfaces e.g. on step treads; - that structures and foundations are secure; - for trip hazards and obstructions in surrounding area; - finger traps; - wooden items for splinters and cracks; - metal items for corrosion and sharp edges; - plastic/polythene items for brittleness and sharp edges. - If parts found to be unsafe and cannot be immediately corrected the equipment should be removed or immobilised and cordoned off with a warning noticed attached. - Check each item against a checklist (as provided by manufacturer for play equipment item) and record each visit and required actions on a spreadsheet, including corresponding actions and any remedial actions undertaken. - Includes a non-dismantling inspection of all equipment where recommended. To be supported by a detailed technical report highlighting any action required. If parts are found to be unsafe and cannot be repaired the equipment should be removed or immobilised and cordoned off with a warning notice attached.
5.1.10	WBC SuDS to be read in conjunction with South Wokingham Distributor Road LEMP by Landpro dated July 2025	Monthly	- Inspect inlets, outlets and overflows for blockages, and clear if required - Inspect banksides, structures, pipework etc for evidence of physical damage. - During the first year, inspect inlets and facility surface for silt accumulation. - Control invasive plants and naturally occurring weed within the marginal planting areas. Remove waste from site and dispose of responsibly.
		Annually	- Check mechanical devices associated with SuDS, report faults or failures and suggest appropriate remedial action. - As necessary, remove sediment from devices associated with the SuDS basin. - Monitor and record plant losses within marginal planting areas. Report losses to the client and replace on instruction. - Prune marginal planting as required to maintain attractive and healthy appearance. Dive any clump forming plants in early spring as required. Once cleared, keep any removed vegetation at the edge of the basin to allow any trapped reptiles, amphibians and invertebrates to migrate to a new habitat.

Establishment Years 0–5			
Ref	Management Categories	Timing	Maintenance Task and Method
5.1.11	Hard Landscape	As necessary	- Remove graffiti – a ‘no tolerance’ policy will apply to graffiti which shall be removed as soon as it appears, where necessary specialist contractors shall be employed to carry out this work. - Repair any reported damaged fences or gates.
		Fortnightly	- Empty bins – remove and replace bags form bins and deposit in legal tip. - Inspect fencing and dog proof mesh to ensure there are no gaps. Repair or replace as needed to maintain a safe space for dog walking. - Keep hard landscape areas clean – remove litter, debris and faeces. Use pressure washer to remove chewing gum and staining. Fortnightly March to October and as required during the winter months.
		Monthly	Maintain all hard landscape areas/elements, including bridges, footpaths, fences, gates, signage, seating and other street furniture, in a safe and clean condition – monitor and report to client on damaged areas/items and repair as instructed by the client. Repair using the original material/product to maintain the integrity of the design. Areas where damage poses a hazard to pedestrians shall be cordoned off with bollards and high visibility tape until repair can be organised.
		2 or 3 times per annum	- Removal of excessive leaf litter and fallen twigs and branches – use leaf blower and leaf litter collection equipment – November to December. - Keep hard landscaped areas clear of weeds – kill weeds using a herbicide spray containing glyphosate using a knapsack sprayer – April, June and August.
		Every 5 years	Check painted and stained surfaces for fading/damage – where necessary prepare and re-paint/stain using the same product to maintain the integrity of the design.
5.1.12	Bat and Bird Boxes	Annually	Visual inspection of all roosting/nesting boxes to maintain potential roosting sites – replace any broken/fallen bat or bird boxes.
5.1.13	Himalayan Balsam	Annually (April/ May)	Monitor Emm Brook river bank for presence of Himalayan Balsam. If present report back to maintenance team to ensure removal operations are carried out as below
		Fortnightly (May– June)	During May and June remove Himalayan Balsam plants by pulling by hand. <u>Plants are not to be removed if seed heads are present.</u> As Himalayan Balsam plants are classed as a ‘controlled waste’ under the Environmental Protection Act 1990 (EPA) they must be removed by a suitably qualified professional and disposed of safely at a licensed landfill site according to the EPA (Duty of Care) Regulations 1991.

5.2 LANDSCAPE MANAGEMENT REVIEW

The below table sets out how the review processes:

Monitoring and Review			
Ref	Management Categories	Timing	Maintenance Task and Method
5.2.1	Landscape and Habitat Management	As necessary	- Monitor comments/suggestions from residents and other users – feedback comments to client/ owner and respond as instructed and incorporate into LEMP as required. - An ecologist will visit the site in May and September for the first year only, then in September to check the establishment of seed mix and weed and to ensure appropriate habitat provision in line with the BNG Metric - Respond to comments from client/ owner and incorporate into LEMP as required.
5.2.2	Habitat Management – annual monitoring report	Annual (in October)	Review of habitat conditions (including grassland, hedgerows, shrub, scrub, trees and habitat piles) and species to be undertaken by a qualified ecological professional. The review and report will be used to determine whether or not objectives for the site and component features have been met. Once the review has been completed a monitoring report is to be produced. Any amendments set out within the report to be incorporated within this LEMP following discussions with the client/ owner.
5.2.3	LEMP Review	Every 5 years	Suitably experienced professional to undertake a review of habitat / landscape establishment and quality, respond to review and incorporate into LEMP as required.

5.3.1 All reviews and audit/monitoring reports are to be made available to the Local Planning Authority and any other statutory authorities who requests it.

6.0 RESPONSIBILITIES

SANG CREATION

6.1 Kier Venture Ltd and Miller Homes Ltd will appoint;

Landscape contractor to;

- Carry out all planting/seeding, hardworks, management of hedgerows and woodland and management of the Emm Brook

Landscape architect to:

- Monitor landscape planting/seeding, hardworks and habitat management.

ECoW to:

- Be responsible for the delivery of actions identified in Sections 4.5 and 5.1, including supervising bat box, bird box and reptile hibernacula installation

POST-SANG CREATION

6.2 It will be required that the SANG is open prior to first occupation. In line with the phasing plan (P19-0052_EN_141B), the SANG will be transferred to WBC 35 days after the completion of each phase.

6.3 It is anticipated that all landscape and ecological management, as outlined in Section 5 and detailed within this LEMP, would be undertaken by WBC or their appointed contractors.

6.4 Management is to include;

- Delivery of the woodland management plan;
- Management of grassland;
- Management of hedgerows;
- Management of wetland habitats including SuDS basins;
- Undertaking of arboricultural assessment of the trees every 2 years;
- Inspection of the bird/bat boxes every two years;
- Inspection and maintenance of the hardworks, including bridges, and undertake the proposed litter picks; and
- Establish a programme of events and activities within the SANG to animate the site and encourage community use and ownership.

6.5 It would be the responsibility of WBC to review and update the LEMP at the end of the five-year post-construction period.

7.0 APPENDICES




APPENDIX 1

List of Associated Detailed Planting Plans and Detailed Hard Landscape Plans

- P19-0052_139C Phase 2b SANG Detailed Hard and Soft Landscape (sheets 1 to 7)
- P19-0052_145C Phase 2b SANG Detailed LLAP
- P19-0052_141B Holme Park SANG Phasing Strategy

KEY


- Existing Vegetation to be retained with RPA's shown refer to ACD Drawings for further details
 - Ancient Woodland (with 15m Woodland Buffer shown)
 - Existing Emm Brook
 - Existing Public Rights of Way
 - Proposed SWDR planting – not to be counted towards BNG
 - Formal circular route: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved). 2m wide with timber edgings with 0.5m wide mown grass edge
 - Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved). 1.5m wide with timber edging
 - Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved). 1.5m wide with no edgings. Length of footpath to come forward when sports hub is operational.
 - East-West Pedestrian cycle route
3m wide flexible bonded aggregate footpath e.g KBI Flexistone in Cappuccino (or similar approved) Flexistone to form edging.
 - Informal mown path / mown path edges: Formed by regular mowing. 1m wide with no edging.
 - Path through Ancient Woodland: Refer to detail on sheet 2 for pedestrians and in-frequent vehicular maintenance access. 2.5m wide no dig footpath (e.g cellweb) within root protection area to be timber edged filled with breedon angular chippings in golden amber (or similar approved)
 - Path through root protection areas: Refer to detail on sheet 2 for pedestrians 2m wide no dig footpath (e.g cellweb) within root protection area to be timber edged to be filled with breedon angular chippings in golden amber (or similar approved)
 - Boardwalk ramp to bridges
Hardwood timber boardwalks to provide ramp to bridges. To be 2m or 3.6m wide to match the bridge crossing width. Refer to technical drawings A389-ANG-III – II4 for further details.
 - Pedestrian crossing point (2 no):
2m wide – each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards with antislip insets to form tread. Handrails to each side – to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III – II4 for further details.
 - Maintenance/pedestrian crossing point (2 no):
3.6m wide to allow maintenance vehicles to cross– each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards to form tread. Handrails to each side – to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III – II4 for further details.
 - Timber litter bin: (6 no.)
120L Okehampton Redwood litter bin, Broxap (BX17 4030), bolt down fixing (or similar approved)
 - Dog waste bin: (6 no.)
40L Sirius dog waste bin, Broxap (BX45 2591-PM) in Moss Green (RA 6005) to be root fixed (or similar approved)
 - Picnic Bench and Table (9 no.)
Cheshunt 6 person (CHS 4), bolt down fixing (or similar approved)
 - Seat: (18 no.)
Cheshunt seat with backrest 2 person (CHS4), bolt down fixing (or similar approved)
 - Welcome/Information Board: (3 no.)
Timber information board with map and information about the SANG. e.g Musketeer twin leg wooden lectern supplied by Fitzpatrick Woolmer or similar approved. To be installed with submerged fixings set into concrete footings as per manufacturer's specification. Content to be confirmed and agreed with WBC prior to installation
 - Play Space Information Board: (3 no.)
Aluminium information board to be fixed to playground fencing near to gates with information to be agreed with WBC prior to installation
 - Wayfinding: (10 no.)
Timber finger posts showing distances and direction to points of interest within and outside of the SANG such as play spaces, neighbourhood centre, neighbouring SANG and walking routes. eg Timber waymarker supplied by Woodscape or similar approved. To be engraved with painted lettering. To be set in concrete footings. Content to be confirmed and agreed with WBC prior to installation
 - Public Art (4no.)
Details of design and location to be confirmed in line with the public art strategy.
 - Mounding:
Earth mounding, maximum height 1m with a maximum 1:4 gradients
 - Dog Beach:
Area of gravel with gentle gradient to allow easy access for dogs to water
 - Gateway Feature: (1 no.)
Design to be confirmed in consultation with Ludgrove School
- Boundary treatments**
- Dog Proof Fencing:
1.2m high post and rail fence with mesh
 - Kissing gate: (12 no.) For pedestrians, pushchairs and wheelchairs
Timber with self-closing mechanism, to be fitted with agricultural wire fencing stock eg Jackson Fencing Mobility Kissing Gate 1.5m wide (or similar approved)
 - Field gate and access: (3 no.)
Timber field gate for maintenance access, 3.6m wide, 1.2m high (with lock) and self-closing pedestrian access gate 1.5m wide, 1.2m high. Both gates are to be fitted with agricultural wire fencing stock.
 - Fence to Play Space:
Timber playground fencing eg Jackson Wooden Playground Fencing (or similar approved) 1.05m high with natural finish.
 - Gate to Play Space: (3no.)
Timber play gate with steel frame eg Jackson Fencing Playtime Gate (or similar approved) inward opening with self closing operation with natural finish to timber gate and powder coating to steel frame.
 - Height Restriction Barrier (1no.)
2.1m high height restrictor barrier 6m wide with single leaf opening for larger vehicles. eg Jacksons Fencing Height restrictor barrier in black
 - Timber knee rail:
0.6m high timber knee rail e.g Jackson Fencing wooden knee rail fencing (or similar approved)
- Scattered Trees**
Proposed native tree planting
- Scattered Trees**
Proposed native feature tree planting
- Traditional Orchard**
Proposed orchard tree planting
- Other broadleaved woodland**
to provide a varied woodland structure with diverse species
- Mixed Scrub**
Woodland edge planting
- Mixed Scrub**
Proposed native shrub/scrub planting
- Sustainable Drainage System**
Proposed native shrub planting within SWDR basin
- Sustainable Drainage System**
Proposed defensible shrub planting within SWDR basin
- Introduced shrub**
Ornamental planting around LLAP
- Native species rich hedgerow**
- Native species rich hedgerow planting with trees**
- Other Neutral Grassland**
Proposed wildflower meadow (e.g. Emorsgate EM3 Special General Purpose Meadow Mixture)
- Proposed Purple Moor Grass and Rush Pasture** e.g Emorsgate EM8 Meadow Mixture for Wetlands with plug plants
- Other Neutral Grassland**
Proposed flowering lawn e.g Emorsgate EL1 with bulb plug planting
- Other Neutral Grassland**
Proposed long mown grass (e.g. Emorsgate EM2 Standard General Purpose Meadow Mixture)
- Modified Grassland**
Mown amenity grass
- Existing grassland to be retained and made good within the sports hub safeguarded route
- River enhancements**
Pre-planted coir rolls along water channel e.g Green-Tech Coir Log Rolls in 200mm. To be located on the eastern side of the Emm Brook

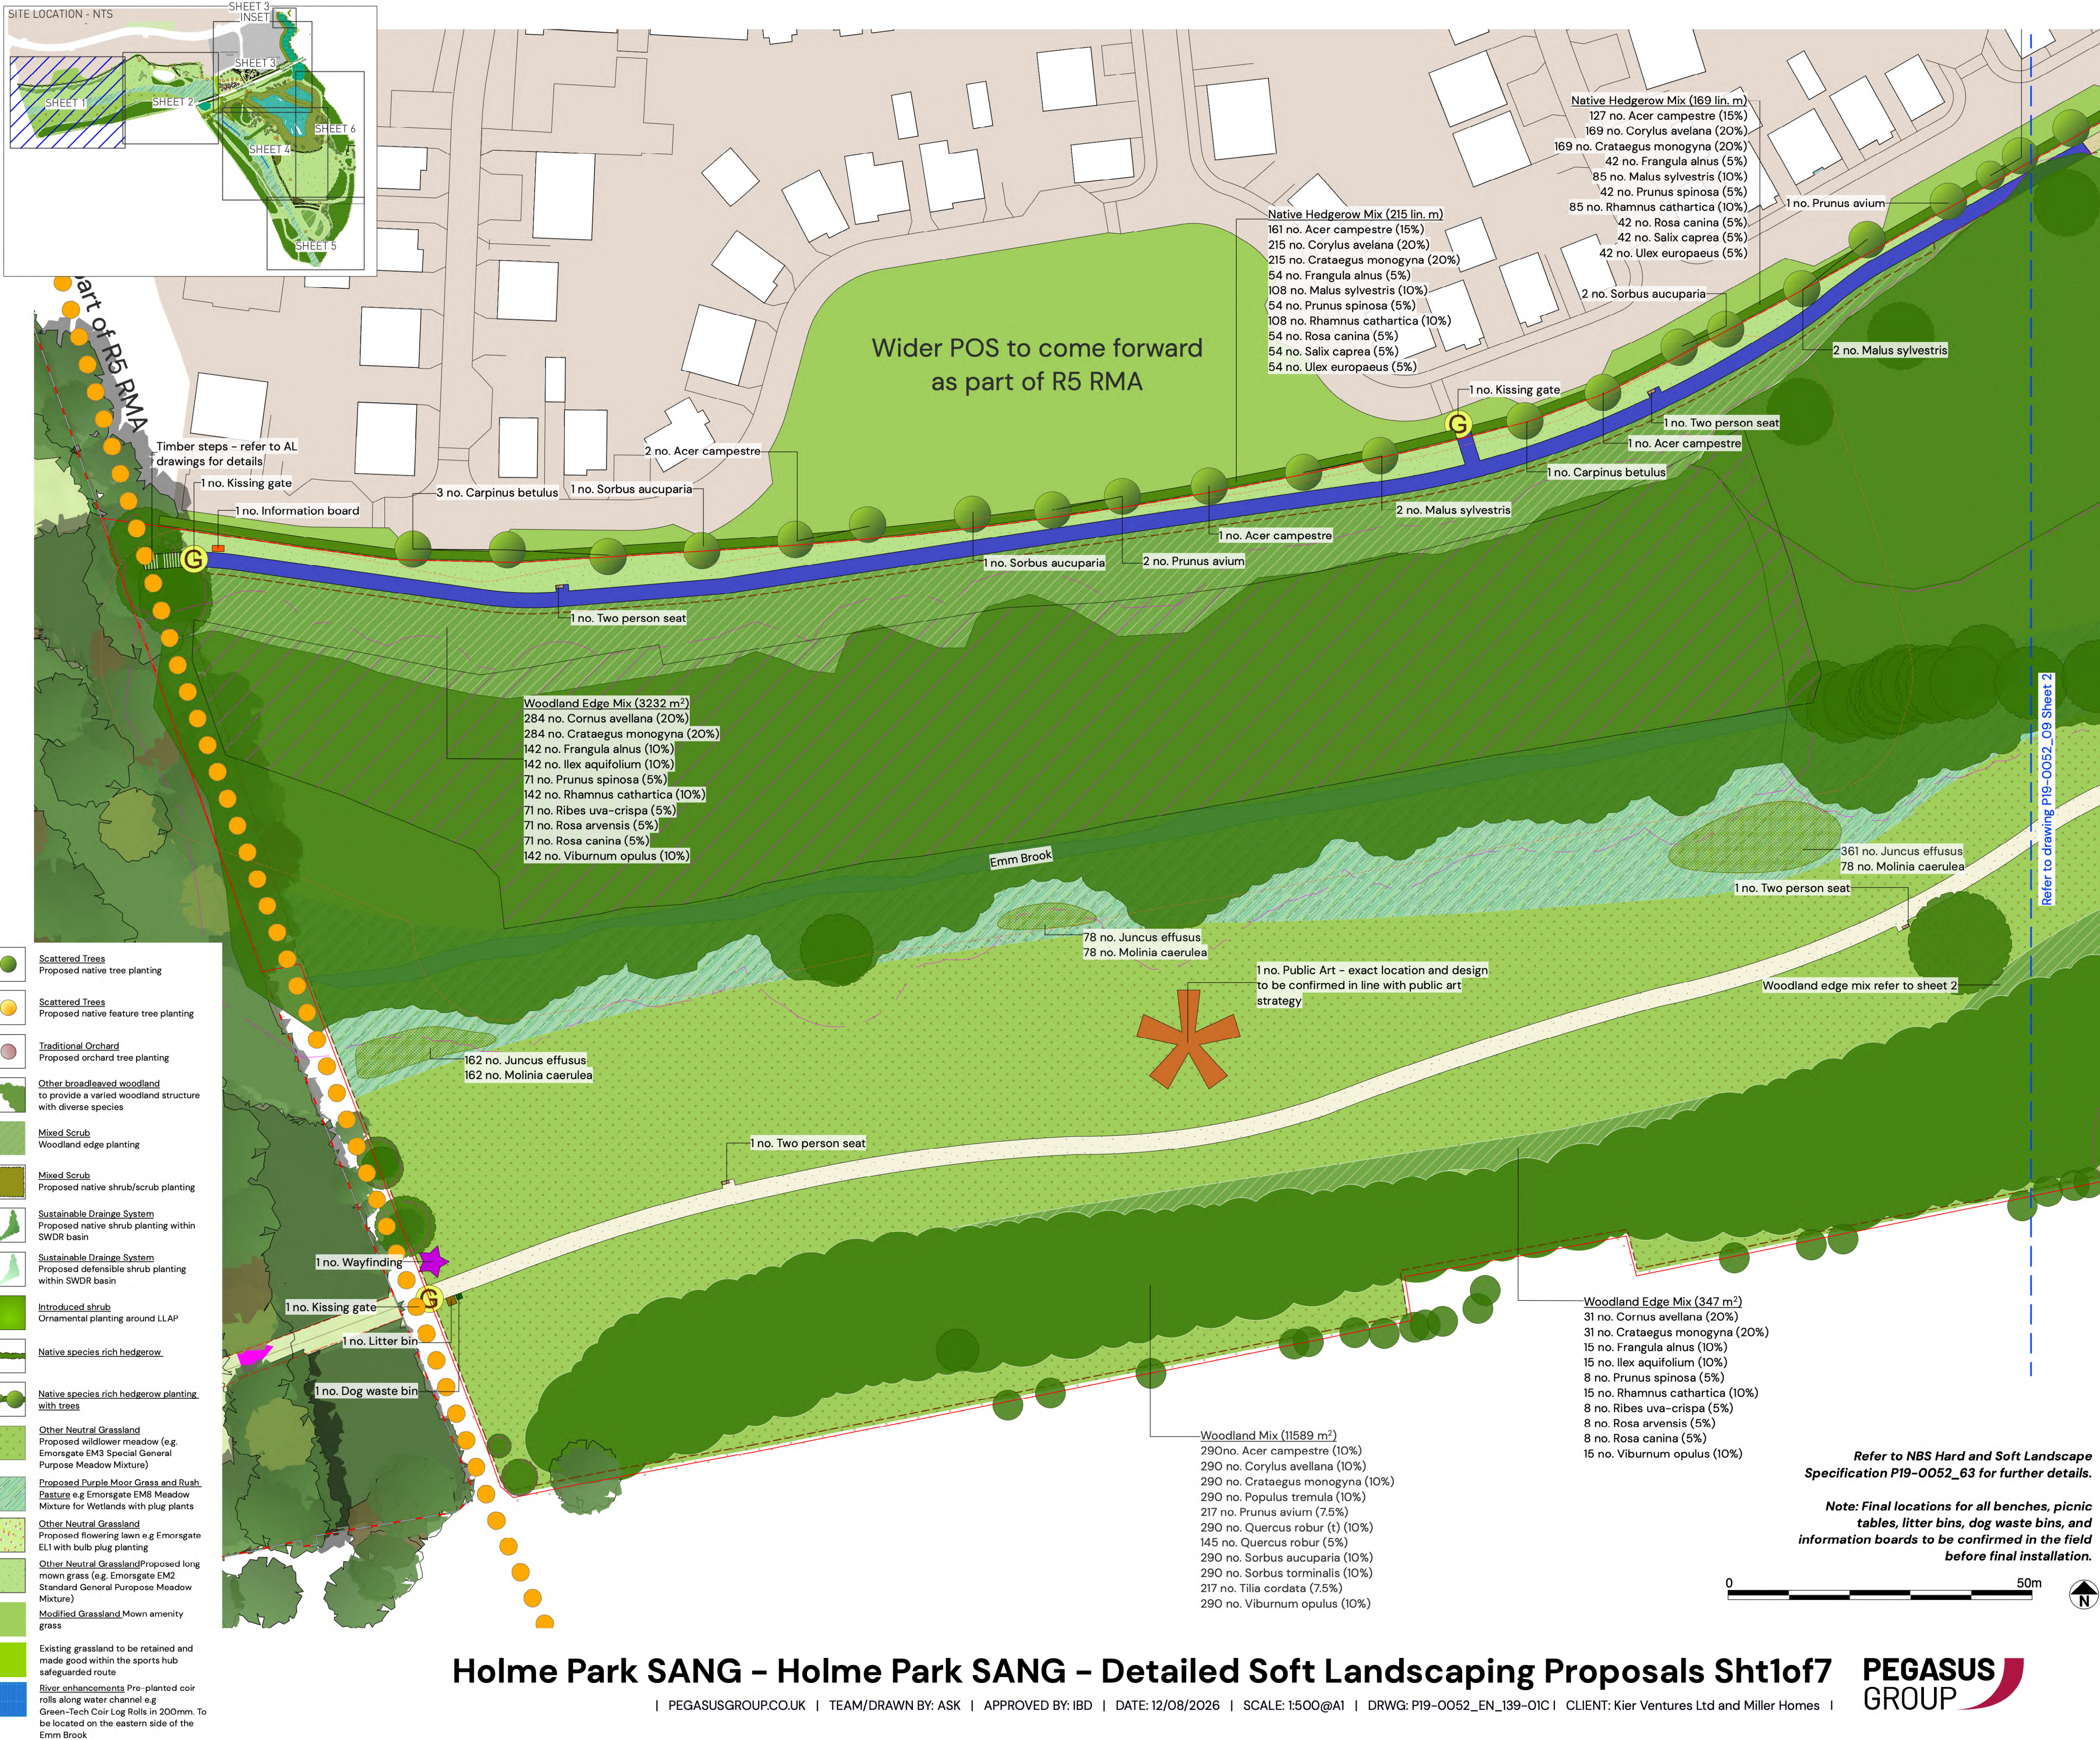

KEY

-
- Boundary treatments**

-

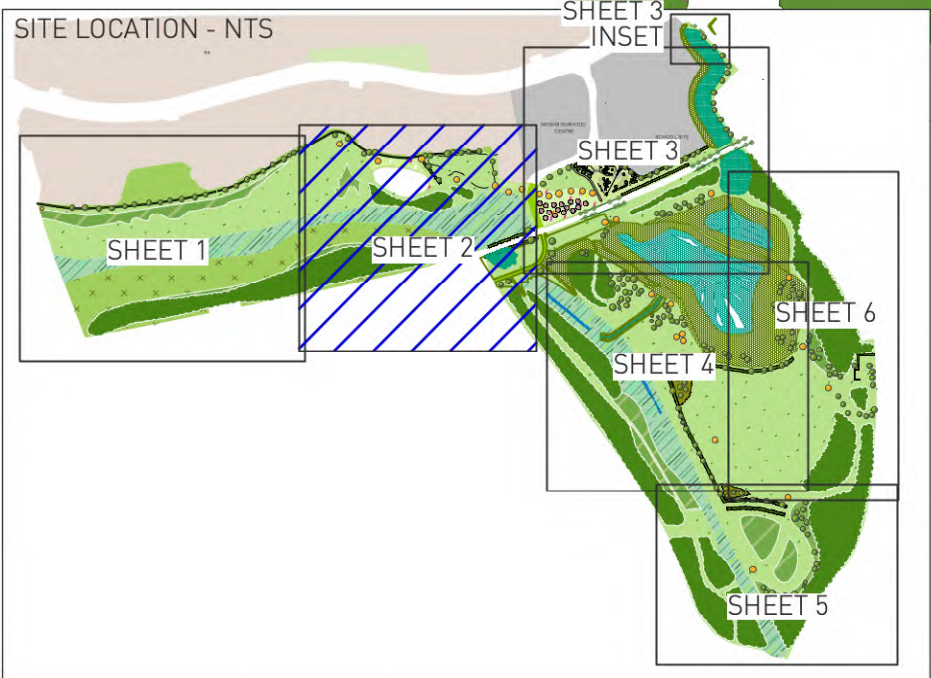

Refer to NBS Hard and Soft Landscape Specification P19-0052_63 for further details.

Note: Final locations for all benches, picnic tables, litter bins, dog waste bins, and information boards to be confirmed in the field before final installation.



Holme Park SANG – Holme Park SANG – Detailed Soft Landscaping Proposals Sht2of7

| PEGASUSGROUP.CO.UK | TEAM/DRAWN BY: ASK | APPROVED BY: IBD | DATE: 12/08/2026 | SCALE: 1:500@A1 | DRWG: P19-0052_EN_139-02C | CLIENT: Kier Ventures Ltd and Miller Homes |



KEY

- Existing Vegetation to be retained with RPA's shown refer to ACD Drawings for further details
- Ancient Woodland (with 15m Woodland Buffer shown)
- Existing Emm Brook
- Existing Public Rights of Way
- Proposed SWDR planting - not to be counted towards BNG
- Formal circular route: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved). 2m wide with timber edgings with 0.5m wide mown grass edge
- Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved). 1.5m wide with timber edging
- Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved). 1.5m wide with no edgings. Length of footpath to come forward when sports hub is operational.
- East-West Pedestrian cycle route
3m wide flexible bonded aggregate footpath e.g KBI Flexistone in Cappuccino (or similar approved) Flexistone to form edging.
- Informal mown path / mown path edges: Formed by regular mowing. 1m wide with no edging.
- Path through Ancient Woodland: Refer to detail on sheet 2 for pedestrians and in-frequent vehicular maintenance access. 2.5m wide no dig footpath (e.g cellweb) within root protection area to be timber edged to be filled with breedon angular chippings in golden amber (or similar approved)
- Path through root protection areas: Refer to detail on sheet 2 for pedestrians 2m wide no dig footpath (e.g cellweb) within root protection area to be timber edged to be filled with breedon angular chippings in golden amber (or similar approved)
- Boardwalk ramp to bridges
Hardwood timber boardwalks to provide ramp to bridges. To be 2m or 3.6m wide to match the bridge crossing width. Refer to technical drawings A389-ANG-III - II4 for further details.
- Pedestrian crossing point (2 no.):
2m wide - each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards with antislip insets to form tread. Handrails to each side - to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III - II4 for further details.
- Maintenance/pedestrian crossing point (2 no.):
3.6m wide to allow maintenance vehicles to cross- each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards to form tread. Handrails to each side - to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III - II4 for further details.
- Timber litter bin: (6 no.)
40L, Okhampston Redwood litter bin, Broxap (BX17 4030), bolt down fixing (or similar approved)
- Dog waste bin: (6 no.)
40L, Sirius dog waste bin, Broxap (BX45 259I-PM) in Moss Green (RA 600S) to be roof fixed (or similar approved)
- Picnic Bench and Table: (9 no.)
Cheshunt 6 person (CHS 4), bolt down fixing (or similar approved)
- Seat: (18 no.)
Cheshunt seat with backrest 2 person (CHS4), bolt down fixing (or similar approved)
- Welcome/Information Board: (3 no.)
Timber information board with map and information about the SANG. e.g Musketeer twin leg wooden lectern supplied by Fitzpatrick Woolmer or similar approved. To be installed with submerged fixings set into concrete footings as per manufacturer's specification. Content to be confirmed and agreed with WBC prior to installation
- Play Space Information Board: (3 no.)
Aluminium information board to be fixed to playground fencing near to gates with information to be agreed with WBC prior to installation
- Wayfinding: (10 no.)
Timber finger posts showing distances and direction to points of interest within and outside of the SANG such as play spaces, neighbourhood centre, neighbouring SANG and walking routes. eg Timber waymarker supplied by Woodscape or similar approved. To be engraved with painted lettering. To be set in concrete footings. Content to be confirmed and agreed with WBC prior to installation
- Public Art: (4no.)
Details of design and location to be confirmed in line with the public art strategy.
- Mounding:
Earth mounding, maximum height 1m with a maximum 1:4 gradients
- Dog Beach:
Area of gravel with gentle gradient to allow easy access for dogs to water
- Gateway Feature: (1 no.)
Design to be confirmed in consultation with Ludgrove School

Boundary treatments

- Dog Proof Fencing:
1.2m high post and rail fence with mesh
- Kissing gate: (12 no.) For pedestrians, pushchairs and wheelchairs
Timber with self-closing mechanism, to be fitted with agricultural wire fencing stock eg Jackson Fencing Mobility Kissing Gate 1.5m wide (or similar approved)
- Field gate and access: (3 no.)
Timber field gate for maintenance access, 3.6m wide, 1.2m high (with lock) and self-closing pedestrian access gate 1.5m wide, 1.2m high. Both gates are to be fitted with agricultural wire fencing stock.
- Fence to Play Space:
Timber playground fencing eg Jackson Wooden Playground Fencing (or similar approved) 1.05m high with natural finish.
- Gate to Play Space: (3no.)
Timber play gate with steel frame eg Jackson Fencing Playtime Gate (or similar approved) inward opening with self closing operation with natural finish to timber gate and powder coating to steel frame.
- Height Restriction Barrier: (1no.)
2.1m high height restrictor barrier 6m wide with single leaf opening for larger vehicles. eg Jacksons Fencing Height restrictor barrier in black
- Timber knee rail:
0.6m high timber knee rail e.g Jackson Fencing wooden knee rail fencing (or similar approved)

- Scattered Trees
Proposed native tree planting
- Scattered Trees
Proposed native feature tree planting
- Traditional Orchard
Proposed orchard tree planting
- Other broadleaved woodland
to provide a varied woodland structure with diverse species
- Mixed Scrub
Woodland edge planting
- Mixed Scrub
Proposed native shrub/scrub planting
- Sustainable Drainage System
Proposed native shrub planting within SWDR basin
- Sustainable Drainage System
Proposed defensible shrub planting within SWDR basin
- Introduced shrub
Ornamental planting around LLAP
- Native species rich hedgerow
- Native species rich hedgerow planting with trees
- Other Neutral Grassland
Proposed wildflower meadow (e.g. Emorsgate EM3 Special General Purpose Meadow Mixture)
- Proposed Purple Moor Grass and Rush Pasture e.g Emorsgate EM8 Meadow Mixture for Wetlands with plug plants
- Other Neutral Grassland
Proposed flowering lawn e.g Emorsgate EL1 with bulb plug planting
- Other Neutral Grassland
Proposed long mown grass (e.g. Emorsgate EM2 Standard General Purpose Meadow Mixture)
- Modified Grassland Mown amenity grass
- Existing grassland to be retained and made good within the sports hub safeguarded route
- River enhancements Pre-planted coir rolls along water channel e.g Green-Tech Coir Log Rolls in 200mm. To be located on the eastern side of the Emm Brook

Refer to NBS Hard and Soft Landscape Specification P19-0052_63 for further details.

Note: Final locations for all benches, picnic tables, litter bins, dog waste bins, and information boards to be confirmed in the field before final installation.




Holme Park SANG - Holme Park SANG - Detailed Soft Landscaping Proposals Sht3of7

| PEGASUSGROUP.CO.UK | TEAM/DRAWN BY: ASK | APPROVED BY: IBD | DATE: 12/08/2026 | SCALE: 1:500@A1 | DRWG: P19-0052_EN_139-03C | CLIENT: Kier Ventures Ltd and Miller Homes |

PEGASUS GROUP

KEY

- Existing Vegetation to be retained with RPA's shown refer to ACD Drawings for further details
- Ancient Woodland (with 15m Woodland Buffer shown)
- Existing Emm Brook
- Existing Public Rights of Way
- Proposed SWDR planting - not to be counted towards BNG
- Formal circular route: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved), 2m wide with timber edgings with 0.5m wide mown grass edge
- Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved), 1.5m wide with timber edging
- Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved), 1.5m wide with no edgings. Length of footpath to come forward when sports hub is operational.
- East-West Pedestrian cycle route
3m wide flexible bonded aggregate footpath e.g KBI Flexistone in Cappuccino (or similar approved) Flexistone to form edging.
- Informal mown path / mown path edges: Formed by regular mowing, 1m wide with no edging.
- Path through Ancient Woodland: Refer to detail on sheet 2 for pedestrians and infrequent vehicular maintenance access, 2.5m wide no dig footpath (e.g cellweb) within root protection area to be timber edged filled with breedon angular chippings in golden amber (or similar approved)
- Path through root protection areas: Refer to detail on sheet 2 for pedestrians 2m wide no dig footpath (e.g cellweb) within root protection area to be timber edged to be filled with breedon angular chippings in golden amber (or similar approved)
- Boardwalk ramp to bridges
- Hardwood timber boardwalks to provide ramp to bridges. To be 2m or 3.6m wide to match the bridge crossing width. Refer to technical drawings A389-ANG-III - T14 for further details.
- Pedestrian crossing point (2 no.)
2m wide - each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards with antislip insets to form tread. Handrails to each side - to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III - T14 for further details.
- Maintenance/pedestrian crossing point (2 no.)
3.6m wide to allow maintenance vehicles to cross- each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards to form tread. Handrails to each side - to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III - T14 for further details.
- Timber litter bin: (6 no.)
120L Okehampton Redwood litter bin, Broxap (BX17 4030), bolt down fixing (or similar approved)
- Dog waste bin: (6 no.)
40L Sirius dog waste bin, Broxap (BX45 2591-PM) in Moss Green (RA 6005) to be root fixed (or similar approved)
- Picnic Bench and Table (9 no.)
Cheshunt 6 person (CHS 4), bolt down fixing (or similar approved)
- Seat: (18 no.)
Cheshunt seat with backrest 2 person (CHS4), bolt down fixing (or similar approved)
- Welcome/Information Board: (3 no.)
Timber information board with map and information about the SANG, e.g Musketeer twin leg wooden lectern supplied by Fitzpatrick Woolmer or similar approved. To be installed with submerged fixings set into concrete footings as per manufacturer's specification. Content to be confirmed and agreed with WBC prior to installation
- Play Space Information Board: (3 no.)
Aluminium information board to be fixed to playground fencing near to gates with information to be agreed with WBC prior to installation
- Wayfinding: (10 no.)
Timber finger posts showing distances and direction to points of interest within and outside of the SANG such as play spaces, neighbourhood centre, neighbouring SANG and walking routes. eg Timber waymarker supplied by Woodscape or similar approved. To be engraved with painted lettering. To be set in concrete footings. Content to be confirmed and agreed with WBC prior to installation
- Public Art (4no.)
Details of design and location to be confirmed in line with the public art strategy.
- Mounding:
Earth mounding, maximum height 1m with a maximum 1:4 gradients
- Dog Beach:
Area of gravel with gentle gradient to allow easy access for dogs to water
- Gateway Feature: (1 no.)
Design to be confirmed in consultation with Ludgrove School
- Boundary treatments**
- Dog Proof Fencing:
1.2m high post and rail fence with mesh
- Kissing gate: (12 no.) For pedestrians, pushchairs and wheelchairs
Timber with self-closing mechanism, to be fitted with agricultural wire fencing stock eg Jackson Fencing Mobility Kissing Gate 1.5m wide (or similar approved)
- Field gate and access: (3 no.)
Timber field gate for maintenance access, 3.6m wide, 1.2m high (with lock) and self-closing pedestrian access gate 1.5m wide, 1.2m high. Both gates are to be fitted with agricultural wire fencing stock.
- Fence to Play Space:
Timber playground fencing eg Jackson Wooden Playground Fencing (or similar approved) 105m high with natural finish.
- Gate to Play Space: (3no.)
Timber play gate with steel frame eg Jackson Fencing Playtime Gate (or similar approved) inward opening with self closing operation with natural finish to timber gate and powder coating to steel frame.
- Height Restriction Barrier (1no.)
2.1m high height restrictor barrier 6m wide with single leaf opening for larger vehicles. eg Jacksons Fencing Height restriction barrier in black
- Timber knee rail:
0.6m high timber knee rail e.g Jackson Fencing wooden knee rail fencing (or similar approved)

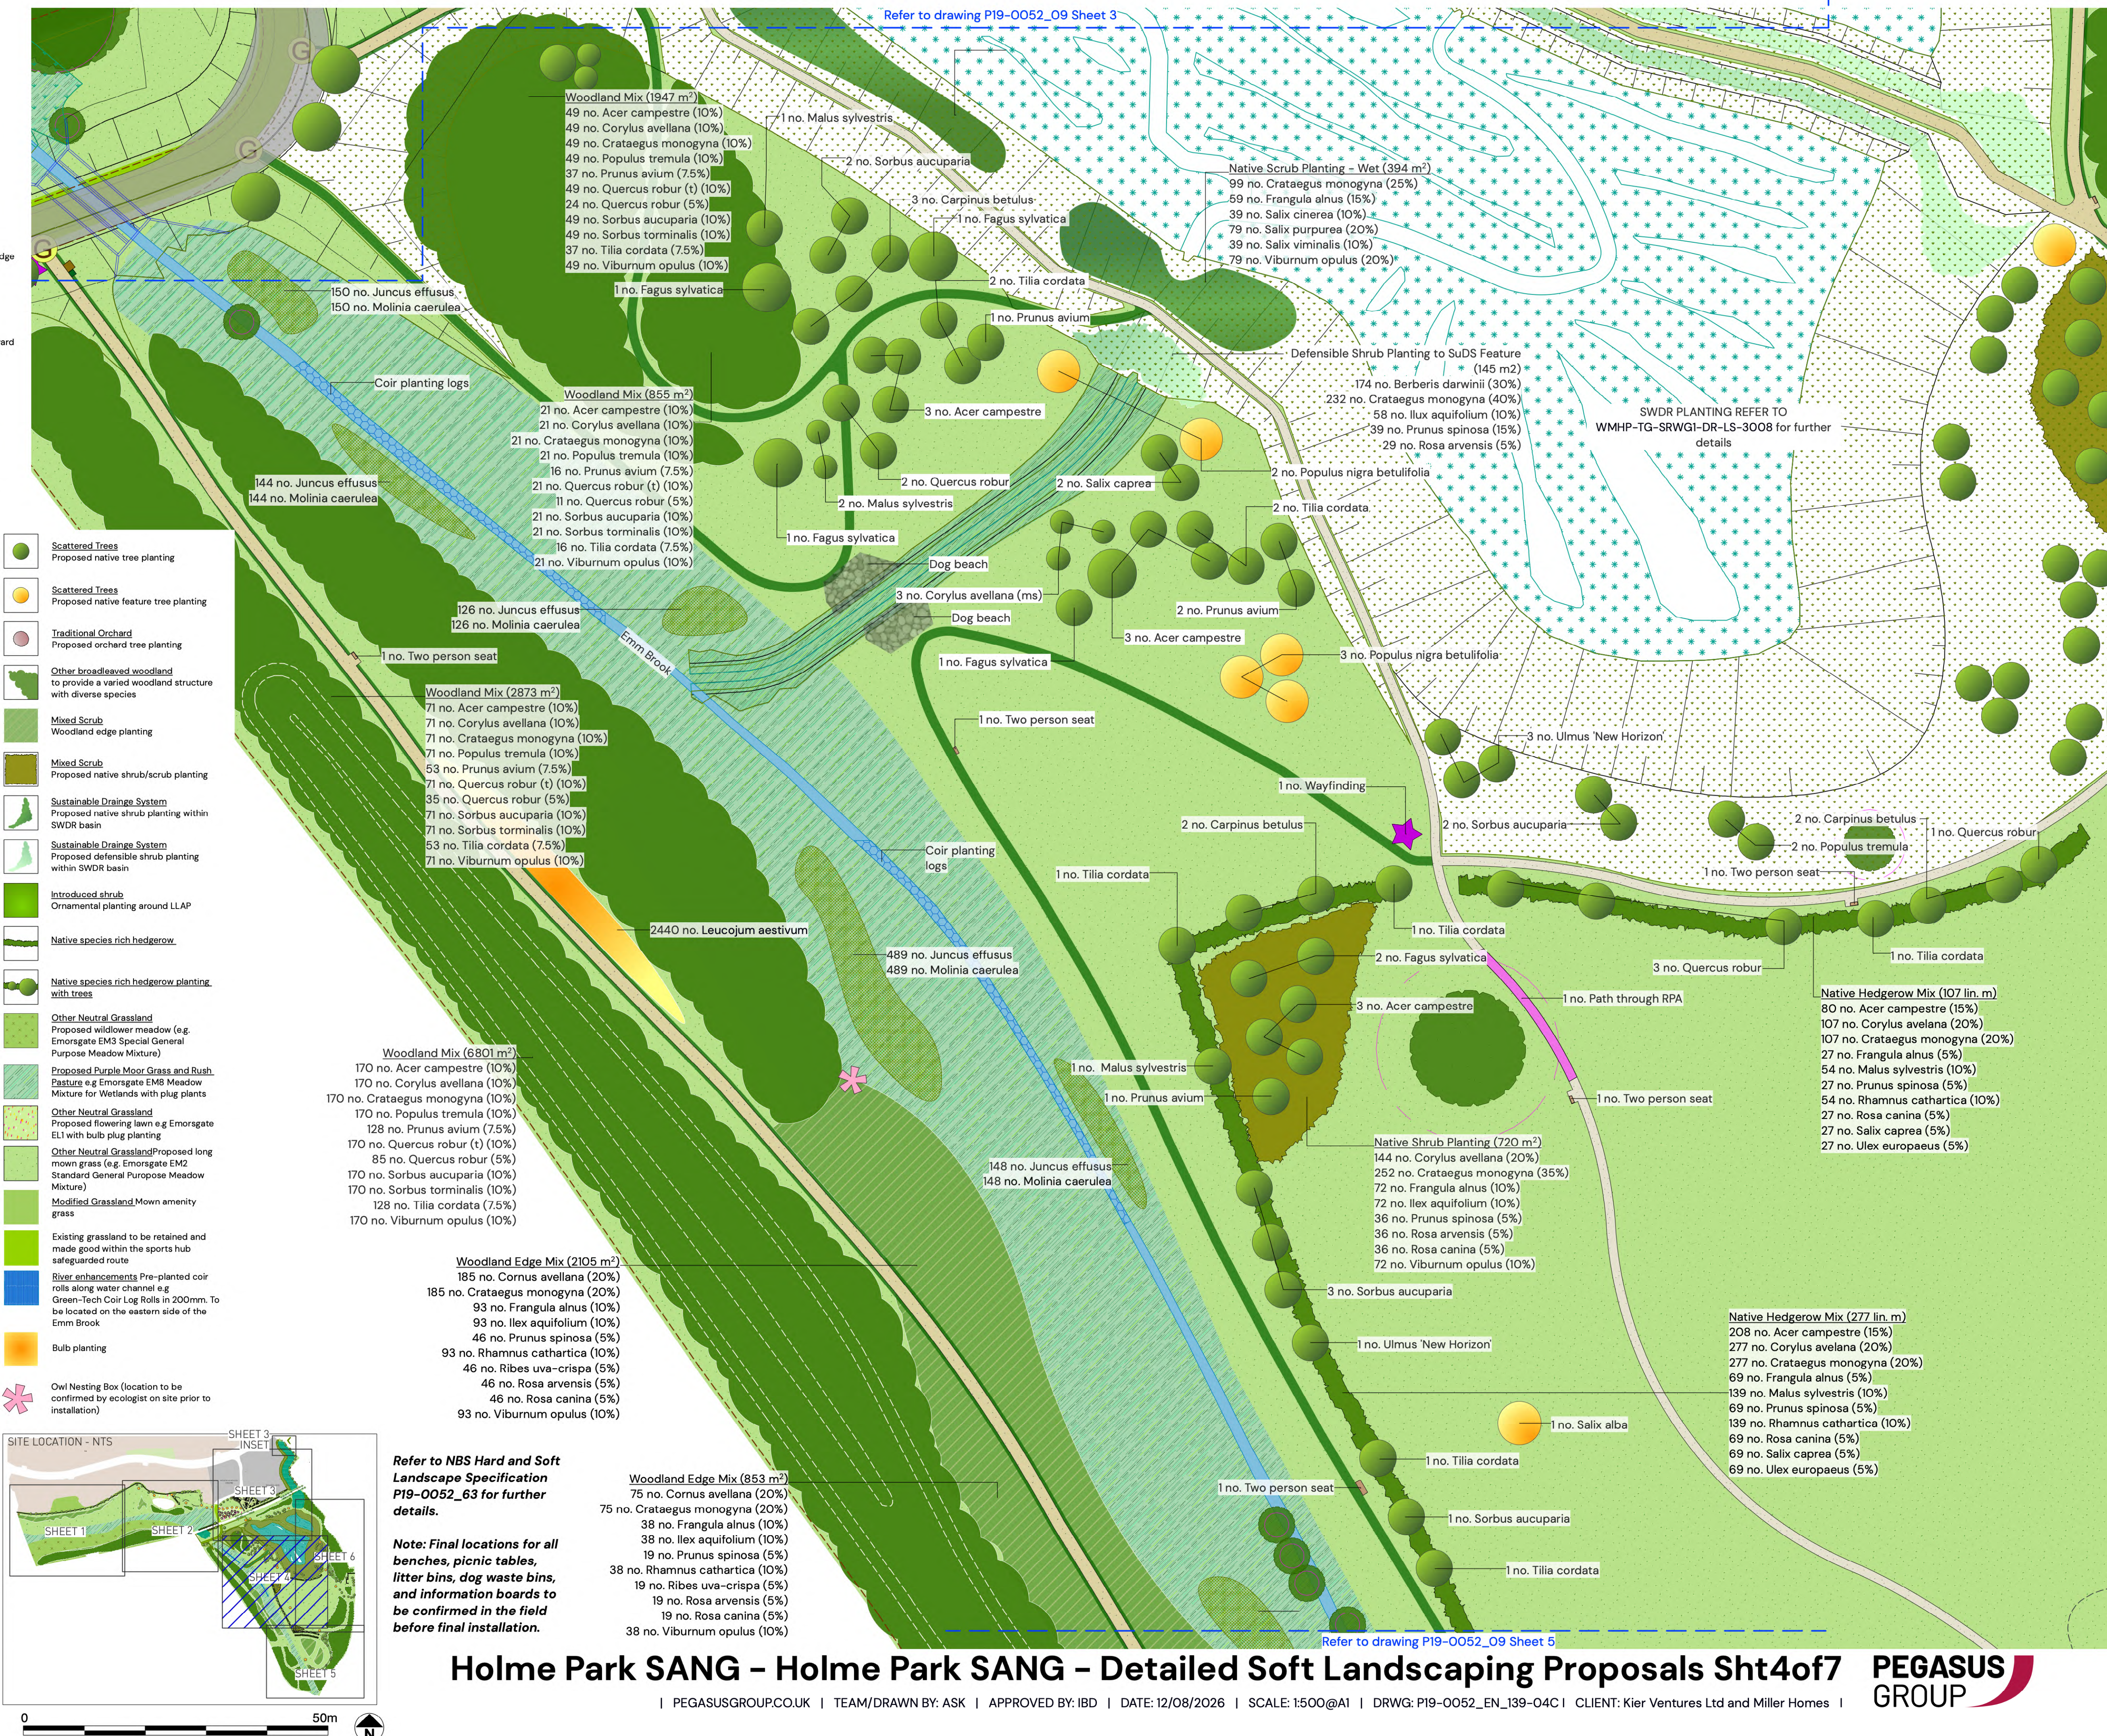

Refer to NBS Hard and Soft Landscape Specification P19-0052_63 for further details.

Note: Final locations for all benches, picnic tables, litter bins, dog waste bins, and information boards to be confirmed in the field before final installation.

Holme Park SANG - Holme Park SANG - Detailed Soft Landscaping Proposals Sht4of7

PEGASUSGROUP.CO.UK | TEAM/DRAWN BY: ASK | APPROVED BY: IBD | DATE: 12/08/2026 | SCALE: 1:500@A1 | DRWG: P19-0052_EN_139-04C | CLIENT: Kier Ventures Ltd and Miller Homes |

PEGASUS GROUP

KEY

- Existing Vegetation to be retained with RPA's shown refer to ACD Drawings for further details
- Ancient Woodland (with 15m Woodland Buffer shown)
- Existing Emm Brook
- Existing Public Rights of Way
- Proposed SWDR planting - not to be counted towards BNG
- Formal circular route: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved), 2m wide with timber edgings with 0.5m wide mown grass edge
- Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved), 1.5m wide with timber edging
- Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved), 1.5m wide with no edgings. Length of footpath to come forward when sports hub is operational.
- East-West Pedestrian cycle route
3m wide flexible bonded aggregate footpath e.g KBI Flexistone in Cappuccino (or similar approved) Flexistone to form edging.
- Informal mown path / mown path edges: Formed by regular mowing. 1m wide with no edging.
- Path through Ancient Woodland: Refer to detail on sheet 2 for pedestrians and in-frequent vehicular maintenance access. 2.5m wide no dig footpath (e.g cellweb) within root protection area to be timber edged filled with breedon angular chippings in golden amber (or similar approved)
- Path through root protection areas: Refer to detail on sheet 2 for pedestrians 2m wide no dig footpath (e.g cellweb) within root protection area to be timber edged to be filled with breedon angular chippings in golden amber (or similar approved)
- Boardwalk ramp to bridges
Hardwood timber boardwalks to provide ramp to bridges. To be 2m or 3.6m wide to match the bridge crossing width. Refer to technical drawings A389-ANG-III - I14 for further details.
- Pedestrian crossing point (2 no):
2m wide - each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards with anti-slip inserts to form tread. Handrails to each side - to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III - I14 for further details.
- Maintenance/pedestrian crossing point (2 no):
3.6m wide to allow maintenance vehicles to cross- each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards to form tread. Handrails to each side - to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III - I14 for further details.
- Timber litter bin: (6 no.)
I20L Okehampton Redwood litter bin, Broxap (BX17 4030), bolt down fixing (or similar approved)
- Dog waste bin: (6 no.)
40L Sirius dog waste bin, Broxap (BX45 2591-PM) in Moss Green (RA 6005) to be root fixed (or similar approved)
- Picnic Bench and Table (9 no.)
Cheshunt 6 person (CHS 4), bolt down fixing (or similar approved)
- Seat: (18 no.)
Cheshunt seat with backrest 2 person (CHS4), bolt down fixing (or similar approved)
- Welcome/Information Board: (3 no.)
Timber information board with map and information about the SANG e.g Musketeer twin leg wooden lectern supplied by Fitzpatrick Woolmer or similar approved. To be installed with submersed fixings set into concrete footings as per manufacturer's specification. Content to be confirmed and agreed with WBC prior to installation
- Play Space Information Board: (3 no.)
Aluminium information board to be fixed to playground fencing near to gates with information to be agreed with WBC prior to installation
- Wayfinding: (10 no.)
Timber finger posts showing distances and direction to points of interest within and outside of the SANG such as play spaces, neighbourhood centre, neighbouring SANG and walking routes. eg Timber waymarker supplied by Woodscape or similar approved. To be engraved with painted lettering. To be set in concrete footings. Content to be confirmed and agreed with WBC prior to installation
- Public Art (4no.)
Details of design and location to be confirmed in line with the public art strategy.
- Mounding:
Earth mounding, maximum height 1m with a maximum 1:4 gradients
- Dog Beach:
Area of gravel with gentle gradient to allow easy access for dogs to water
- Gateway Feature: (1no.)
Design to be confirmed in consultation with Ludgrove School


Boundary treatments

- Dog Proof Fencing:
1.2m high post and rail fence with mesh
- Kissing gate: (12 no.) For pedestrians, pushchairs and wheelchairs
Timber with self-closing mechanism, to be fitted with agricultural wire fencing stock eg Jackson Fencing Mobility Kissing Gate 1.5m wide (or similar approved)
- Field gate and access: (3 no.)
Timber field gate for maintenance access, 3.6m wide, 1.2m high (with lock) and self-closing pedestrian access gate 1.5m wide, 1.2m high. Both gates are to be fitted with agricultural wire fencing stock.
- Fence to Play Space:
Timber playground fencing eg Jackson Wooden Playground Fencing (or similar approved) 1.05m high with natural finish.
- Gate to Play Space: (3no.)
Timber play gate with steel frame eg Jackson Fencing Playtime Gate (or similar approved) inward opening with self closing operation with natural finish to timber gate and powder coating to steel frame.
- Height Restriction Barrier (1no.)
2.1m high height restrictor barrier 6m wide with single leaf opening for larger vehicles. eg Jacksons Fencing Height restriction barrier in black
- Timber knee rail:
0.6m high timber knee rail e.g Jackson Fencing wooden knee rail fencing (or similar approved)

- Scattered Trees
Proposed native tree planting
- Scattered Trees
Proposed native feature tree planting
- Traditional Orchard
Proposed orchard tree planting
- Other broadleaved woodland
to provide a varied woodland structure with diverse species
- Mixed Scrub
Woodland edge planting
- Mixed Scrub
Proposed native shrub/scrub planting
- Sustainable Drainage System
Proposed native shrub planting within SWDR basin
- Sustainable Drainage System
Proposed defensible shrub planting within SWDR basin
- Introduced shrub
Ornamental planting around LLAP
- Native species rich hedgerow
- Native species rich hedgerow planting with trees
- Other Neutral Grassland
Proposed willowher meadow (e.g. Emorsgate EM3 Special General Purpose Meadow Mixture)
- Proposed Purple Moor Grass and Rush
Pasture e.g Emorsgate EM8 Meadow Mixture for Wetlands with plug plants
- Other Neutral Grassland
Proposed flowering lawn e.g Emorsgate EL1 with bulb plug planting
- Other Neutral Grassland
Proposed long mown grass (e.g. Emorsgate EM2 Standard General Purpose Meadow Mixture)
- Modified Grassland Mown amenity grass
- Existing grassland to be retained and made good within the sports hub safeguarded route
- River enhancements Pre-planted coir rolls along water channel e.g Green-Tech Coir Log Rolls in 200mm. To be located on the eastern side of the Emm Brook
- Bulb planting

Refer to NBS Hard and Soft Landscape Specification P19-0052_63 for further details.

Note: Final locations for all benches, picnic tables, litter bins, dog waste bins, and information boards to be confirmed in the field before final installation.

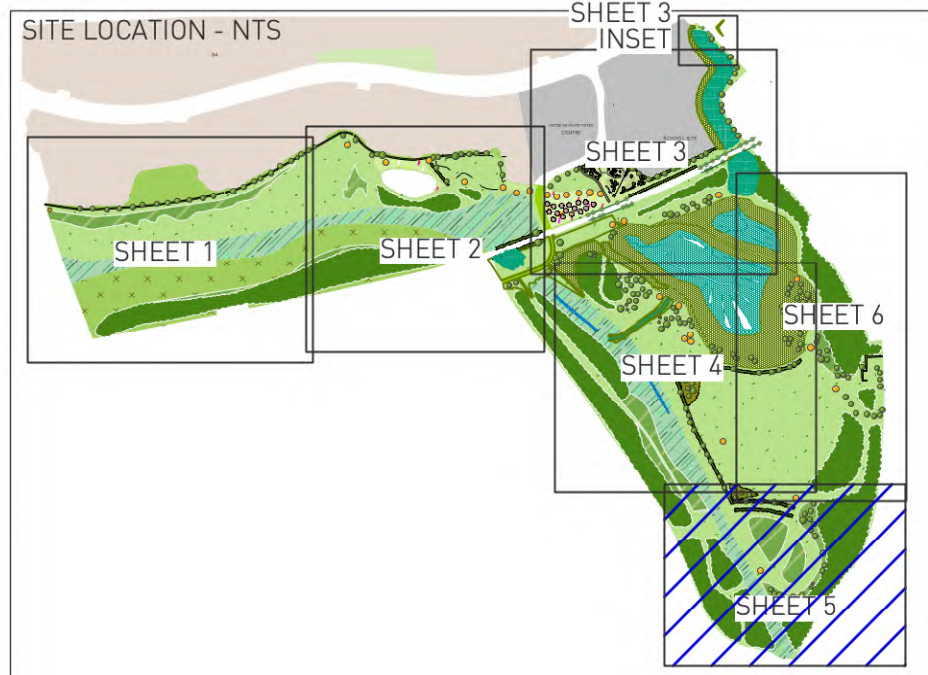

Holme Park SANG – Holme Park SANG – Detailed Soft Landscaping Proposals Sht5of7

| PEGASUSGROUP.CO.UK | TEAM/DRAWN BY: ASK | APPROVED BY: IBD | DATE: 12/08/2026 | SCALE: 1:500@A1 | DRWG: P19-0052_EN_139-05C | CLIENT: Kier Ventures Ltd and Miller Homes |



KEY



- Existing Vegetation to be retained with RPA's shown refer to ACD Drawings for further details
- Ancient Woodland (with 15m Woodland Buffer shown)
- Existing Emmn Brook
- Existing Public Rights of Way
- Proposed SWDR planting – not to be counted towards BNG
- Formal circular route: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved). 2m wide with timber edgings with 0.5m wide mown grass edge
- Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved). 1.5m wide with timber edging
- Informal surfaced footpath: For pedestrians
Compacted self binding 'Breedon Golden Amber' gravel (or similar approved). 1.5m wide with no edgings. Length of footpath to come forward when sports hub is operational.
- East-West Pedestrian cycle route
3m wide flexible bonded aggregate footpath e.g KBI Flexistone in Cappuccino (or similar approved) Flexistone to form edging.
- Informal mown path / mown path edges: Formed by regular mowing. 1m wide with no edging.
- Path through Ancient Woodland: Refer to detail on sheet 2 for pedestrians and in-frequent vehicular maintenance access. 2.5m wide no dig footpath (e.g cellweb) within root protection area to be timber edged filled with breedon angular chippings in golden amber (or similar approved)
- Path through root protection areas: Refer to detail on sheet 2 for pedestrians 2m wide no dig footpath (e.g cellweb) within root protection area to be timber edged to be filled with breedon angular chippings in golden amber (or similar approved)
- Boardwalk ramp to bridges
Hardwood timber boardwalks to provide ramp to bridges. To be 2m or 3.6m wide to match the bridge crossing width. Refer to technical drawings A389-ANG-III – II4 for further details.
- Pedestrian crossing point (2 no.):
2m wide – each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards with anti-slip insets to form tread. Handrails to each side – to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III – II4 for further details.
- Maintenance/pedestrian crossing point (2 no.):
3.6m wide to allow maintenance vehicles to cross – each bridging point to consist of steel girders spanning crossing set on concrete foundation with hardwood timber decking boards to form tread. Handrails to each side – to consist of vertical posts attached to steel girder with 3 horizontal rails. Refer to technical drawings A389-ANG-III – II4 for further details.
- Timber litter bin: (6 no.)
120L Okehampton Redwood litter bin, Broxap (BX17 4030), bolt down fixing (or similar approved)
- Dog waste bin: (6 no.)
40L Sirius dog waste bin, Broxap (BX45 2591-PM) in Moss Green (RA 6005) to be root fixed (or similar approved)
- Picnic Bench and Table (9 no.)
Cheshunt 6 person (CHS 4), bolt down fixing (or similar approved)
- Seat: (18 no.)
Cheshunt seat with backrest 2 person (CHS4), bolt down fixing (or similar approved)
- Welcome/Information Board: (3 no.)
Timber information board with map and information about the SANG, e.g. Musketeer twin leg wooden lectern supplied by Fitzpatrick Woolmer or similar approved. To be installed with submerged fixings set into concrete footings as per manufacturer's specification. Content to be confirmed and agreed with WBC prior to installation
- Play Space Information Board: (3 no.)
Aluminium information board to be fixed to playground fencing near to gates with information to be agreed with WBC prior to installation
- Wayfinding: (10 no.)
Timber finger posts showing distances and direction to points of interest within and outside of the SANG such as play spaces, neighbourhood centre, neighbouring SANG and walking routes. eg Timber waymarker supplied by Woodscape or similar approved. To be engraved with painted lettering. To be set in concrete footings. Content to be confirmed and agreed with WBC prior to installation
- Public Art (4no.)
Details of design and location to be confirmed in line with the public art strategy.
- Mounding:
Earth mounding, maximum height 1m with a maximum 1:4 gradients
- Dog Beach:
Area of gravel with gentle gradient to allow easy access for dogs to water
- Gateway Feature: (1 no.)
Design to be confirmed in consultation with Ludgrove School

Boundary treatments

- Dog Proof Fencing:
1.2m high post and rail fence with mesh
- Kissing gate: (12 no.) For pedestrians, pushchairs and wheelchairs
Timber with self-closing mechanism, to be fitted with agricultural wire fencing stock eg Jackson Fencing Mobility Kissing Gate 1.5m wide (or similar approved)
- Field gate and access: (3 no.)
Timber field gate for maintenance access, 3.6m wide, 1.2m high (with lock) and self-closing pedestrian access gate 1.5m wide, 1.2m high. Both gates are to be fitted with agricultural wire fencing stock.
- Fence to Play Space:
Timber playground fencing eg Jackson Wooden Playground Fencing (or similar approved) 1.05m high with natural finish.
- Gate to Play Space: (3no.)
Timber play gate with steel frame eg Jackson Fencing Playtime Gate (or similar approved) inward opening with self closing operation with natural finish to timber gate and powder coating to steel frame.
- Height Restriction Barrier (1no.)
2.1m high height restrictor barrier 6m wide with single leaf opening for larger vehicles. eg Jacksons Fencing Height restriction barrier in black
- Timber knee rail:
0.8m high timber knee rail e.g Jackson Fencing wooden knee rail fencing (or similar approved)
- Scattered Trees
Proposed native tree planting
- Scattered Trees
Proposed native feature tree planting
- Traditional Orchard
Proposed orchard tree planting
- Other broadleaved woodland
to provide a varied woodland structure with diverse species
- Mixed Scrub
Woodland edge planting
- Mixed Scrub
Proposed native shrub/scrub planting
- Sustainable Drainage System
Proposed native shrub planting within SWDR basin
- Sustainable Drainage System
Proposed defensible shrub planting within SWDR basin
- Introduced shrub
Ornamental planting around LLAP
- Native species rich hedgerow
Proposed long mown grass (e.g. Emorsgate EM2 Standard General Purpose Meadow Mixture)
- Native species rich hedgerow planting with trees
Modified Grassland: Mown amenity grass
- Other Neutral Grassland
Proposed wildflower meadow (e.g. Emorsgate EM3 Special General Purpose Meadow Mixture).
- Proposed Purple Moor Grass and Rush.
Pasture e.g Emorsgate EM6 Meadow Mixture for Wetlands with plug plants
- Other Neutral Grassland
Proposed flowering lawn e.g Emorsgate EL1 with bulb plug planting
- Existing grassland to be retained and made good within the sports hub safeguarded route
- River enhancements
Pre-planted coir rolls along water channel e.g Green-Tech Coir Log Rolls in 200mm. To be located on the eastern side of the Emmn Brook

Refer to NBS Hard and Soft Landscape Specification
P19-0052_63 for further details.

Note: Final locations for all benches, picnic tables, litter bins, dog waste bins, and information boards to be confirmed in the field before final installation.

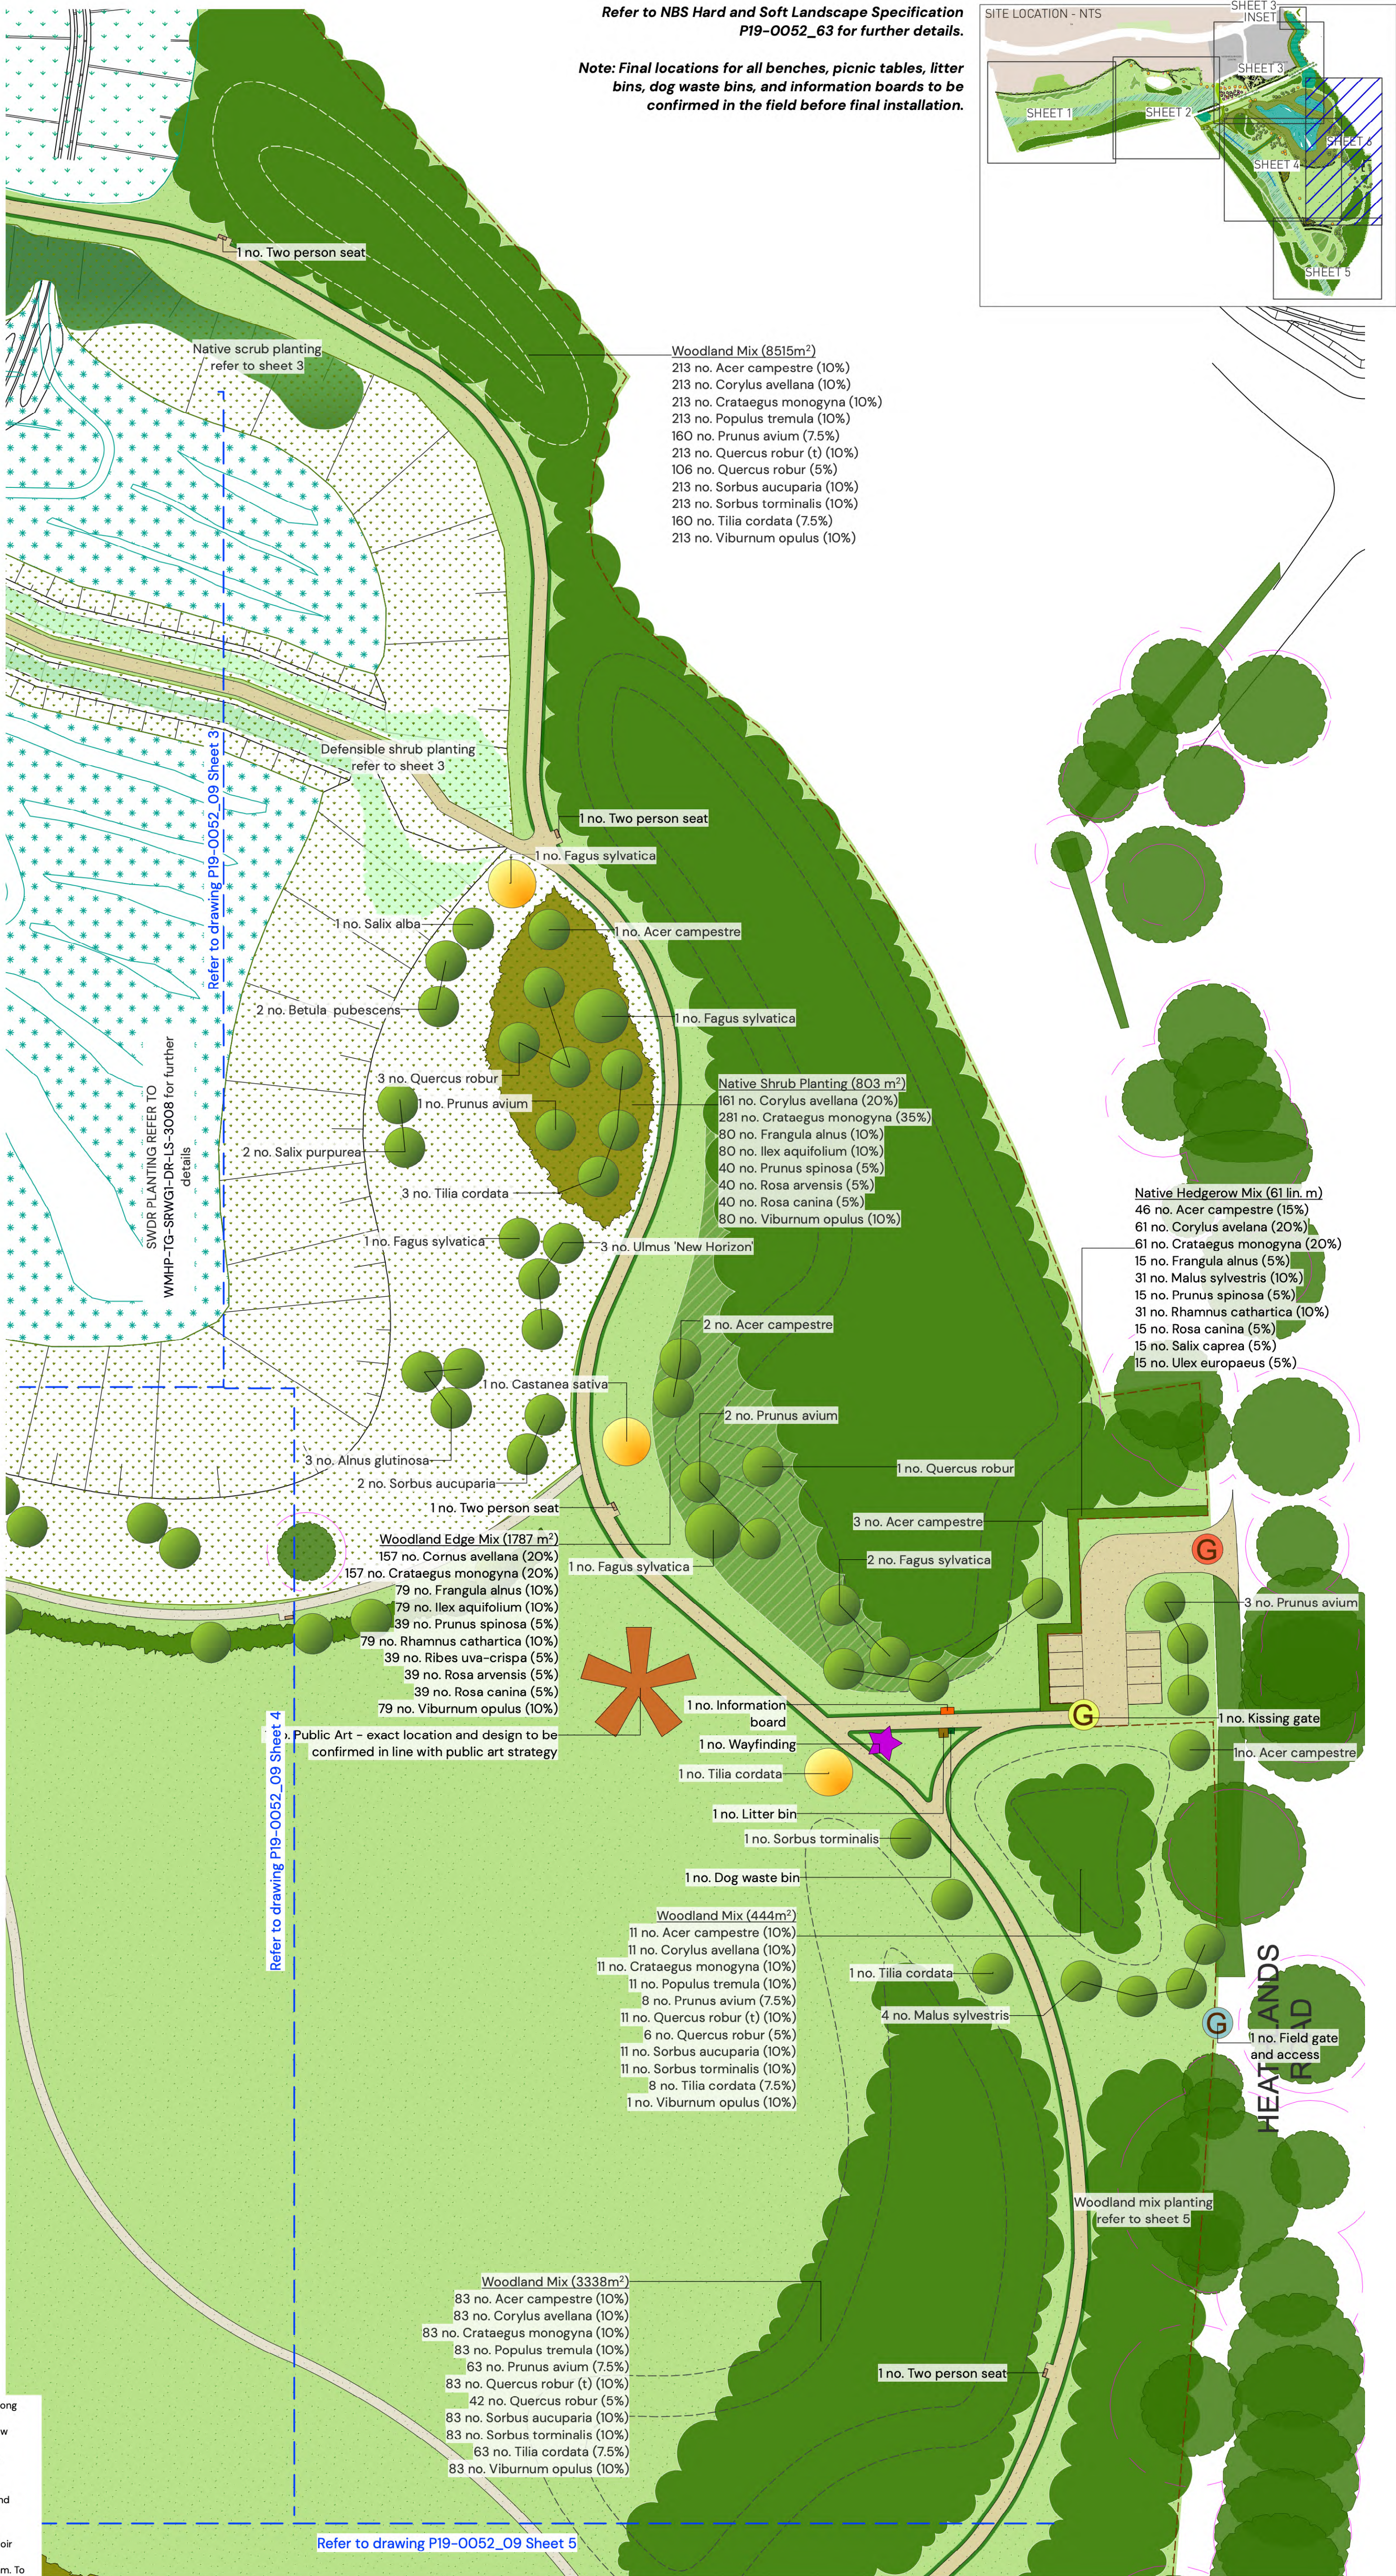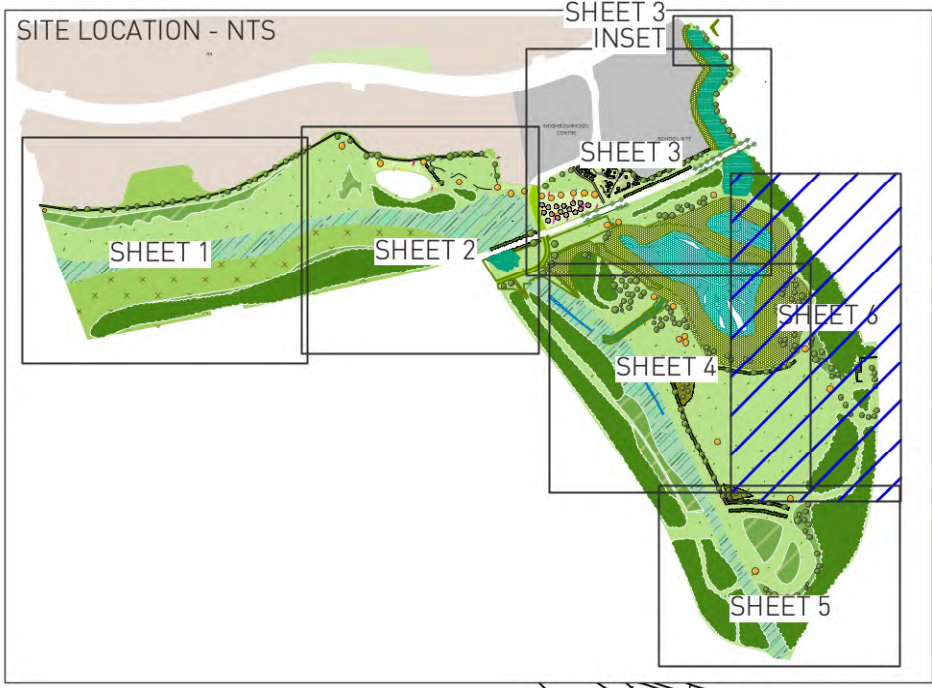

Phase 2B SANG Planting Schedule

Tree Planting

Species	Form	Girth cm	Height (cm)	Clear Stem (cm)	Root Condition
Acer campestre	EHS	14-16	425-600	Min. 200	RB
Alnus glutinosa	EHS	14-16	400-450	Min 200	RB
Betula pubescens	EHS	14-16	400-450	175-200	RB
Carpinus betulus	EHS	14-16	425-600	Min. 200	RB
Castanea sativa	EHS	14-16	400-450	175-200	RB
Corylus avellana (ms)	Multi-Stem	-	250-300	-	RB
Fagus sylvatica	EHS	14-16	425-600	Min. 200	RB
Malus sylvestris	EHS	14-16	425-600	Min. 200	RB
Populus nigra betulifolia	EHS	14-16	425-600	175-200	RB
Populus tremula	EHS	14-16	425-600	175-200	RB
Prunus avium	EHS	14-16	425-600	Min. 200	RB
Quercus robur	EHS	14-16	400-450	175-200	RB
Salix alba	EHS	18-20	450-500	Min 200	RB
Salix caprea	EHS	14-16	400-450	175-200	RB
Salix purpurea	Feathered	-	200-250	-	B
Sorbus aucuparia	EHS	14-16	425-600	Min. 200	RB
Sorbus torminalis	EHS	14-16	400-450	Min 200	RB
Tilia cordata	EHS	14-16	400-450	175-200	RB
Ulmus 'New Horizon'	EHS	14-16	400-450	175-200	RB

Orchard Tree Planting

Species	Form	Girth cm	Height (cm)	Clear Stem	Root Condition
Malus 'Breedon Pippin'	Half Standard	6-8cm	150-200	175-200	B
Malus 'Charles Ross'	Standard	8-10cm	200-250	175-200	B
Malus 'John Downie'	EHS	14-16	425-600	175-200	B
Malus 'Millers Seedling'	Standard	8-10cm	200-250	175-200	B
Pyrus communis 'Stinking Bishop'	Half Standard	6-8cm	150-200	175-200	B
Pyrus communis 'Williams'	Half Standard	6-8cm	150-200	175-200	B
Pyrus communis 'Winter Nellis'	Half Standard	6-8cm	150-200	175-200	B

Woodland Edge Mix – to be planted at 1.5m spacing (0.44/m²)

Species	Mix Percentage %	Height (cm)	Form	Root Condition
Corylus avellana	20	60-80	Branched	B
Crataegus monogyna	20	60-80	Branched	B
Frangula alnus	20	60-80	Leader with laterals	B
Ilex aquifolium	10	60-80	Leader with laterals	3L C
Prunus spinosa	5	60-80	Branched	B
Rhamnus cathartica	10	60-80	Leader with laterals	B
Ribes uva-crispa	5	30-40	Branched	B
Rosa arvensis	5	40-60	Branched	B
Rosa canina	5	40-60	Branched	B
Viburnum opulus	10	60-80	Branched	B

Woodland Mix – to be planted at 2m spacing (0.25/m²)

Species	Mix Percentage %	Height (cm)	Form	Root Condition
Acer campestre	10	250-300	Feathered	B
Corylus avellana	10	60-80	Branched	B
Crataegus monogyna	10	40-60	Seedling	B
Populus tremula	10	40-60	Seedling	B
Prunus avium	7.5	40-60	Transplant	B
Quercus robur	10	125-150	Transplant	B
Quercus robur	5	250-300	Feathered	15L C
Sorbus aucuparia	10	250-300	Standard	B
Sorbus torminalis	10	200-250	Feathered	B
Tilia cordata	7.5	200-250	Feathered	B
Viburnum opulus	10	80-100	Branched	B

Native Hedgerow Mix – to be planted at 5/linear m, to be planted in double staggered rows, 500mm apart, at 400m centres

Species	Mix Percentage %	Height (cm)	Form	Root Condition
Acer campestre	15	60-80	Whip/Feather	2L C
Corylus avellana	20	100-125	Branched	RB
Crataegus monogyna	20	60-80	Seedling	B
Frangula alnus	5	60-80	Leader with laterals	B
Malus sylvestris	10	60-80	Transplant	B
Prunus spinosa	5	60-80	Branched	B
Rhamnus cathartica	10	60-80	Leader with laterals	B
Rosa canina	5	60-80	Branched	B
Salix caprea	5	60-80	Branched	B
Ulex europaeus	5	30-40	Bushy	3L

Native Shrub Planting – to be planted at 2/m²

Species	Mix Percentage %	Height (cm)	Age	Form	Root Condition
Corylus avellana	20	60-80	1+2	Branched	3L C
Crataegus monogyna	35	60-80	1+1	Branched	B
Frangula alnus	10	60-80	1+1	Branched	B
Ilex aquifolium	10	60-80	-	Leader with Laterals	3L C
Prunus spinosa	5	60-80	1+1	Branched	B
Rosa arvensis	5	60-80	1+1	Branched	3L C
Rosa canina	5	40-60	1+1	Branched	B
Viburnum opulus	10	60-80	1+2	Branched	B

Defensible Shrub Planting to SuDS Feature – to be planted at 4/m²

Species	Mix Percentage %	Height (cm)	Age	Form	Root Condition
Berberis darwinii	30	60-80	-	Bushy; 8 breaks	B
Crataegus monogyna*	40	60-80	1+1	Branched	B
Ilex aquifolium	10	60-80	1+1	Leader w/ laterals	7.5L
Prunus spinosa	15	60-80	1+1	Branched	B
Rosa arvensis	5	60-80	1+1	Branched	B

*Denotes species suitable for seasonal immersion within the attenuation basins. Species marked with * are to be planted along the lower slopes of the basins.

Native Scrub Planting (Wet)– to be planted at 1/m²

Species	Mix Percentage %	Height (cm)	Age	Form	Root Condition
Crataegus monogyna	25	60-80	1+1	Branched	B
Frangula alnus	15	60-80	1+1	Branched	B
Salix cinerea	10	60-80	0+1	Branched	B
Salix purpurea	20	60-80	0+1	Branched	B
Salix viminalis	10	60-80	0+1	Branched	B
Viburnum opulus	20	60-80	1+2	Branched	B

Other Neutral Grassland (wildflower meadow)

Emorsgate Seed Mix EM3 – Special General Purpose Meadow Mixture (sown at 4g/m²)

%	Latin Name	Common Name
Wildflowers		
0.5	Achillea millefolium	Yarrow
0.6	Betonica officinalis	Betony
2.5	Centaurea nigra	Common Knapweed
0.8	Centaurea scabiosa	Greater Knapweed
1	Daucus carota	Wild Carrot
0.6	Filipendula ulmaria	Meadowsweet
0.6	Galium album	Hedge Bedstraw
2	Galium verum	Lady's Bedstraw
0.4	Knautia arvensis	Field Scabious
0.3	Leontodon hispidus	Rough Hawkbit
0.6	Leucanthemum vulgare	Oxeye Daisy
0.5	Lotus corniculatus	Birdsfoot Trefoil
0.1	Origanum vulgare	Wild Marjoram
0.5	Plantago media	Hoary Plantain
1	Poterium sanguisorba	Salad Burnet
0.4	Primula veris	Cowslip
2	Prunella vulgaris	Selfheal
2.5	Ranunculus acris	Meadow Buttercup
1	Rhinanthus minor	Yellow Rattle
0.6	Rumex acetosa	Common Sorrel
1.2	Silene dioica	Red Campion
0.2	Silene flos-cuculi	Ragged Robin
0.1	Trifolium pratense	Wild Red Clover
20		
Grasses		
8	Agrostis capillaris	Common Bent
40	Cynosurus cristatus	Crested Dogstail
28	Festuca rubra	Slender-creeping Red-fescue
4	Phleum bertolonii	Smaller Cat's-tail
80		

Purple Moor Grass and Rush Pasture

Emorsgate Seed Mix EM8 –Meadow Mixture for Wetlands (Mixture to be sown at a rate of 4g/m2.

%	Latin Name	Common Name
Wildflowers (20%)		
2	Achillea millefolium	Yarrow
0.6	Agrimonia eupatoria	Agrimony
3.6	Centaurea nigra	Common Knapweed
1	Filipendula ularia	Meadowsweet
2	Galium verum	Lady's Bedstraw
0.2	Geum rivale	Water avens
0.5	Lathyrus pratensis	Meadow Vetchling
0.1	Leontodon hispidus	Rough Hawkbit
1.2	Leucanthemum vulgare	Oxeye Daisy (Moon Daisy)
0.1	Lotus corniculatus	Birdsfoot Trefoil
0.4	Lotus pendunculatus	Greater Birdsfoot Trefoil
3.2	Plantago lanceolata	Ribwort Plantain
0.2	Primula veris	Cowslip
0.1	Prunella vulgaris	Selfheal
0.4	Ranunculus acris	Meadow Buttercup
1.4	Rhinanthus minor	Yellow Rattle
1.2	Rumex acetosa	Common Sorrel
1	Sanguisorba officinalis	Great Burnet
0.3	Silene flos-cuculi	Ragged Robin
0.1	Succisa pratensis	Devil's-bit Scabious
0.4	Vicia cracca	Tufted Vetch
Grasses (80%)		
4	Agrostis capillaris	Common Bent (w)
4	Anthoxanthum odoratum	Sweet Vernal-grass (w)
2	Carex divulsa ssp divulsa	Grey Sedge (w)
38.4	Cynosurus cristatus	Crested Dogstail
1.6	Deschampsia cespitosa	Tufted Hair-grass (w)
20	Festuca rubra	Red Fescue
4	Hordeum secalinum	Meadow Barley (w)
8	Poa trivialis	Rough-stalked Meadowgrass
2.4	Schedonorus arundinaceus	Tall Fescue

Soft Rush – To be planted 3/m²

Latin Name	Common Name
Juncus effusus	Soft Rush

River Enhancements

Pre-planted coir rolls (planted at 6m²)

Latin Name	Common Name
Phragmites australis	Norfolk reed
Phalaris arundinacea	Reed canary grass
Glyceria maxima	Reed sweet grass
Iris pseudacorus	Yellow Flag
Lythrum salicaria	Purple Loosestrife
Carex riparia	Greater pond sedge
Carex acutiformis	Lesser pond sedge
Juncus effusus	Soft rush

Other Neutral Grassland (Long Grass)

Emorsgate EG1 General Purpose Meadow Grass Mixture (sown at 5g/m2)

%	Species	Common Name
10	Agrostis capillaris	Common Bent
35	Cynosurus cristatus	Crested Dogstail
30	Festuca rubra	Red Fescue
5	Phleum bertolonii	Smaller Cat's-tail
20	Poa pratensis	Smooth-stalked Meadow-grass

Other Neutral Grassland (Flowering Lawn with bulb planting)

EMORSGATE EM2 STANDARD GENERAL PURPOSE MEADOW MIXTURE

Example seed mix (exact mix to be specified by ecologist to suit site conditions) containing species that characteristic of traditional meadows across a wide range of soil types.

Mixture to be sown at a rate of 4g/m2.

%	Latin Name	Common Name
Wildflowers (15%)		
0.75	Achillea millefolium	Yarrow
0.3	Agrimonia eupatoria	Agrimony
1.5	Centaurea nigra	Common Knapweed
0.9	Daucus carota	Wild Carrot
1.5	Galium verum	Lady's Bedstraw
0.45	Knautia arvensis	Field Scabious
1.27	Leucanthemum vulgare	Oxeye Daisy
1.8	Malva moschata	Muck Mallow
1.8	Plantago lanceolata	Ribwort Plantain
0.9	Poterium sanguisorba ssp sanguisorba	Salad Burnet
0.3	Primula veris	Cowslip
0.75	Ranunculus acris	Meadow Buttercup
0.98	Rhinanthus minor	Yellow Rattle
0.3	Rumex acetosa	Common Sorrel
1.5	Silene dioica	Red Campion
Grasses (85%)		
8.5	Agrostis capillaris	Common Bent (w)
29.75	Cynosurus cristatus	Crested Dogstail
25.5	Festuca rubra	Red-Fescue
4.25	Phleum bertolonii	Smaller Cat's-tail (w)
17	Poa pratensis	Smooth-Stalked Meadow-grass

Bulb Planting – to be planted at 10/m2

Species	Bulb Size
Fritillaria meleagris	
Galanthus nivalis	Grade 4/5
Leucojum aestivum	

Refer to NBS Hard and Soft Landscape Specification P19-0052_63 for further details

Play Specification

- (A) Timber play totem/sculpture


- (B) Stainless steel tower slide with wave (on mound) - Jupiter Play (FHS-Holztechnik) Age: 3 - 10 years


- (C) Climbing log (on mound) Jupiter Play (FHS-Holztechnik) Age: from 3 years


- (D) Scramble net (on mound) Jupiter Play (FHS-Holztechnik) Age: from 3 years


- (E) Climbing Ramp (on mound) Russell Play (Spielart) Age: from 3 years


- (F) Fiberglass Play Boulder - Lil' Buddy and Ever-Rest Climber (colour - brown) Nicos Age: from 3 years


- (G) Varioset Freising Jupiter Play (FHS-Holztechnik) Age: from 6 years


- (H) Triple-spring bouncing disk Jupiter Play (FHS-Holztechnik) Age: from 4 - 10 years


- (I) Zigzag balancing Bridge Jupiter Play (FHS-Holztechnik) Age: from 5 - 12 years


- (J) Slide platform (on mound) Russell Play (Spielart) Age: 3 - 10 years


- (K) Play structure Immenstadt (on mound) Russell Play (Spielart) Age: 3 - 10 years



- (L) Spring-mounted rocker beam Jupiter Play (FHS-Holztechnik) Age: from 3 - 12 years


- (M) Nest Swing Frame Jupiter Play (FHS-Holztechnik) Age: from 3 years


- (N) Underground Tunnel Fahr Industries Ltd Age: from 2 years


- (O) Willow dome Handmade places Age: from 3 years



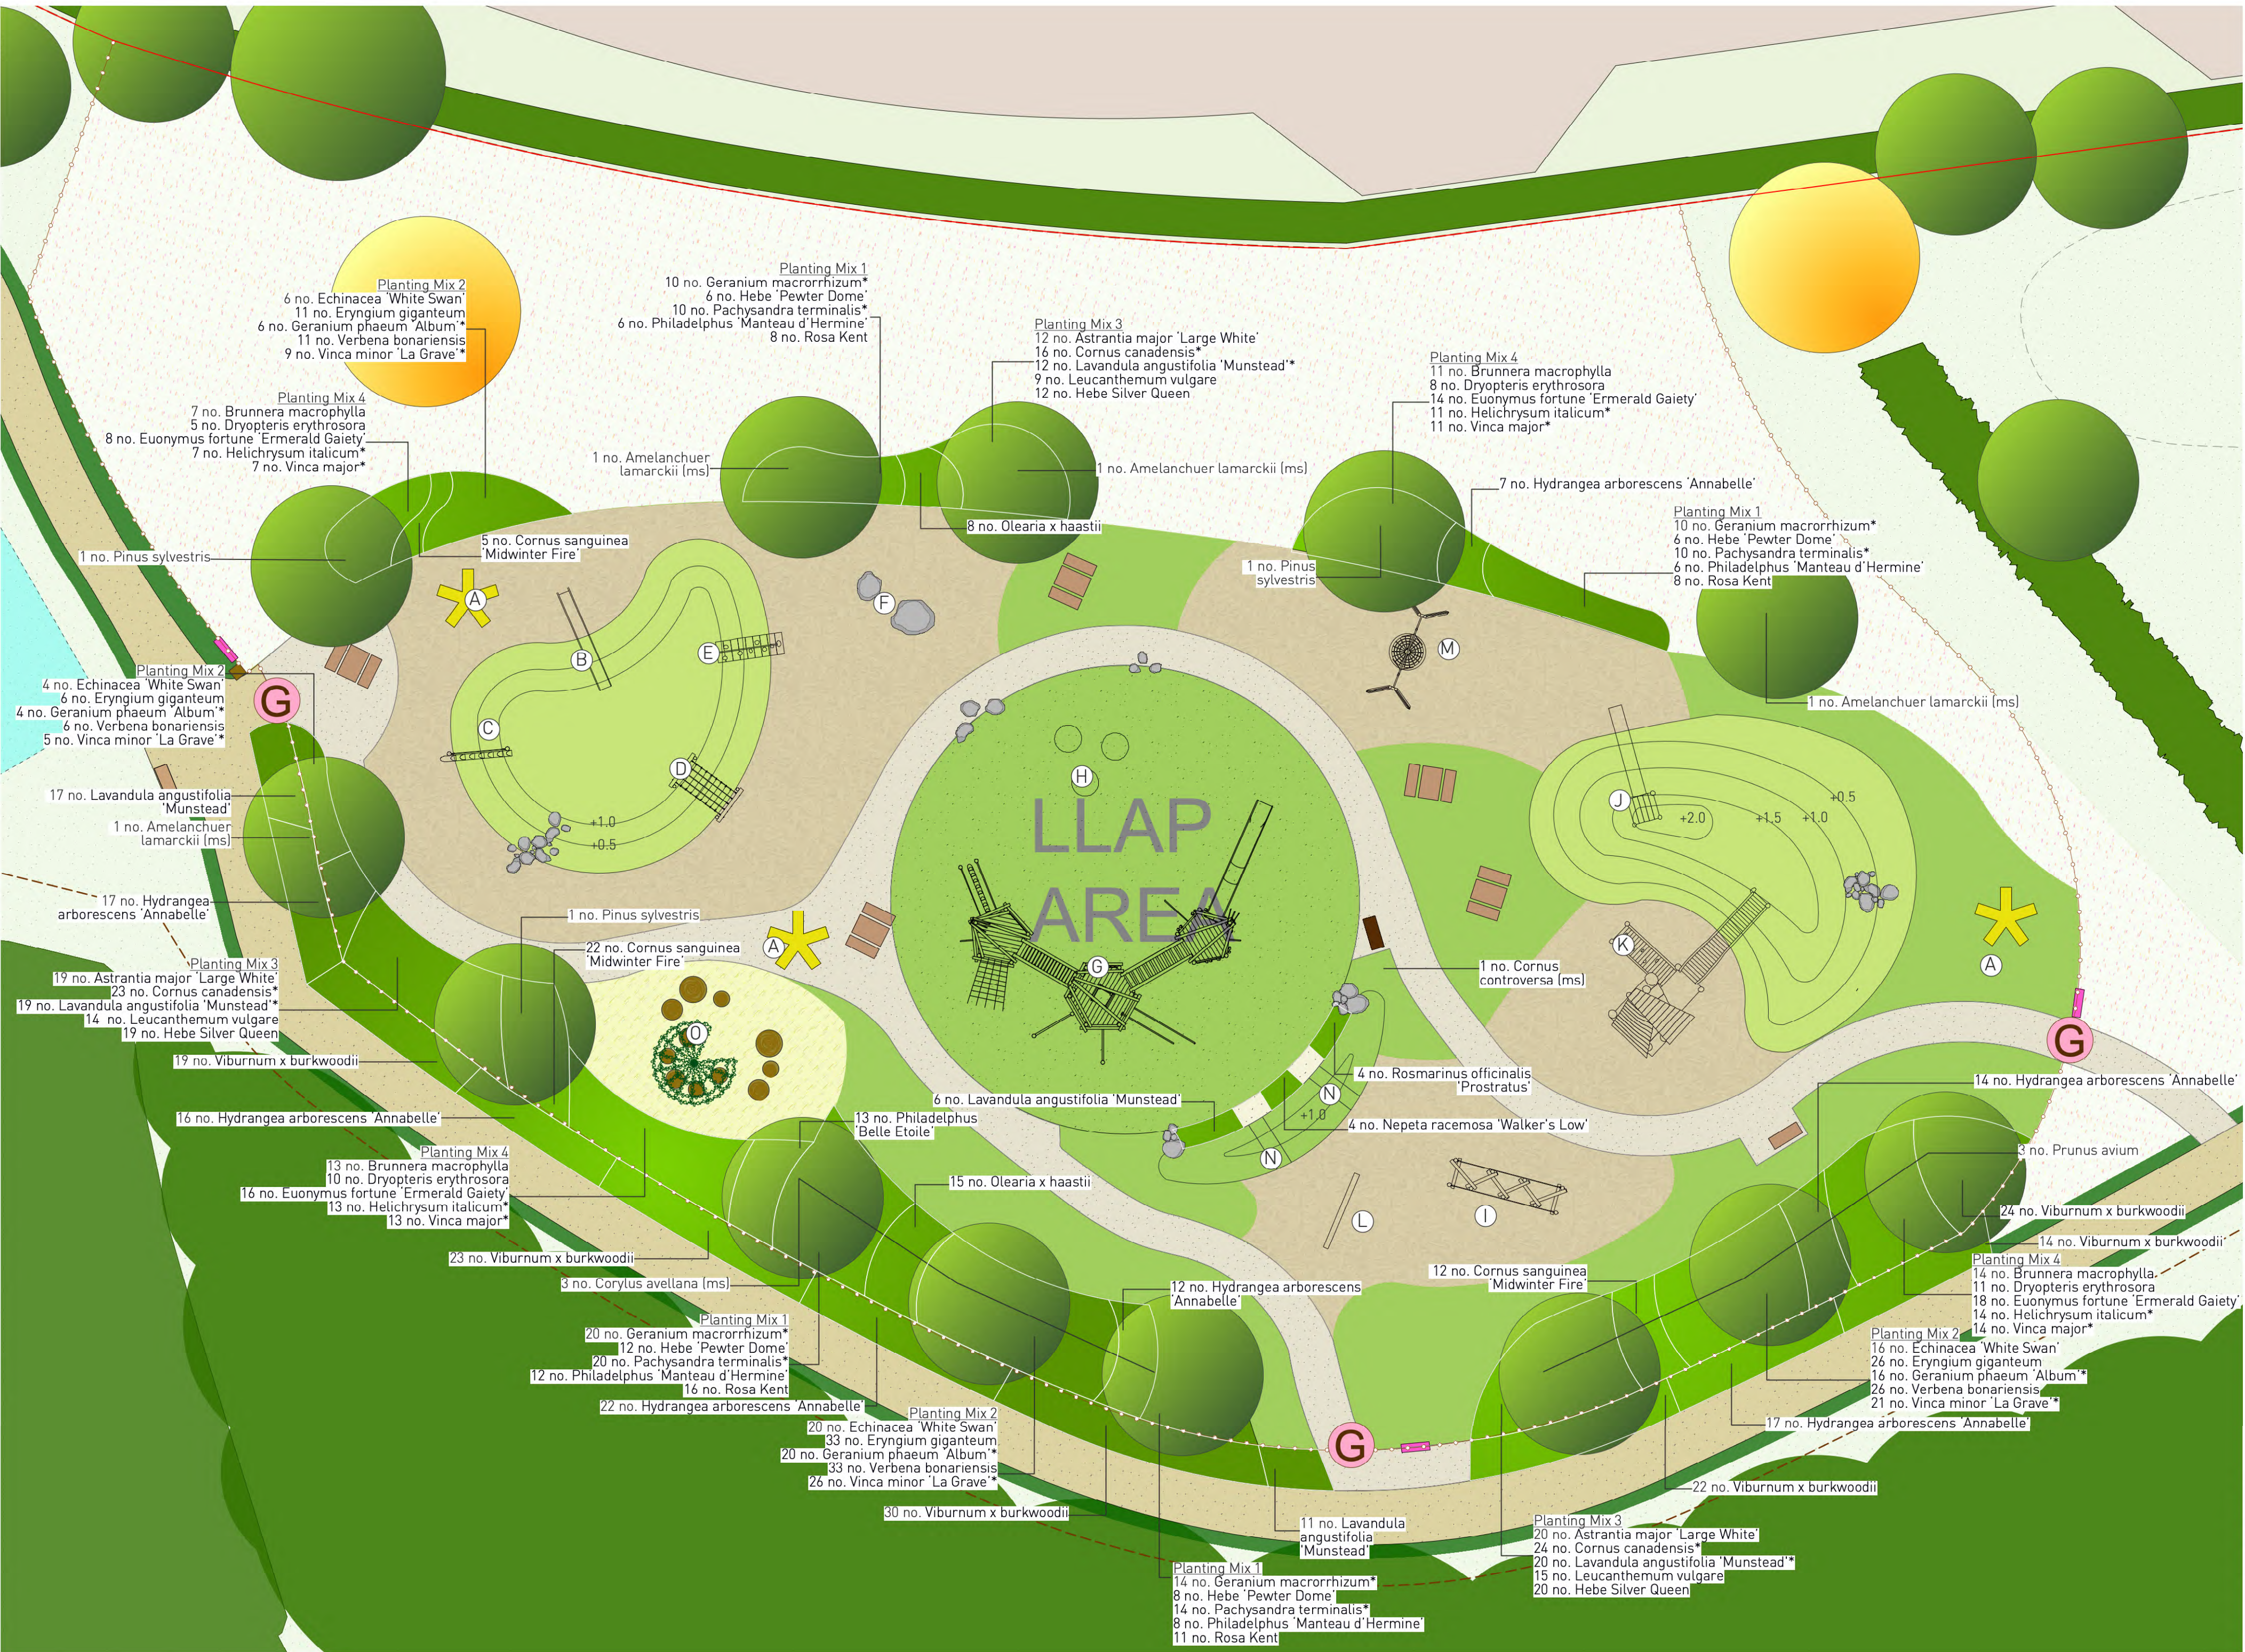

- KEY**
- Proposed scattered trees
 - Introduced shrub
Ornamental planting around LLAP
 - Modified Grassland
Mown amenity grass
 - Formal circular route - 2m wide with timber edging - compacted self binding gravel 'Breedon Golden Amber' (or similar approved)
 - Proposed play equipment refer to play specification
 - Play Bark to comply with BS EN 1176. Installed to a suitable depth to cover critical fall height. Needs to be free draining with a geotextile membrane. e.g. Melcourt playbark or similar approved. To be edged with rubber border edging e.g. Rubber Kerb Playground Surface Edging by Online Playgrounds or similar approved
 - Play Sand to comply with BS EN 1176 and 71-3. Installed to a suitable depth to cover critical fall height. To be installed above layer of clean gravel and geotextile e.g. Melcourt playsand or similar approved with timber edging
 - Wetpour Safety Surfacing
Wetpour rubber playground safety surfacing in a green colour suitable for childrens play (e.g. RubbaSmart by Play Smart UK) and laid to the critical fall heights and extent as specified by the manufacturer. All play safety surfaces to be laid to BS EN1176 + BS EN 1177.
 - Grass Mound
with smooth flowing contours. Gradient to be a max 1:3 except where play equipment requires a localised steeper gradient
 - Play Boulders
To be naturally smooth or have a slightly rough surface with no sharp edges. Must not be slippery when wet. To be sustainably sourced - locally where possible. Location to provide suitable offset to fall height
 - Play log seats
To be locally sourced where possible, to be range of sizes between 200mm and 400mm width and 100mm and 300mm high.
 - Picnic Bench and Table
Cheshunt 6 person (CHS 4), bolt down fixing (or similar approved)
 - Fence to Play Space
Timber playground fencing eg Jackson Wooden Playground Fencing (or similar approved) 1.05m high with natural finish
 - Gate to Play Space
Timber play gate with steel frame eg Jackson Fencing Playtime Gate (or similar approved) inward opening with self closing operation with natural finish to timber gate and powder coating to steel frame.
 - Seat
Cheshunt seat 2 person with backrest (CHS 4), bolt down fixing (or similar approved)
 - Bench
Cheshunt bench 2 person (CHS B4), bolt down fixing (or similar approved)
 - Timber litter bin
120L Okehampton Redwood litter bin, Broxap (BX17 4030), bolt down fixing (or similar approved)
 - Play Space Information Board
Aluminium information board to be fixed to playground fencing near to gates with information (to be agreed with WBC prior to installation) for example:
 - Operational information (rules of the space)
 - Dogs to be kept on leads and no dog fouling
 - Name and telephone number of the operator of the facility with an invitation to report any incident or damage
- Refer to P19-0052_EN_139 for wider SANG hard and soft landscaping proposals**
Refer to NBS Hard and Soft Landscape Specification P19-0052_63 for further details
Note: Final locations for all benches, picnic tables, litter bins, dog waste bins, and information boards to be confirmed in the field before final installation. Content of information boards to be confirmed with WBC prior to installation.

Phase 2B LLAP Planting Schedule

Tree Planting

Species	Form	Girth cm	Height (cm)	Clear Stem (cm)	Root Condition
Amelanchier lamarckii (ms)	Multi-Stem	-	250-300	3 stems min	RB
Cornus controversa (ms)	Multi-Stem	-	400-450	-	RB
Corylus avellana (ms)	Multi-Stem	-	250-300	3 stems min	RB
Pinus sylvestris	EHF	-	250-300	-	RB
Prunus avium	EHF	14-16	425-600	Min. 200	RB

Semi-ornamental shrub and herbaceous planting - Mixes

Mix	Species	%	Height/spread	Habit	Root Condition	Density
1	Geranium macrorrhizum*	25	-	Full Pot	3L	4/m ²
	Hebe 'Pewter Dome'	15	20-30	Bushy	3L	
	Pachysandra terminalis*	25	15-30	Several Shoots	3L	
	Philadelphus 'Manteau d' Hermine'	15	30-40	Branched	3L	
	Rosa Kent	20	30-40	Bush	3L	
2	Echinacea 'White Swan'	15	-	Full Pot	3L	5/m ²
	Eryngium giganteum	25	-	Full Pot	3L	
	Geranium phaeum 'Album'	15	-	Full Pot	3L	
	Veronica bonariensis	25	-	Full Pot	3L	
	Vinca minor 'La Grave'	20	20-30	Several Shoots	3L	
3	Astrantia major 'Large White'	20	-	Full Pot	3L	5/m ²
	Cornus canadensis*	25	15-20	Several Shoots	3L	
	Leucanthemum vulgare	20	-	Full Pot	3L	
	Lavandula angustifolia 'Munstead'	15	20-30	Bushy	3L	
	Hebe Silver Queen	20	20-30	Bushy	3L	
4	Brunnera macrophylla	20	-	Full Pot	3L	4/m ²
	Dryopteris erythrosora	15	-	Full Pot	3L	
	Euonymus fortune 'Emerald Gaiety'	25	20-30	Bushy	3L	
	Helichrysum italicum*	20	20-30	Bushy	3L	
	Vinca major*	20	20-30	Several Shoots	3L	

*Species to be planted at edge of beds


Semi-ornamental shrub and herbaceous planting

Species	Height/spread	Habit	Root Condition	Density
Cornus sanguinea 'Midwinter Fire'	60-80	Branched	5L	2
Hydrangea arborescens 'Annabelle'	60-80	Branched	5L	2
Lavandula angustifolia 'Munstead'	20-30	Bushy	3L	3
Nepeta racemosa 'Walker's Low'	-	Full Pot	3L	4
Olearia x haastii	40-60	Bushy	5L	2
Philadelphus 'Belle Etoile'	40-60	Branched	5L	2
Rosemarinus officinalis 'Prostratus'	20-30	Bushy	3L	3
Viburnum x burkwoodii	20-30	Bushy	3L	3


Holme Park SANG - LLAP Detailed Landscape Proposals

| PEGASUSGROUP.CO.UK | TEAM/DRAWN BY: ASK | APPROVED BY: IBD | DATE: 12/08/2026 | SCALE: 1:150@A1 | DRWG: P19-0052_EN_145C | CLIENT: Kier Ventures Ltd and Miller Homes |



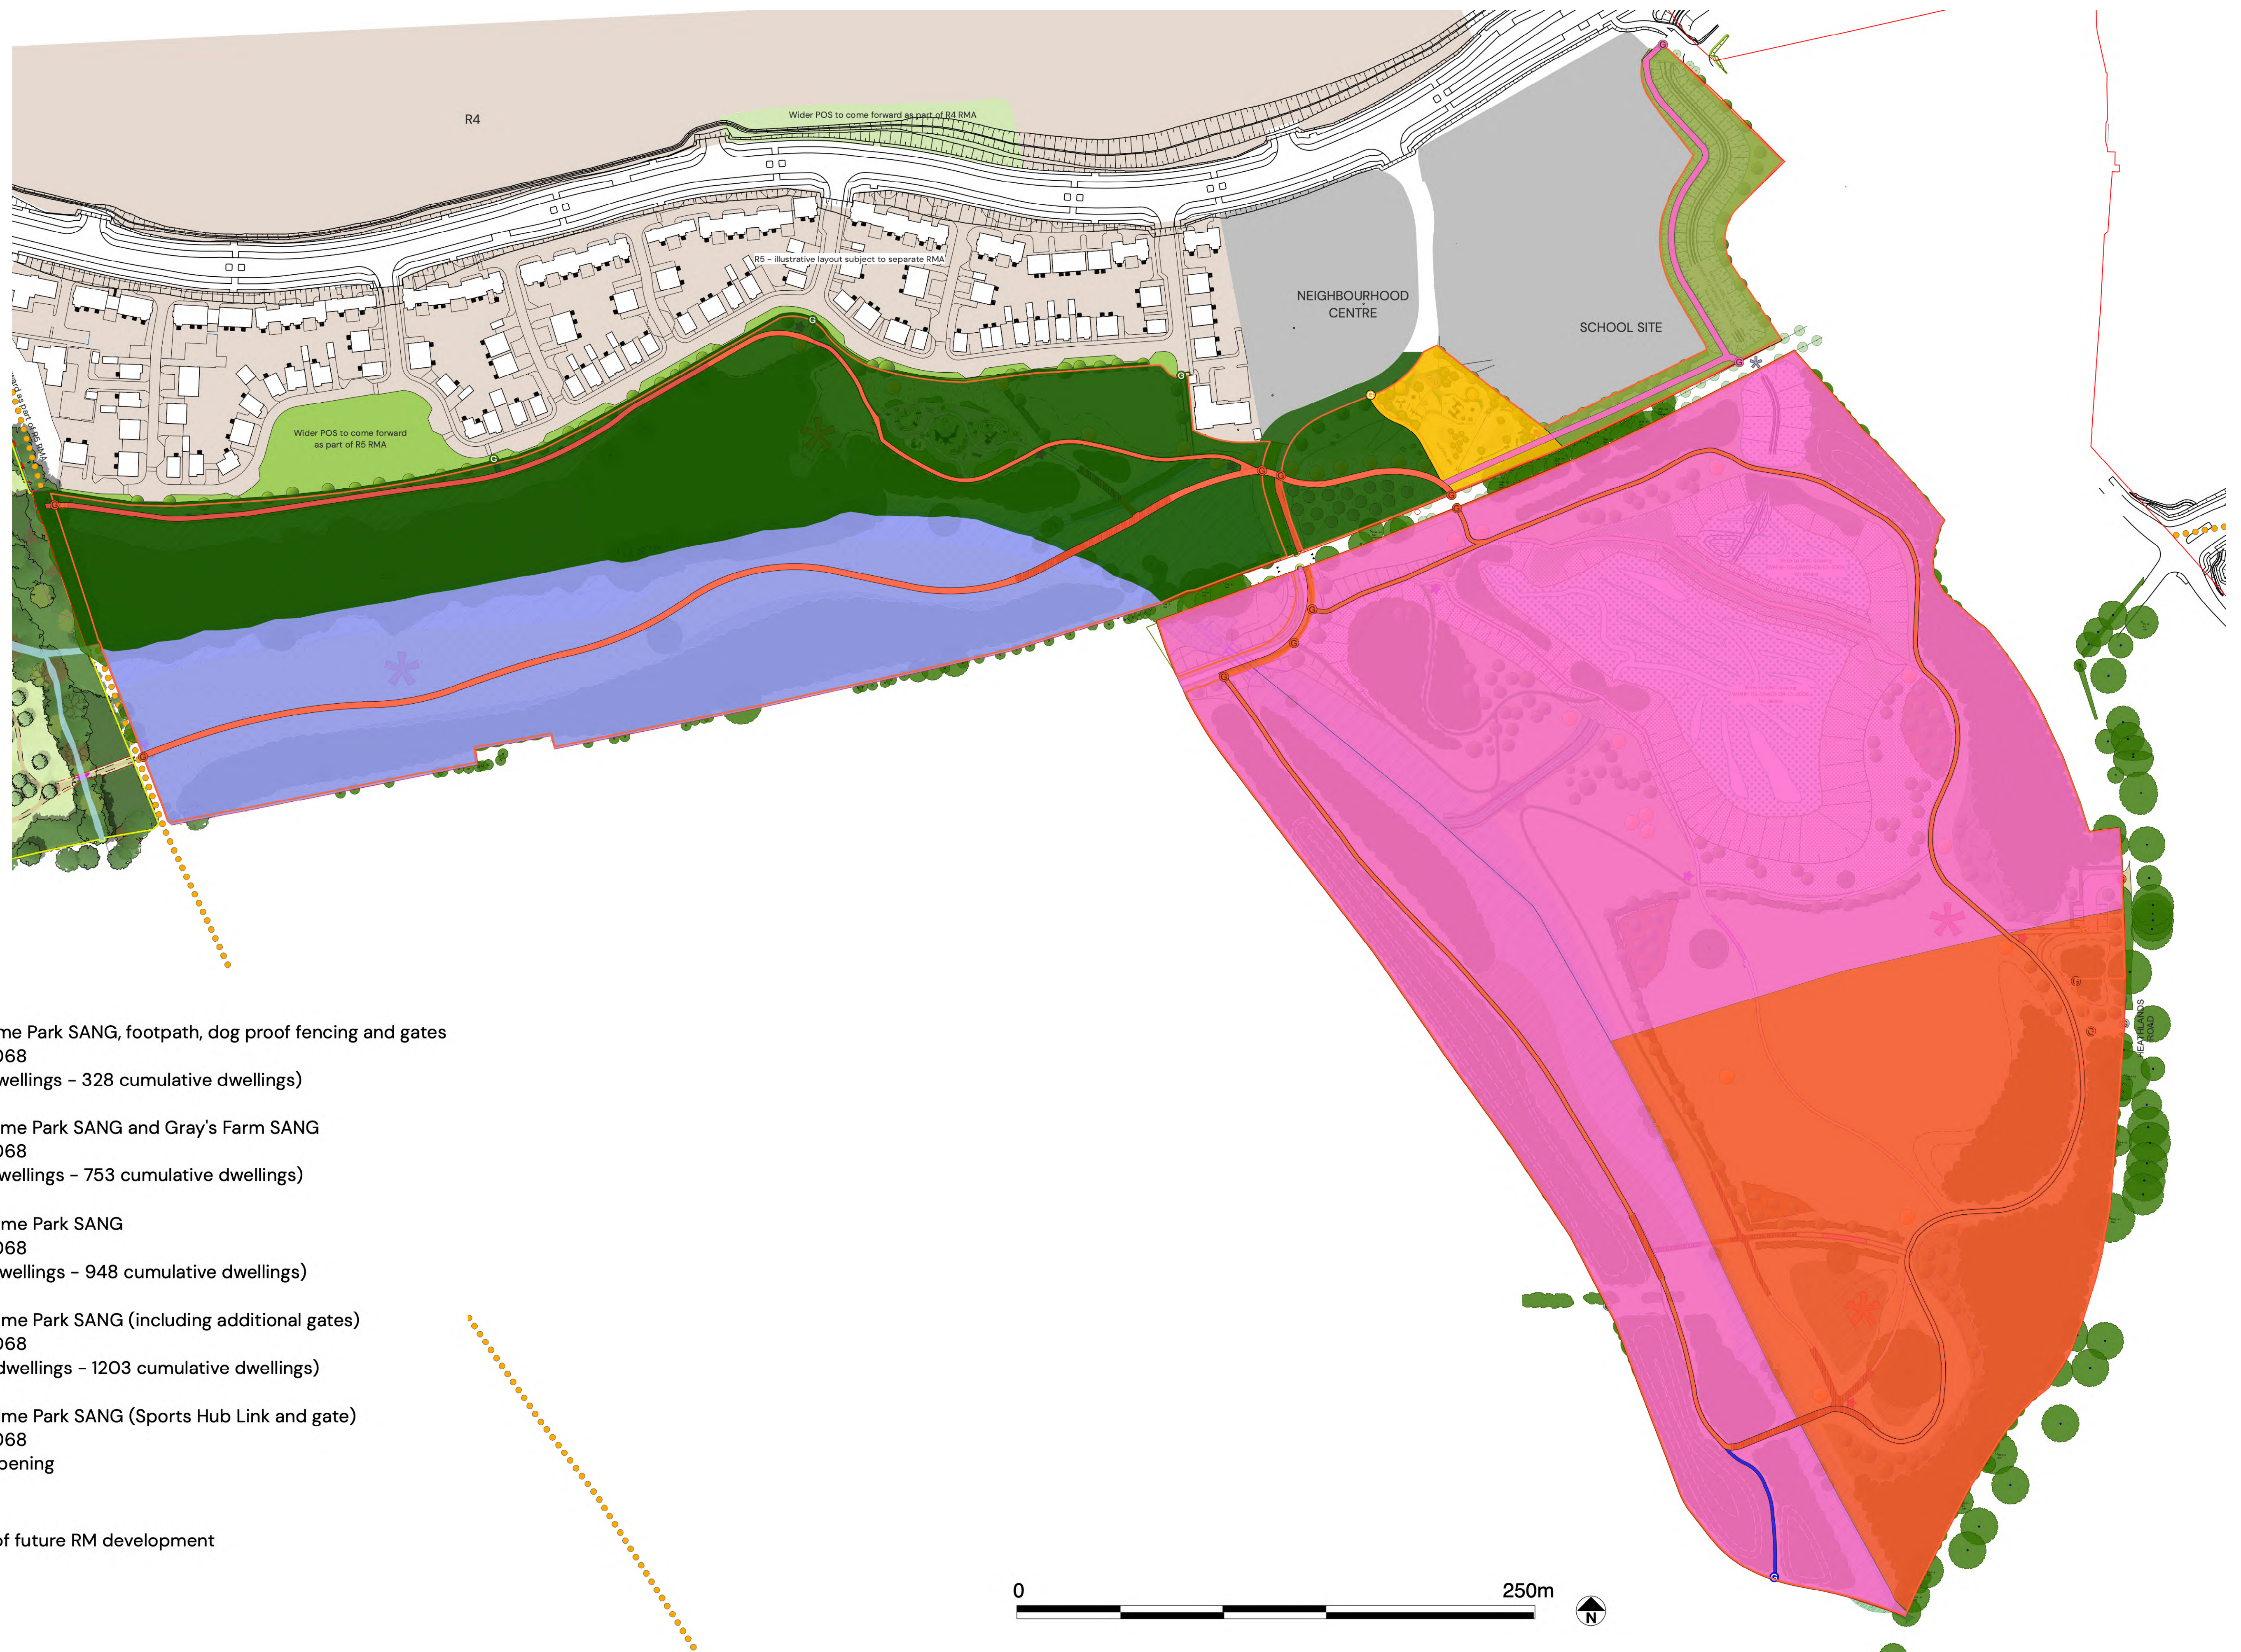

PHASING



Phase 1 – Holme Park SANG, footpath, dog proof fencing and gates
WBC Ref. 191068
4.6ha (240 dwellings – 328 cumulative dwellings)




Phase 2 – Holme Park SANG and Gray's Farm SANG
WBC Ref. 191068
8.17ha (425 dwellings – 753 cumulative dwellings)




Phase 3 – Holme Park SANG
WBC Ref. 191068
3.75ha (195 dwellings – 948 cumulative dwellings)



Phase 4 – Holme Park SANG (including additional gates)
WBC Ref. 191068
4.89ha (255 dwellings – 1203 cumulative dwellings)



Phase 5 – Holme Park SANG (Sports Hub Link and gate)
WBC Ref. 191068
Sports hub opening



NEAP – part of future RM development



NGS4

Holme Park SANG – Holme Park SANG Phasing Strategy

| PEGASUSGROUP.CO.UK | TEAM/DRAWN BY: ASK | APPROVED BY: ASK | DATE: 12/08/2026 | SCALE: 1:1500@ISO A1 | DRWG: P19-0052_EN_141B | CLIENT: Kier Ventures Ltd and Miller Homes |

