


## **Keep Hatch Primary School – Traffic Management Plan**

Site access located on: Ashridge Road, Wokingham RG40 1PG

The delivery vehicles with the modular units will approach the site from the A329M, London Road, Binfield Road, Keep Hatch Road, Hughes Road, Norrys Avenue & Ashridge Road. Access into site is via the gate and through the school car park.



Abnormal load escort vehicles will be used on the day of installation. These will escort the delivery vehicles from the A329M and into site.

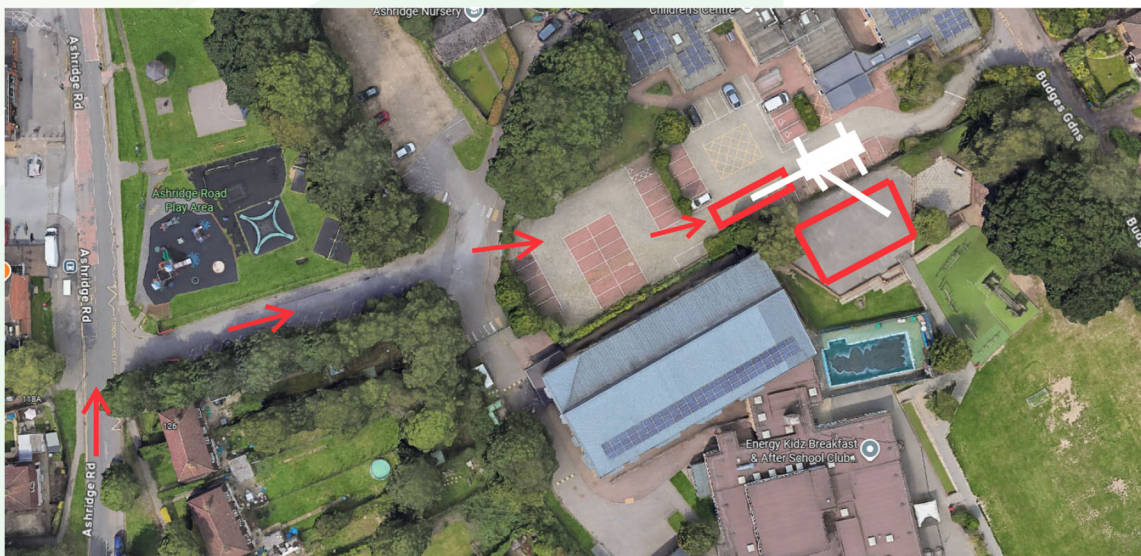

The modular buildings will travel on 700mm high step frame trailers. These will be pulled by tag axle tractor units as these are more manoeuvrable for the turn from Ashridge Road into the gate onto the school drive.

This route has been surveyed by the transport company and will be the specified route on the movement order.

The car parking spaces on the school drive do not pose a problem to the delivery vehicles as the drive is of sufficient width but it would be helpful if these were clear to avoid pedestrian/vehicle clashes. The car park for Brambles & Foundry School will need to be cleared due to the crane setting up in this area.

Delivery vehicles will drive through the site compound up to the crane for the modular building to be lifted off. Once empty, the trailers will be closed up allowing the vehicle to turn around and be driven out of site.

During the fit out & completion works for the building, all contractor vehicles will be parked within the site compound. The maximum number of vehicles on site during these works is expected to be around 6 and the compound is of sufficient size to accommodate these.



No vehicles will be parked outside the site compound.
