




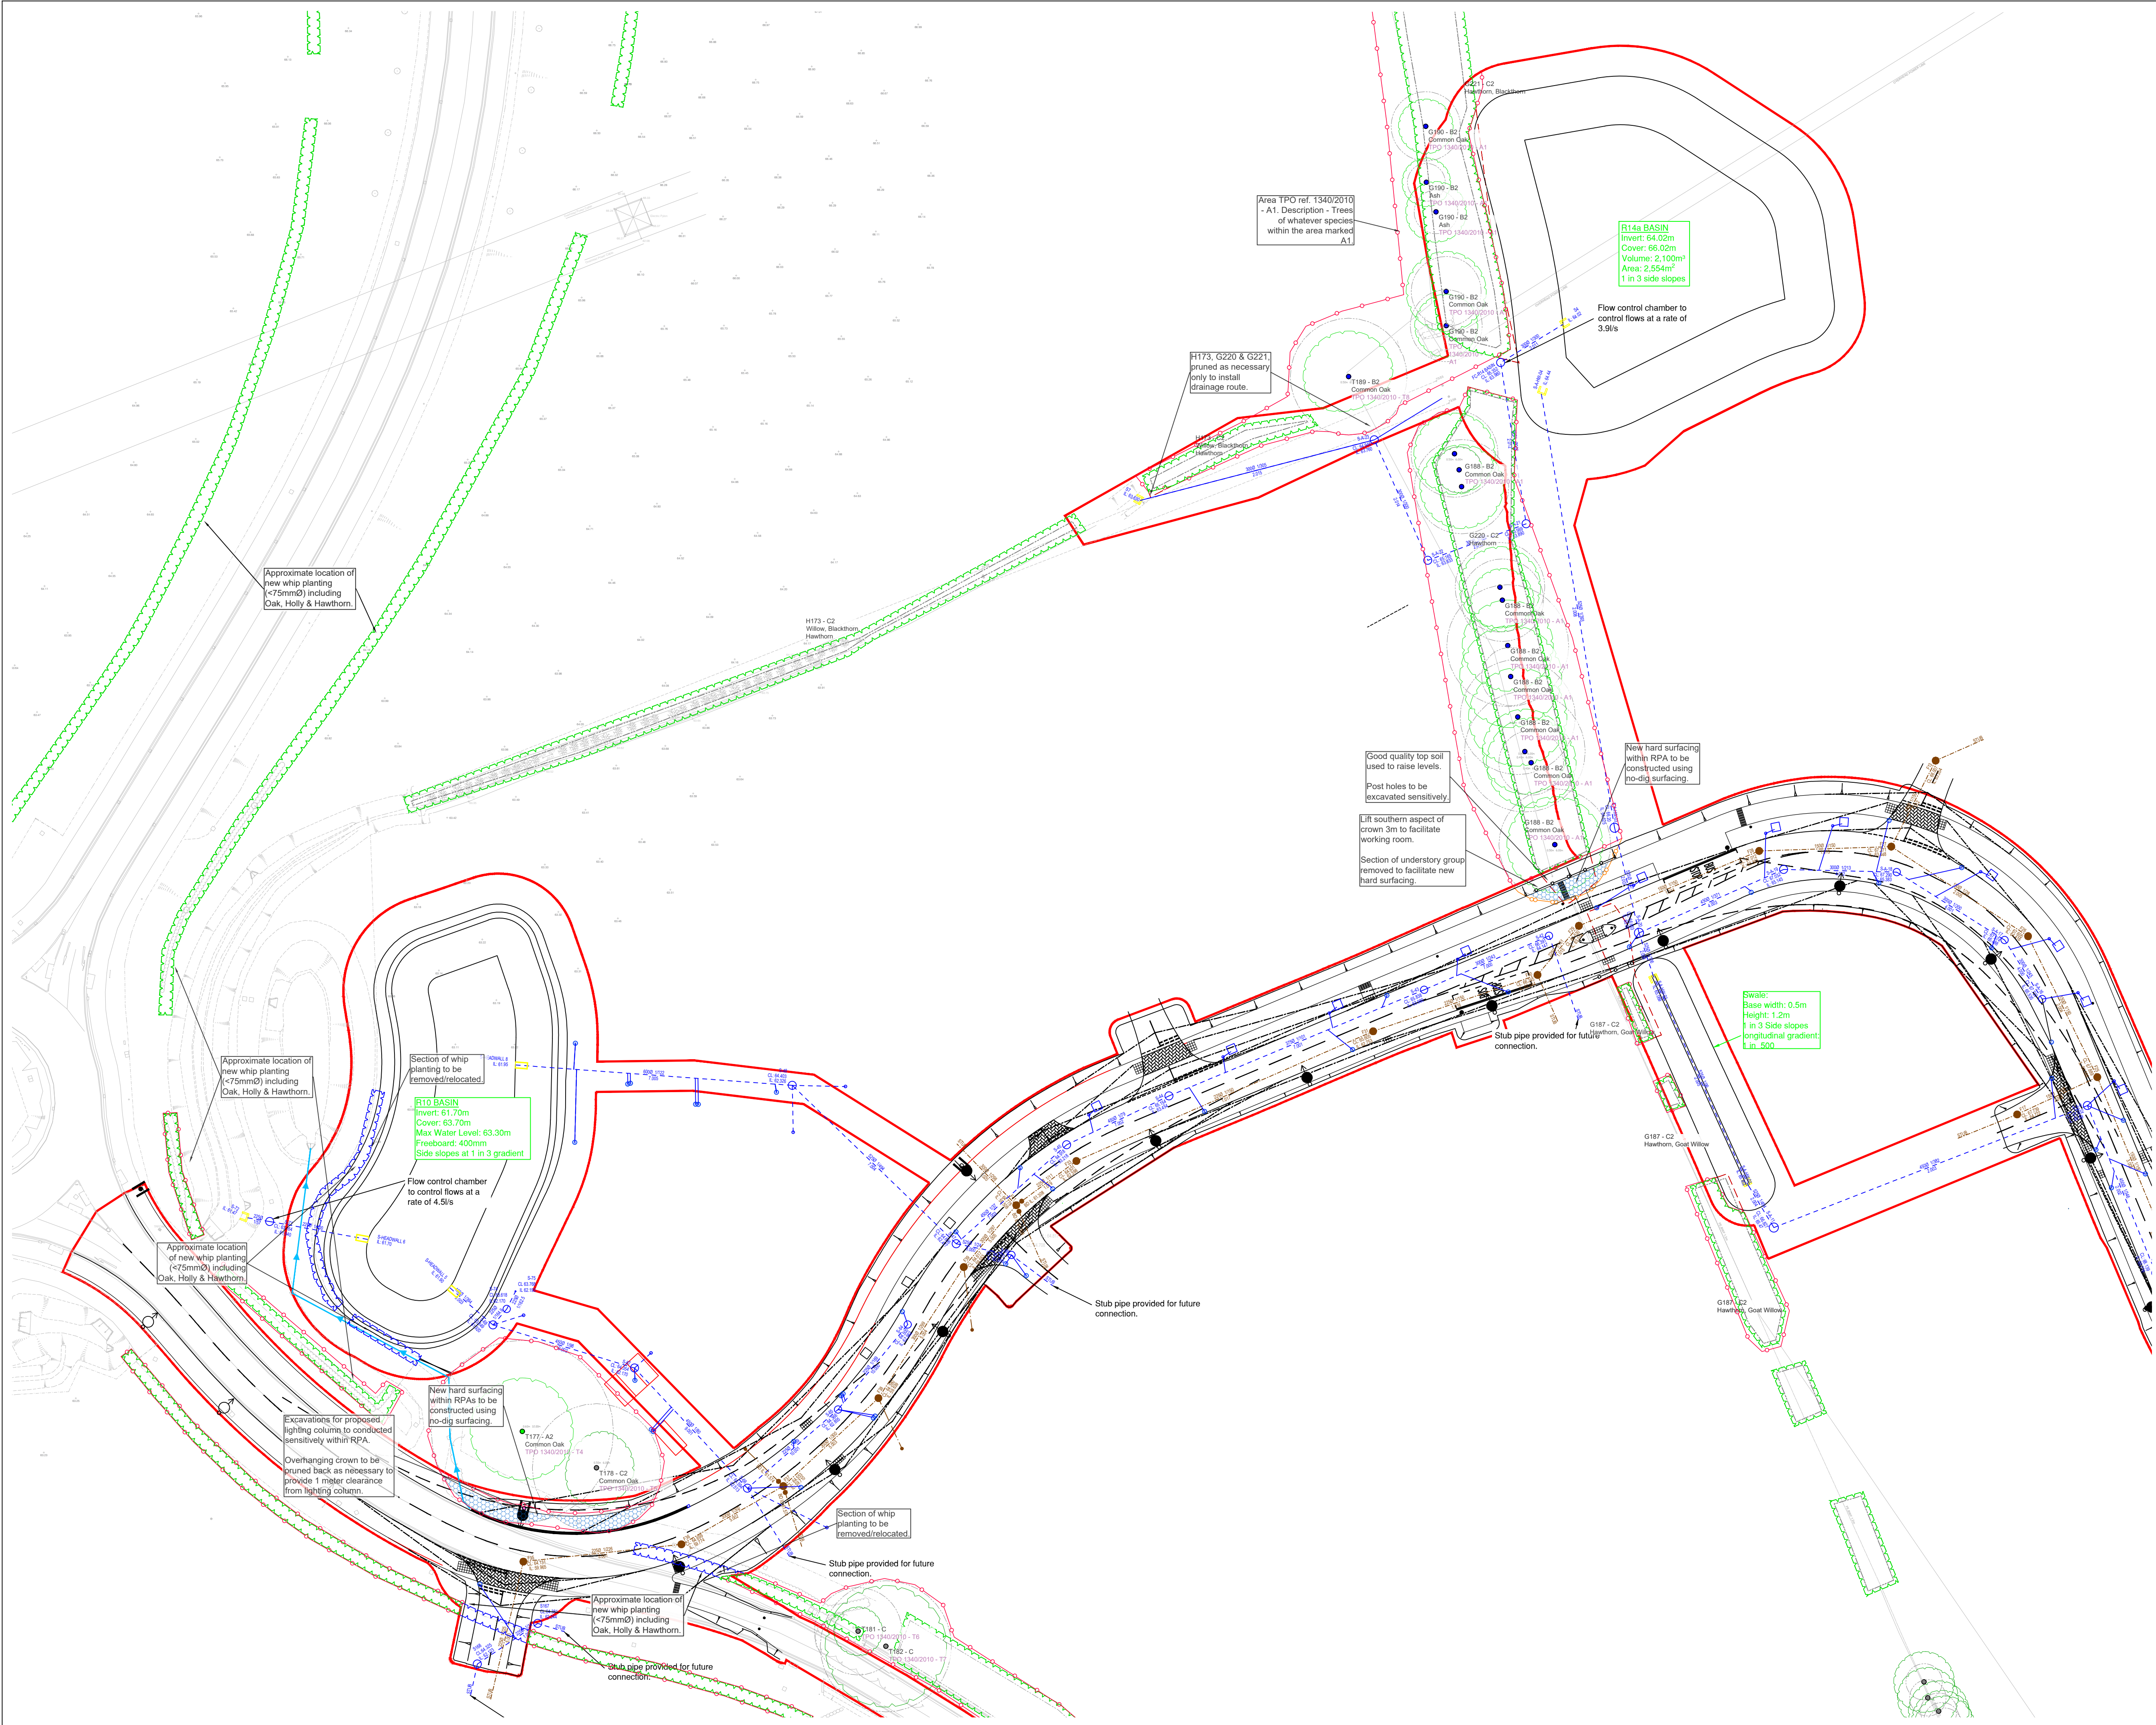

**LEGEND**  
**TREE PROTECTION FENCING & EXCLUSION ZONE**  
A) Tree Protection Fence (TPF) shall be installed prior to any plant activity on site whatsoever, including demolition, utility installation, groundworks, and soil stripping. Once erected, all TPF will be regarded as permanent, and will not be removed or altered without prior consultation by the project arboriculturist and approval of the local planning authority.  
B) Tree Protection Fence shall comprise of Herea type panels on 'horns', well braced by attachment to scaffold pole uprights driven firmly into the ground. Once the exclusion zone has been protected by barriers under ground protection, construction work can commence. All weather notices may be erected on the barriers.

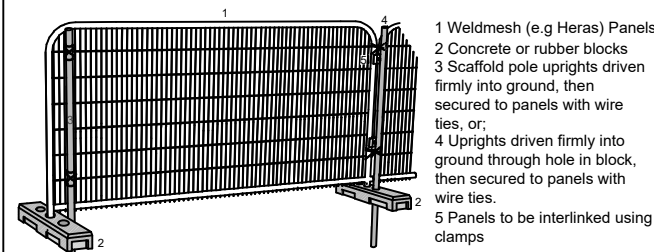

**NO-DIG SURFACE**  
Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 60-75mm for pedestrian surfaces and 100-200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. All specifications subject to engineering design.  
Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications  
TreeTex T300 geotextile or similar laid over CellWeb  
Porous surface to finish  
Peg and board edging  
Top soil to BS3882:2007  
Original ground level  
Depressions and soft spots in formation to be filled with sharp sand to levels required  
CCS/Cellular confinement system (Geosynthetic CellWeb or similar approved)

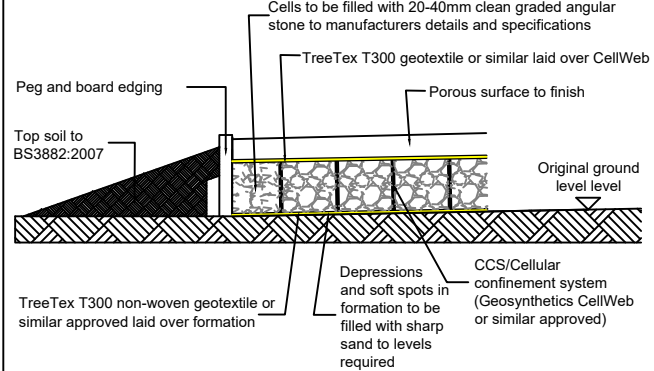

**TEMPORARY FENCING**  
This fencing position is used to protect trees prior to excavation and construction works.

**SENSITIVE EXCAVATION**  
The required excavation is within retained RPA. To reduce impacts to underlying roots the excavation is to be conducted in a sensitive manner, either by use of handtools and as-spade where feasible or through use of an excavator with a toothless bucket and under direct supervision.


**TREE TO BE RETAINED**

**HEDGE/GROUP TO BE REMOVED**

**HEDGE/GROUP CANOPY TO BE REDUCED**  
Hedge to be trimmed back from the red dashed line to the green line as indicated.

**HEDGE/GROUP TO BE TRANSPLANTED**

**A CATEGORY TREE**  
**B CATEGORY TREE**  
**C CATEGORY TREE**  
**U CATEGORY TREE**  
**ROOT PROTECTION AREA (RPA) FOR RETAINED TREES**




|     |          |                                                 |       |
|-----|----------|-------------------------------------------------|-------|
| F   | 22/09/25 | Update to layout                                | WTW   |
| E   | 06/12/24 | Additional TPF show outside of redline boundary | WTW   |
| D   | 29/10/24 | Correct drainage and lighting columns shown     | WTW   |
| C   | 28/10/24 | Update to layout                                | WTW   |
| B   | 06/09/24 | Update to layout                                | WTW   |
| A   | 30/08/24 | Update to layout                                | WTW   |
| Rev | Date     | Details                                         | Drawn |

**ACD ENVIRONMENTAL**  
HEAD OFFICE  
Rodbourne Rail Business Centre, Grange Lane,  
Malmesbury, SN16 0ES  
Tel: 01666 825646  
Unit 7, Godalming Business Centre, Woolsack Way  
Godalming, GU7 1XW  
Tel: 01483 425714  
Suite 6, Crescent House, Yonge Close,  
Eastleigh, SO50 9SX  
Tel: 02382 026300  
email: mail@acdenvco.co.uk  
www.acdenvco.co.uk

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally asserted. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.

scheme: South Wokingham  
R10 - R14 Link Road  
client: Kingacre, Kier & Miller  
drawing: Tree Protection Plan  
date: 22/02/2024  
scale: 1:500@A1  
dwg no: CONS24461-03F  
Sheet 1 of 2  
drawn: WTW checked: AJB

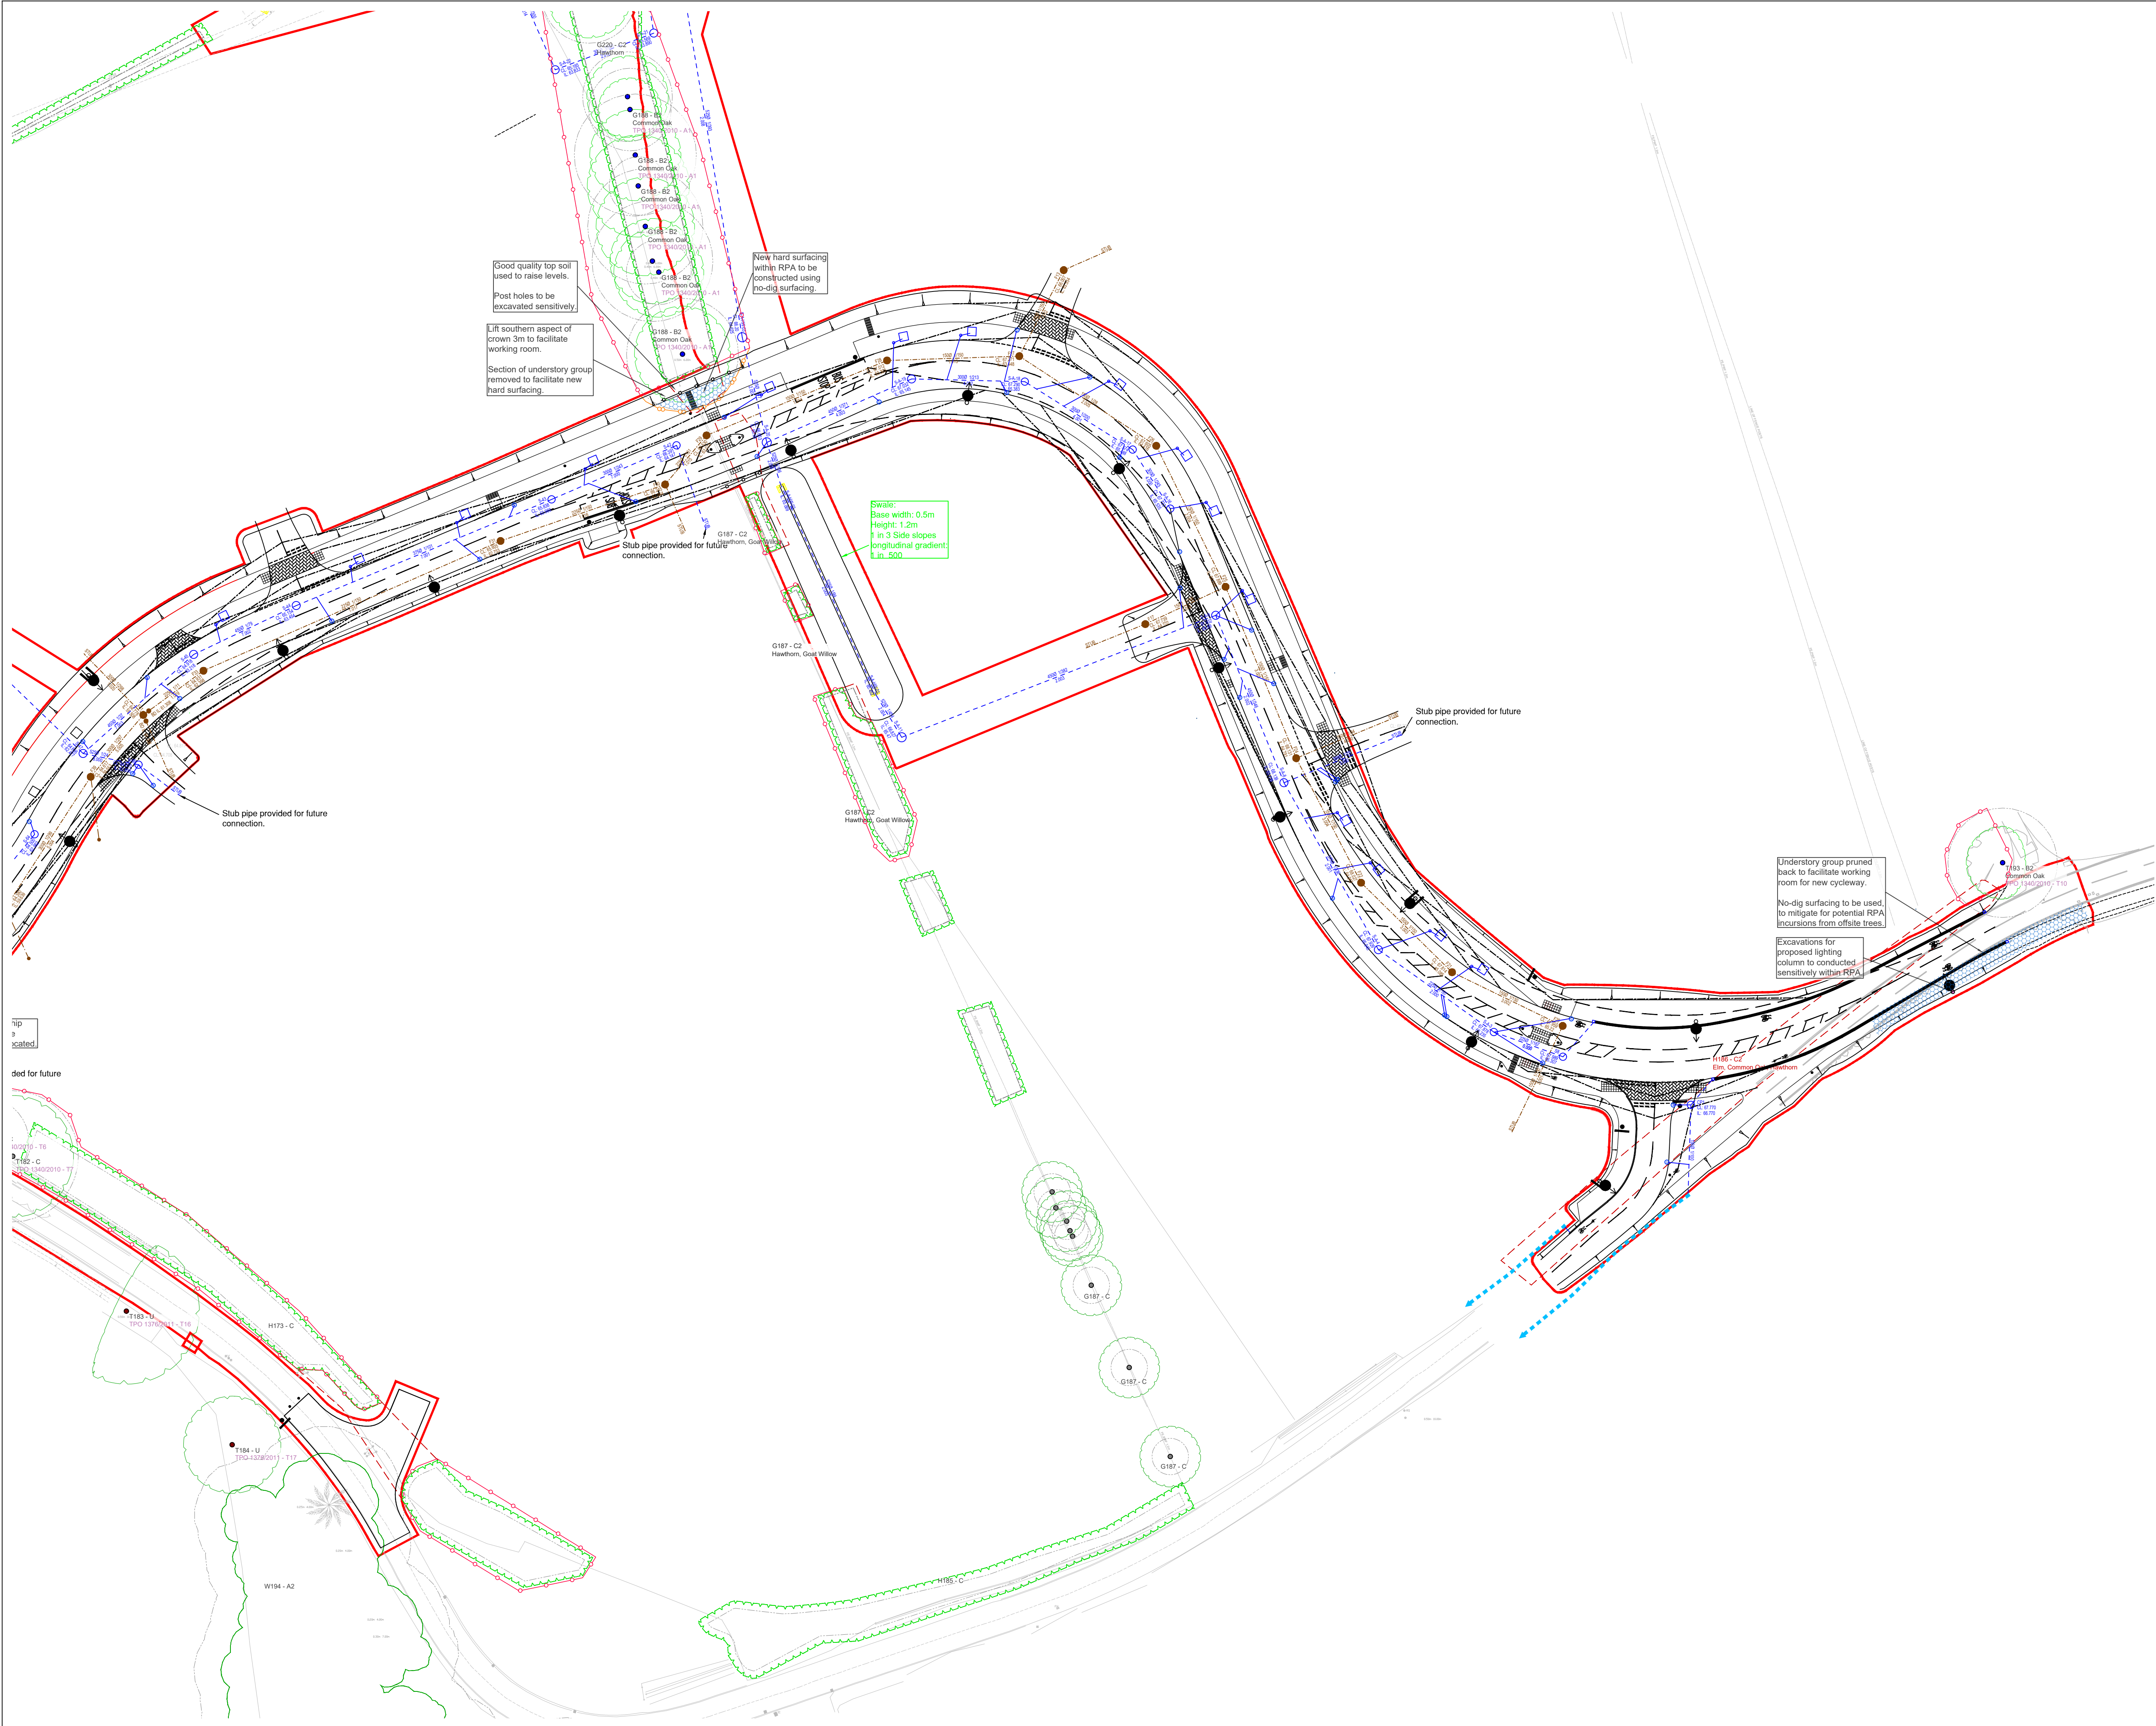

**LEGEND**

**TREE PROTECTION FENCING & EXCLUSION ZONE**  
All Tree Protection Fencing (TPF) shall be installed prior to any plant activity on site whatsoever, including demolition, utility installation, groundworks, and soil stripping. Once erected, all TPF will be regarded as permanent, and will not be removed or altered without prior consultation by the project arboriculturist and approval of the local planning authority.

Tree Protection Fence and Exclusion Zone of Here type panels on 'locks', well braced by attachment to scaffold pole uprights driven firmly into the ground. Once the exclusion zone has been protected by barriers under ground protection, construction work can commence. All weather notices may be erected on the barriers.

1 Weldmesh (e.g. Heras) Panels  
2 Concrete or rubber blocks  
3 Scaffold pole uprights driven firmly into ground, then secured to panels with wire ties, or  
4 Uprights driven firmly into ground through hole in block, then secured to panels with wire ties.  
5 Panels to be interlinked using clamps

**NO-DIG SURFACE**  
Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50-75mm for pedestrian surfaces and 100-200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. All specifications subject to engineering design.  
Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications  
TreeTex T300 geotextile or similar laid over CellWeb  
Porous surface to finish  
Peg and board edging  
Top soil to BS3882:2007  
Original ground level  
TreeTex T300 non-woven geotextile or similar approved laid over formation  
Depressions and soft spots in formation to be filled with sharp sand to levels required  
CCS/Cellular confinement system (Geosynthetic CellWeb or similar approved)

**TEMPORARY FENCING**  
This fencing position is used to protect trees prior to excavation and construction works.

**SENSITIVE EXCAVATION**  
The required excavation is within retained RPA. To reduce impacts to underlying roots the excavation is to be conducted in a sensitive manner, either by use of hand-tools and air-spade where feasible or through use of an excavator with a toothless bucket and under direct supervision.

**TREE TO BE RETAINED**

**HEDGE/GROUP TO BE REMOVED**

**HEDGE/GROUP CANOPY TO BE REDUCED**  
Hedge to be trimmed back from the red dashed line to the green line as indicated.

**HEDGE/GROUP TO BE TRANSPLANTED**

**A CATEGORY TREE**  
**B CATEGORY TREE**  
**C CATEGORY TREE**  
**U CATEGORY TREE**

**ROOT PROTECTION AREA (RPA) FOR RETAINED TREES**

The original of this drawing was produced in colour - a monochrome copy should not be relied upon.



|     |          |                                                |       |
|-----|----------|------------------------------------------------|-------|
| F   | 22/09/25 | Update to layout                               | WTW   |
| E   | 06/12/24 | Additional TPF show outside of reline boundary | WTW   |
| D   | 29/10/24 | Correct drainage and lighting columns shown    | WTW   |
| C   | 28/10/24 | Update to layout                               | WTW   |
| B   | 06/09/24 | Update to layout                               | WTW   |
| A   | 30/08/24 | Update to layout                               | WTW   |
| Rev | Date     | Details                                        | Drawn |

**ACD ENVIRONMENTAL**

HEAD OFFICE  
Rodbourne Rail Business Centre, Grange Lane,  
Malmesbury, SN16 0ES  
Tel: 01666 825646

Unit 7, Godalming Business Centre, Woolsack Way  
Godalming, GU7 1XW  
Tel: 01483 425714

Suite 6, Crescent House, Yonge Close,  
Eastleigh, SO50 9SX  
Tel: 02382 026300

email: mail@acdenv.co.uk  
www.acdenvironmental.co.uk

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally asserted. 2015. Copyright of this plan remains with ACD until all fees have been paid in full.

scheme: South Wokingham  
R10 - R14 Link Road  
client: Kingacre, Kier & Miller  
drawing: Tree Protection Plan  
date: 22/02/2024  
scale: 1:500@A1  
dwg no: CONS24461-03F  
Sheet 2 of 2  
drawn: WTW checked: AJB
