
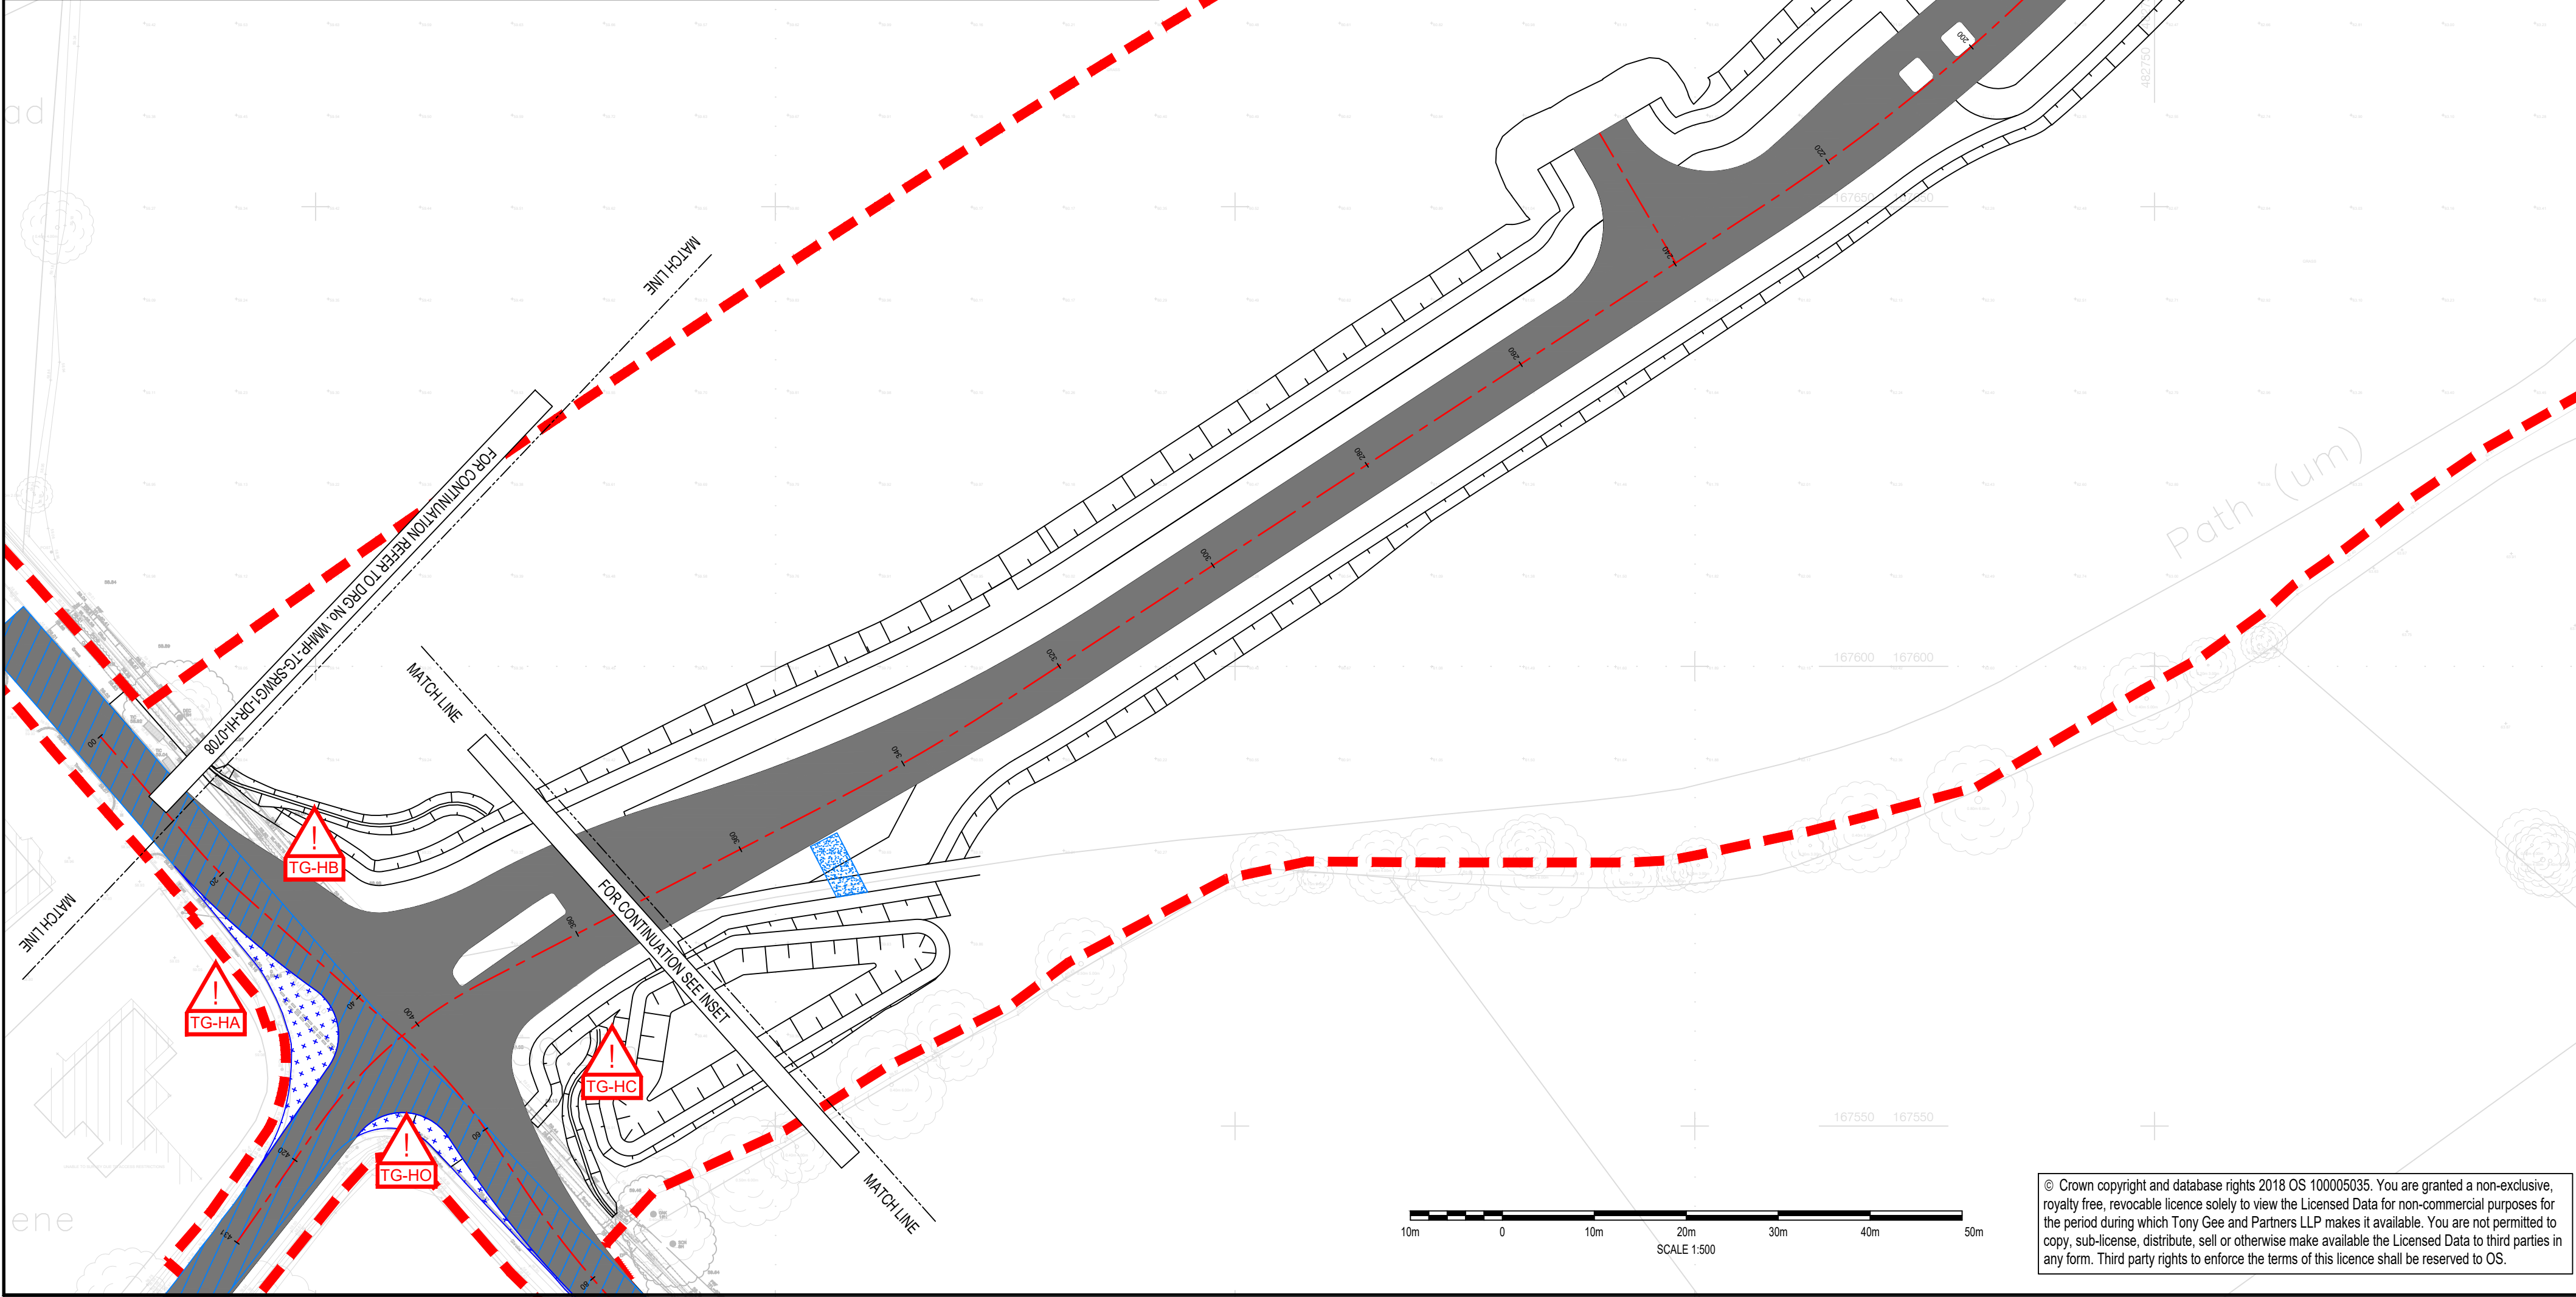


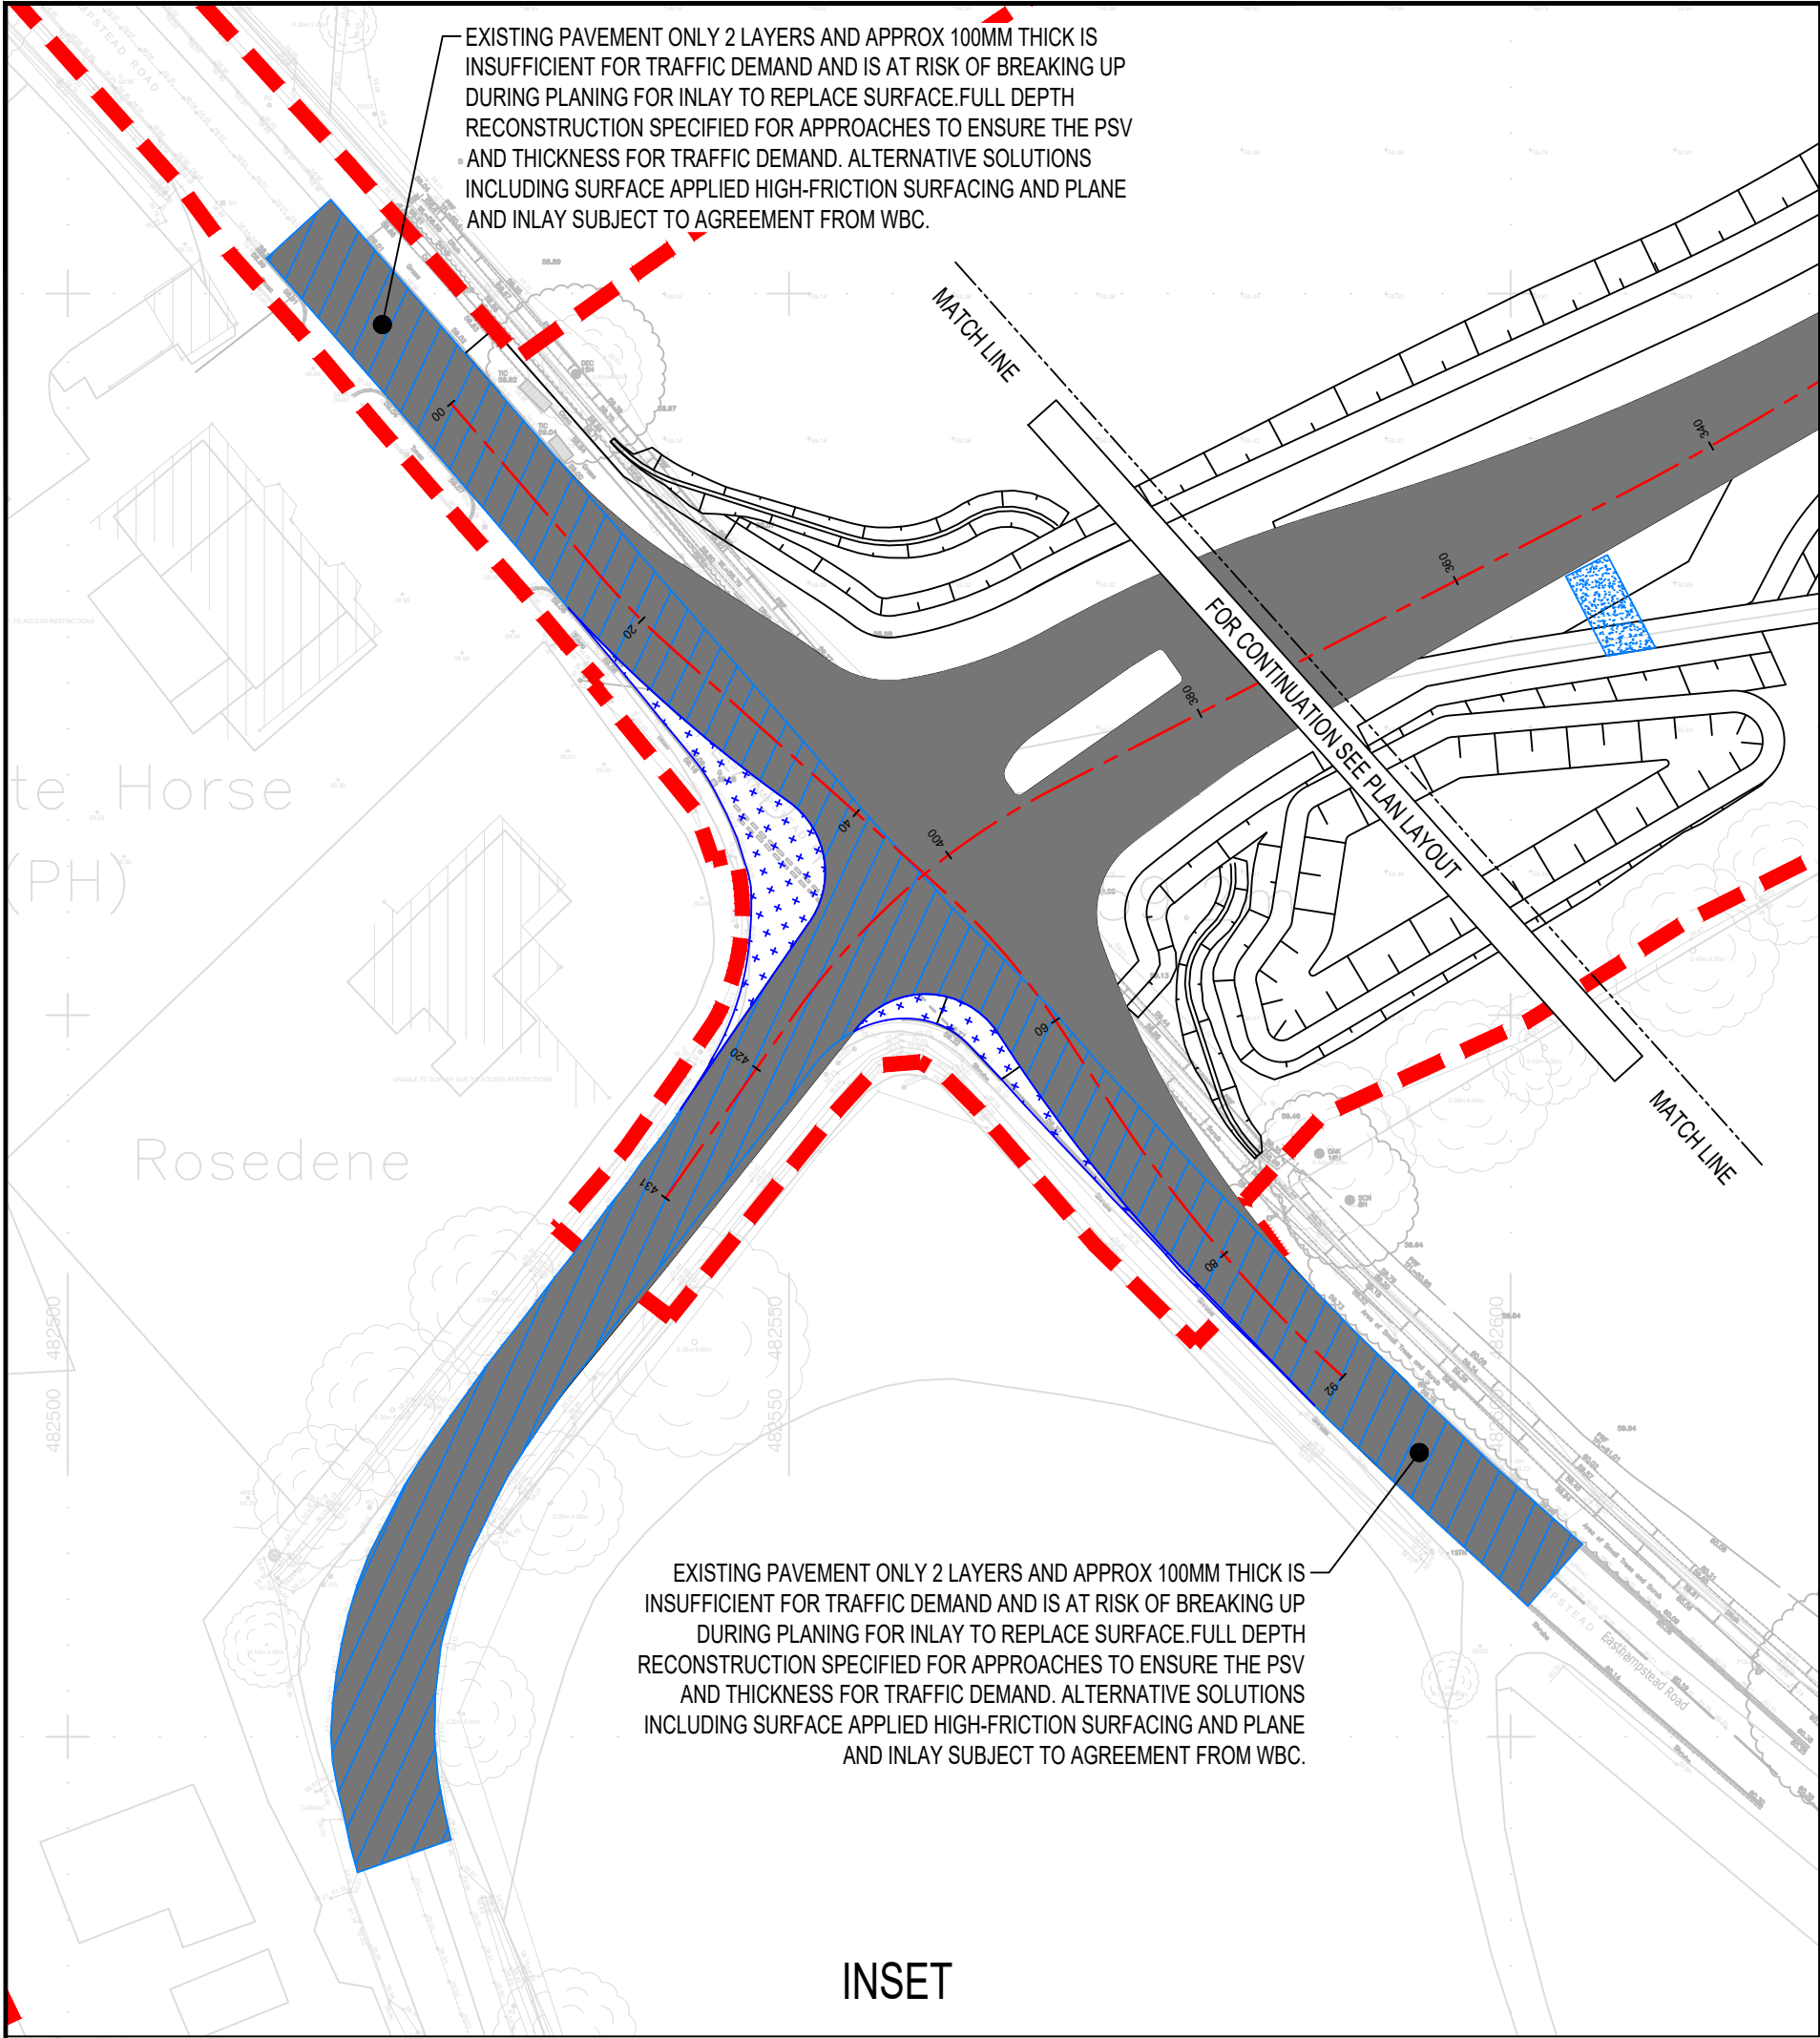

SIGNIFICANT RESIDUAL HAZARDS		
RESIDUAL HAZARD	STAGE	SUGGESTED CONTROL MEASURE
 STRIKING UNDERGROUND SERVICES	D	HAND DIGGING AND CAT SCANNING TECHNIQUES SHALL BE UNDERTAKEN TO LOCATE SERVICES/UTILITIES. MARK UP ON SITE IF REQUIRED. NO WORKS TO BE UNDERTAKEN WITHOUT A VALID PERMIT TO DIG. DIVERTED SERVICES TO BE ACCURATELY RECORDED FOR FUTURE WORKS INCLUDING DECOMMISSIONED PLANT.
 ELECTROCUTION OF OPERATIVES. LARGE PLANT STRIKING OVERHEAD CABLES. SMALL PLANT/EQUIPMENT STRIKING ELECTRICITY PYLON/POLE(S).	D / M	ALL OPERATIVES WORKING IN THE VICINITY ARE TO BE AWARE OF THE LOCATION OF OVERHEAD CABLES AND ELECTRICITY PYLON/POLE(S) AT ALL TIMES DURING THE WORKS. IF THE EXISTING POSITION REMAINS DURING THE SITE CLEARANCE WORKS. ENSURE THAT THE PROCEDURES SET OUT IN GUIDANCE NOTE GS6 AND AGRICULTURE INFORMATION SHEET NO. 8 ARE CARRIED OUT AND A SAFE SYSTEM OF WORK IS IN PLACE. IF THE SERVICE DIVERSION WORKS TO REDIRECT THE ELECTRICITY CABLES MEAN THAT OVERHEAD CABLES REMAIN POSITIONED IN CLOSE PROXIMITY OF THE WORKS (AS PER GUIDANCE), A SIMILAR PROCEDURE SHOULD BE UNDERTAKEN FOR THE NEW LOCATION(S). TEMPORARY FENCE TO BE ERRECTED AROUND PYLON AT 6M FROM ITS BASE TO CREATE EXCLUSION ZONE.
 WORKING IN CLOSE PROXIMITY TO WATERCOURSES. EXPOSURE TO HAZARDOUS SUBSTANCES, E.G. LEPTOSPIROSIS.	C / D	CONTRACTOR TO LIAISE WITH THE LEAD LOCAL FLOOD AUTHORITY TO GAIN FLOOD ALERTS. ENSURE WORKFORCE IS SUITABLY TRAINED AND COMPETENT AND ARE WEARING THE APPROPRIATE LEVEL OF PPE FOR THE INTENDED TASK TO REDUCE THE RISK OF WORKERS CONTRACTING LEPTOSPIROSIS OR WEIL'S DISEASE.
 POTENTIAL PRESENCE OF CONTAMINATED MATERIALS WHEN PERFORATING, BREAKING OUT, PLANING AND DISPOSING OF EXISTING PAVEMENT MATERIAL	D / M	ARISING'S MUST BE CHECKED FOR THE PRESENCE OF COAL TAR. IF COAL TAR IS FOUND THEN THE MATERIAL CANNOT BE RECYCLED AS IT IS CLASSSED AS HAZARDOUS/SPECIAL WASTE AND DISPOSED OF APPROPRIATELY.
NOTE: The above hazards do not include every hazard or assumption, but identify significant residual construction hazards that are not likely to be obvious to a competent contractor and those that could be difficult to manage effectively. Refer also to the designer's risk documentation.		

DO NOT SCALE

NOTES:

1. ALL DIMENSIONS ARE IN MILLIMETRES UNLESS NOTED OTHERWISE.

2. ALL LEVELS ARE IN METRES AOD UNLESS NOTED OTHERWISE.

3. DRAWING TO BE READ IN CONJUNCTION WITH DETAILS DRAWING WMHP-TG-SRWG1-DR-HI-0721 AND SPECIFICATION REF. WMHP-TG-SRWG1-SP-HI-0701.

4. FOR DETAILS OF KERBS AND FOOTWAYS REFER TO DRAWINGS WMHP-TG-SRWG1-DR-HI-1101 TO WMHP-TG-SRWG1-DR-HI-1107.

LEGEND

RED LINE BOUNDARY

TYPE A - MAINLINE

TYPE B - BRIDGE DECK

TYPE C - FINCHAMPSTEAD ROAD

TYPE D - TESCO ROUNDABOUT

TYPE E - FINCHAMPSTEAD ROAD ROUNDABOUT

TYPE F - EASTHAMPSTEAD ROAD/ OAKLEY DRIVE AREAS

TYPE G - MAINTENANCE ACCESS

TYPE H - FOOTWAY CROSSOVER

TYPE J - INLAY

TYPE K - OVERLAY

AREAS TO BE PERFORATED OR BROKEN OUT

AREAS TO BE BROKEN OUT

SHEET LOCATION PLAN

N.T.S.

KEYPLAN

SWDR - SPINE ROAD AND WESTERN GATEWAY PHASE 1

P03	28/09/2021	BH	REVISED FOR PLANNING DISCHARGE	JC	ARL
P02	20/08/2021	JF	REVISED FOR PLANNING DISCHARGE AND SCO COMMENTS	DJF	JC
P01	26/05/2021	TCH	FIRST ISSUE	DJF	JC
REV	DATE	BY	DESCRIPTION	CHK	APP

DRAWING STATUS:

SUITABLE FOR REVIEW & COMMENT

S3

DESIGNER:



Tony Gee and Partners LLP

Hardy House

140 High Street

Esher, Surrey

KT10 9QJ

Tel: 01372 461600

www.tonygee.com

Consulting Civil, Structural and Geotechnical Engineers

CONTRACTOR:



CLIENT:



WOKINGHAM BOROUGH COUNCIL

Shute End, Wokingham, Berkshire RG40 1BN

Tel: (0118) 974 6000 Web: www.wokingham.gov.uk

PROJECT:

WOKINGHAM MAJOR HIGHWAYS PROGRAMME

SPINE ROAD AND WESTERN GATEWAY PHASE 1

TITLE:

HIGHWAYS PAVEMENT PLAN LAYOUT

SHEET 7

SCALE @ A1:	1:500	CHECKED:	DJF	APPROVED:	JC
PROJECT NO:	C118047	DESIGNED:	DJF	DRAWN:	TCH
DRAWING NO:	WMHP-TG-SRWG1-DR-HI-0707	DATE:	APRIL 21	REV:	P03
