


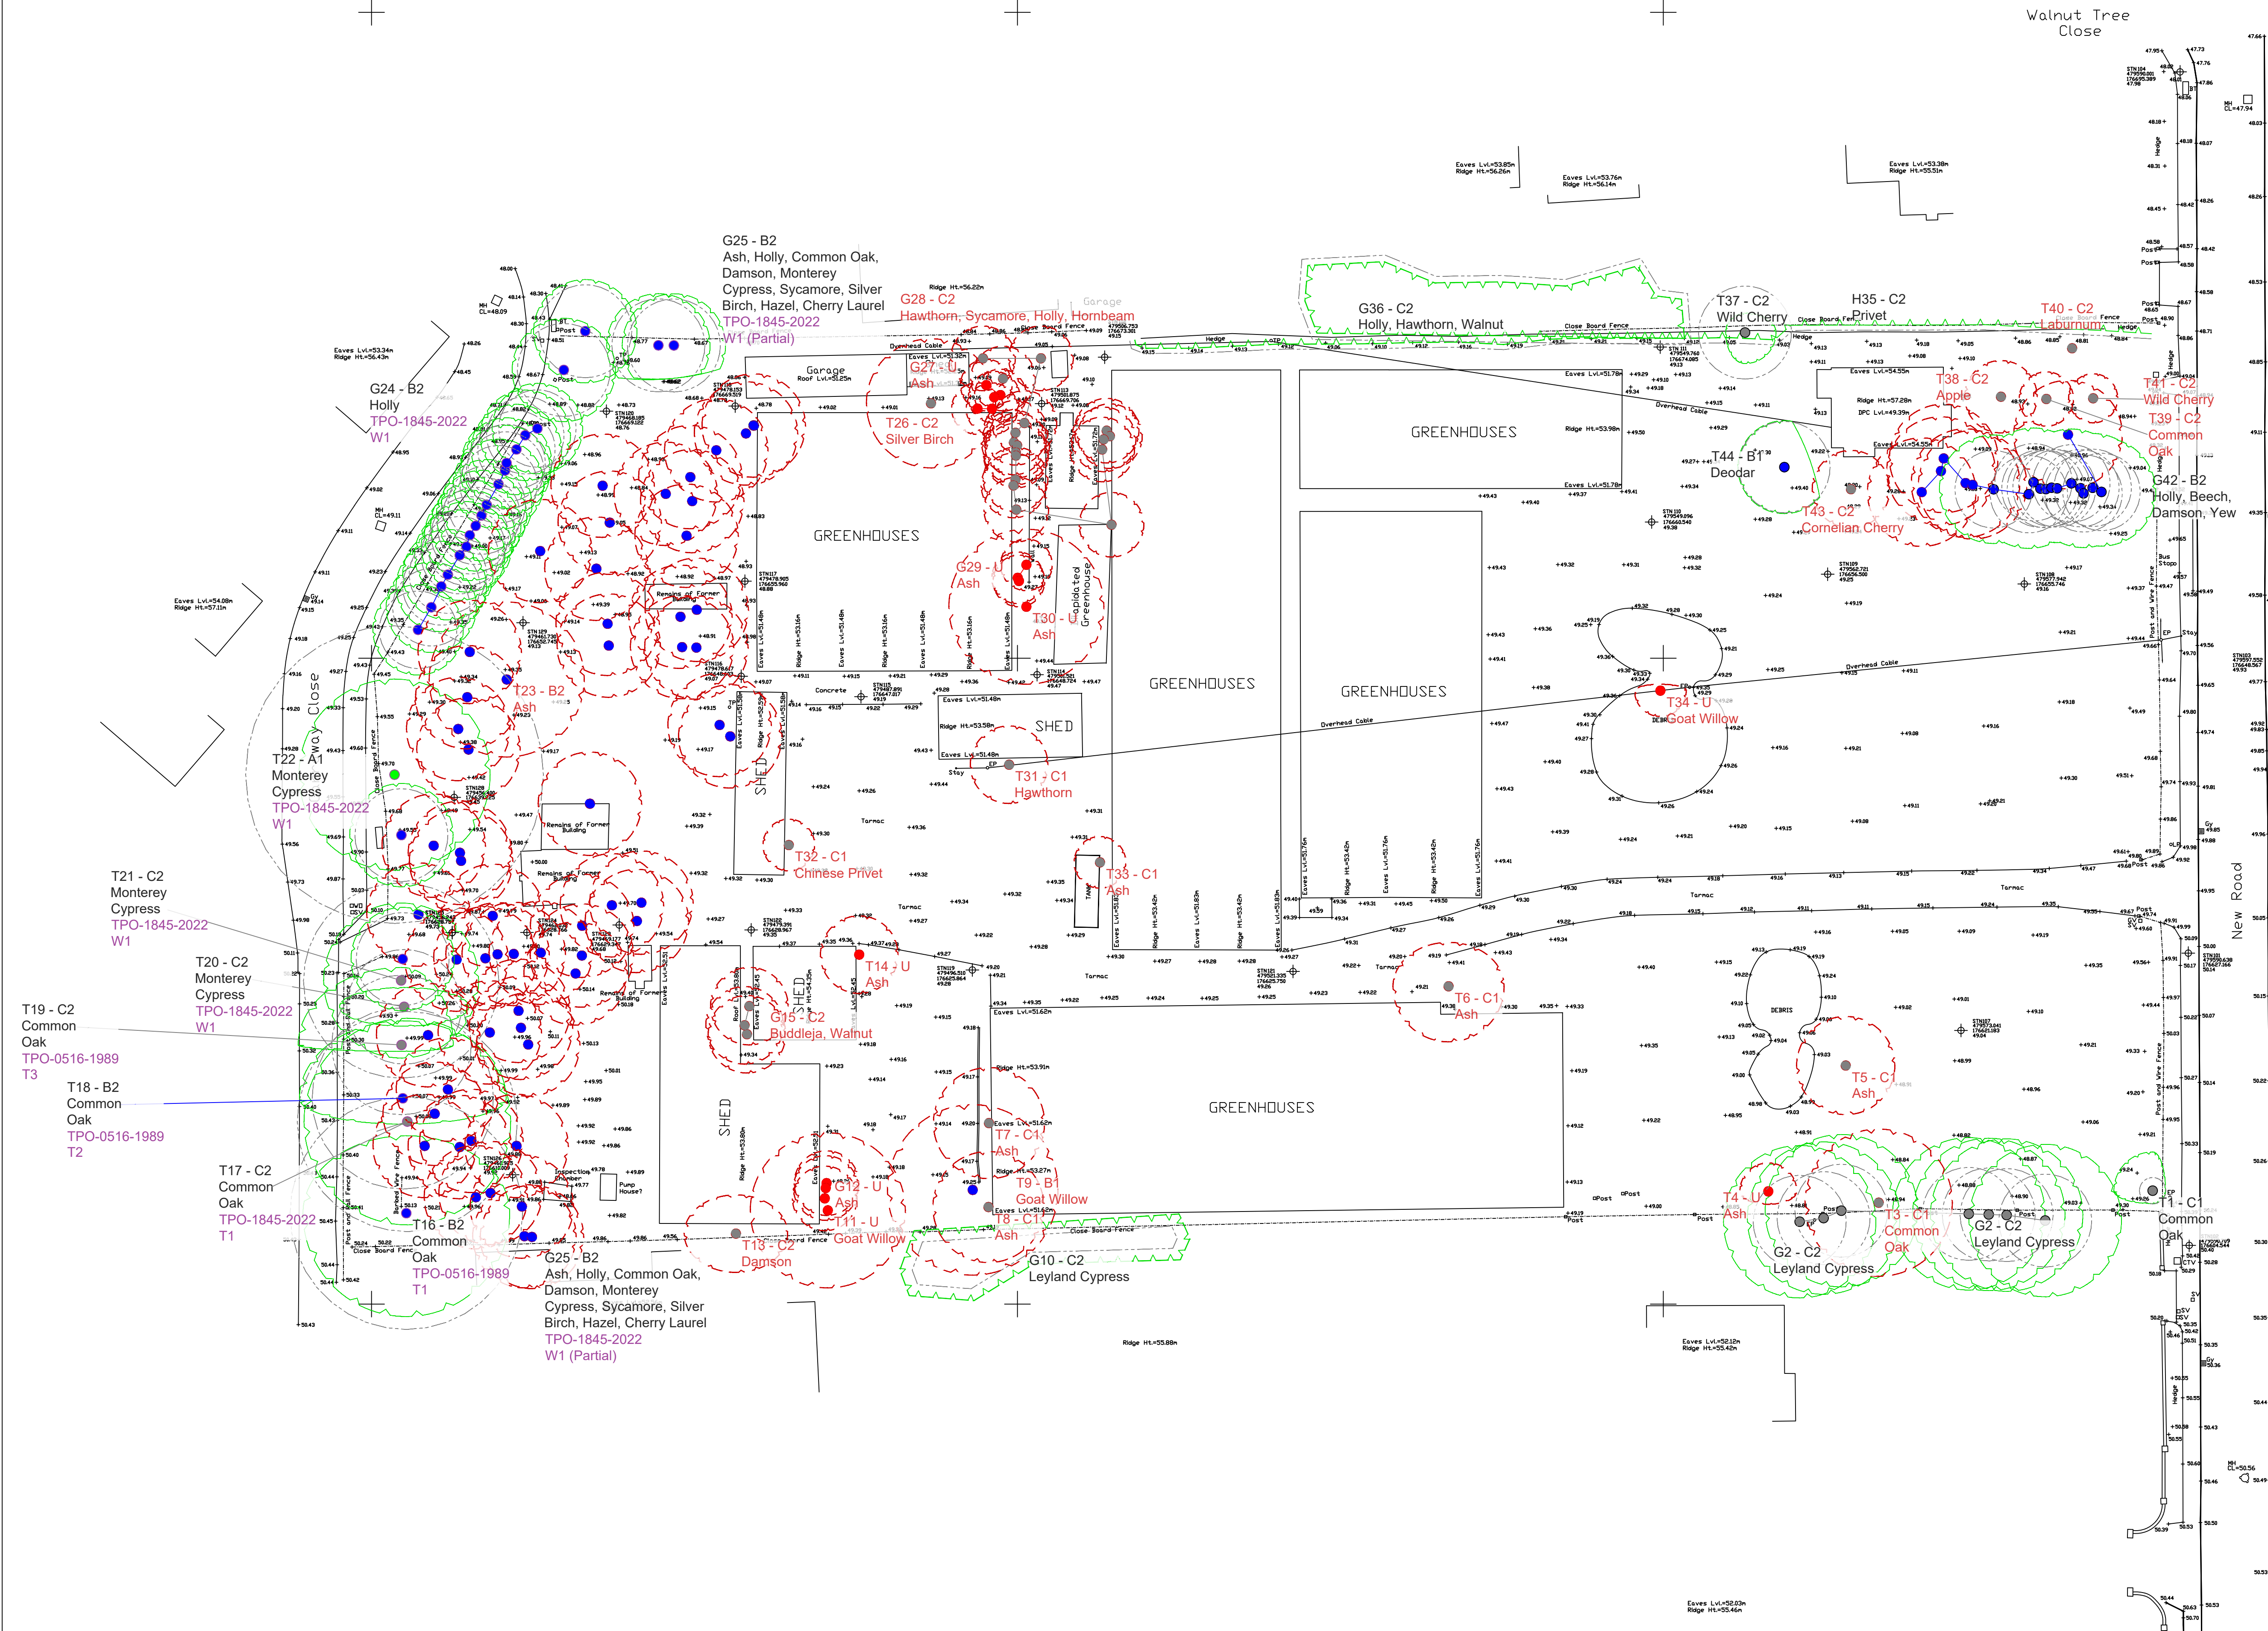

**LEGEND**

**TREE PROTECTION FENCING & EXCLUSION ZONE**  
All Tree Protection Fencing (TPF) shall be installed prior to any plant activity on site whatsoever, including demolition, utility installation, groundworks, and any siting. Once erected, all TPF will be regarded as sacrosanct, and will not be removed or altered without prior recommendation by the project arboriculturist and approval of the local planning authority.

Tree Protection Fencing shall comprise of:  
1. Tree Protection Panels (e.g. Hesco) Panels  
2. Concrete or rubber blocks  
3. Scaffold pole uprights driven firmly into ground, then secured to panels with wire ties, or  
4. Uprights driven firmly into ground through hole in block, then secured to panels with wire ties.  
5. Panels to be interlinked using clamps.

**TEMPORARY FENCING**  
The fencing is used to protect areas of special detail and is to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist.

**NO-DIG SURFACE**  
Cellular Confinement System (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50-75mm for pedestrian surfaces and 100-200mm for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. All specifications subject to engineering design.  
Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications  
TreeTex T300 geotextile or similar laid over CellWeb  
Porous surface to finish  
Top soil to BS3882:2015  
TreeTex T300 non-woven geotextile or similar approved laid over formation  
Depressions and soft spots to be filled with sharp sand to levels required  
CCS/Cellular confinement system (Geocymex CellWeb or similar approved)

**GROUND PROTECTION ADJACENT TO PROPOSED BUILDINGS**  
Where Tree Protection Fencing has been offset to allow working room for building construction, Ground protection must be installed over the exposed soft ground within the retained RPA as per the below specification.  
For further details see BS5837:2012 Section 6

**GROUND PROTECTION WITHIN ROOT PROTECTION AREAS**  
Platform level at first lift of scaffold  
Protective fencing  
Protected area  
Ground undisturbed and protected by additional level of scaffold boards mounted 150mm above ground level  
For pedestrian movements the installation of ground protection as shown will suffice.

**SENSITIVE EXCAVATION**  
Foundations for root to be excavated in a sensitive manner, with the use of excavator using a toothless bucket incrementally scraping the ground layer away from the stems. Works to be conducted under arboricultural supervision.

**TREE TO BE RETAINED**  
**TREE TO BE REMOVED**  
**TREE CANOPY TO BE REDUCED**  
**HEDGE/GROUP SECTION TO BE PRUNED**  
Hedge/Group section to be removed from the red dashed line to the green line as indicated.  
**A CATEGORY TREE**  
**B CATEGORY TREE**  
**C CATEGORY TREE**  
**U CATEGORY TREE**  
**ROOT PROTECTION AREA (RPA) FOR RETAINED TREES**

The original of this drawing was produced in colour - a monochrome copy should not be relied upon.


0 1 2 3 4 5 6 7 8 9 10m

| Rev | Date | Details | Drawn |
|-----|------|---------|-------|
|     |      |         |       |

**Arbiculture  
Archaeology  
Ecology  
Landscape Architecture**  
**ACD ENVIRONMENTAL**  
Phone: 01666 825646  
Email: mail@acdenv.co.uk  
Web: www.acdenvironmental.co.uk

project: Hyde Nursery  
New Road, Ruscombe  
client: Westbourne Homes  
drawing: Tree Protection Plan (Tree Removals)  
date: 16/09/2026  
scale: 1:250@A1  
drawing no: WEST25231-03 (1 of 2)  
drawn: WTW checked: AJB

Copyright of ACD Environmental Ltd. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally asserted. 2011. Copyright of this plan remains with ACD until all fees have been paid in full.

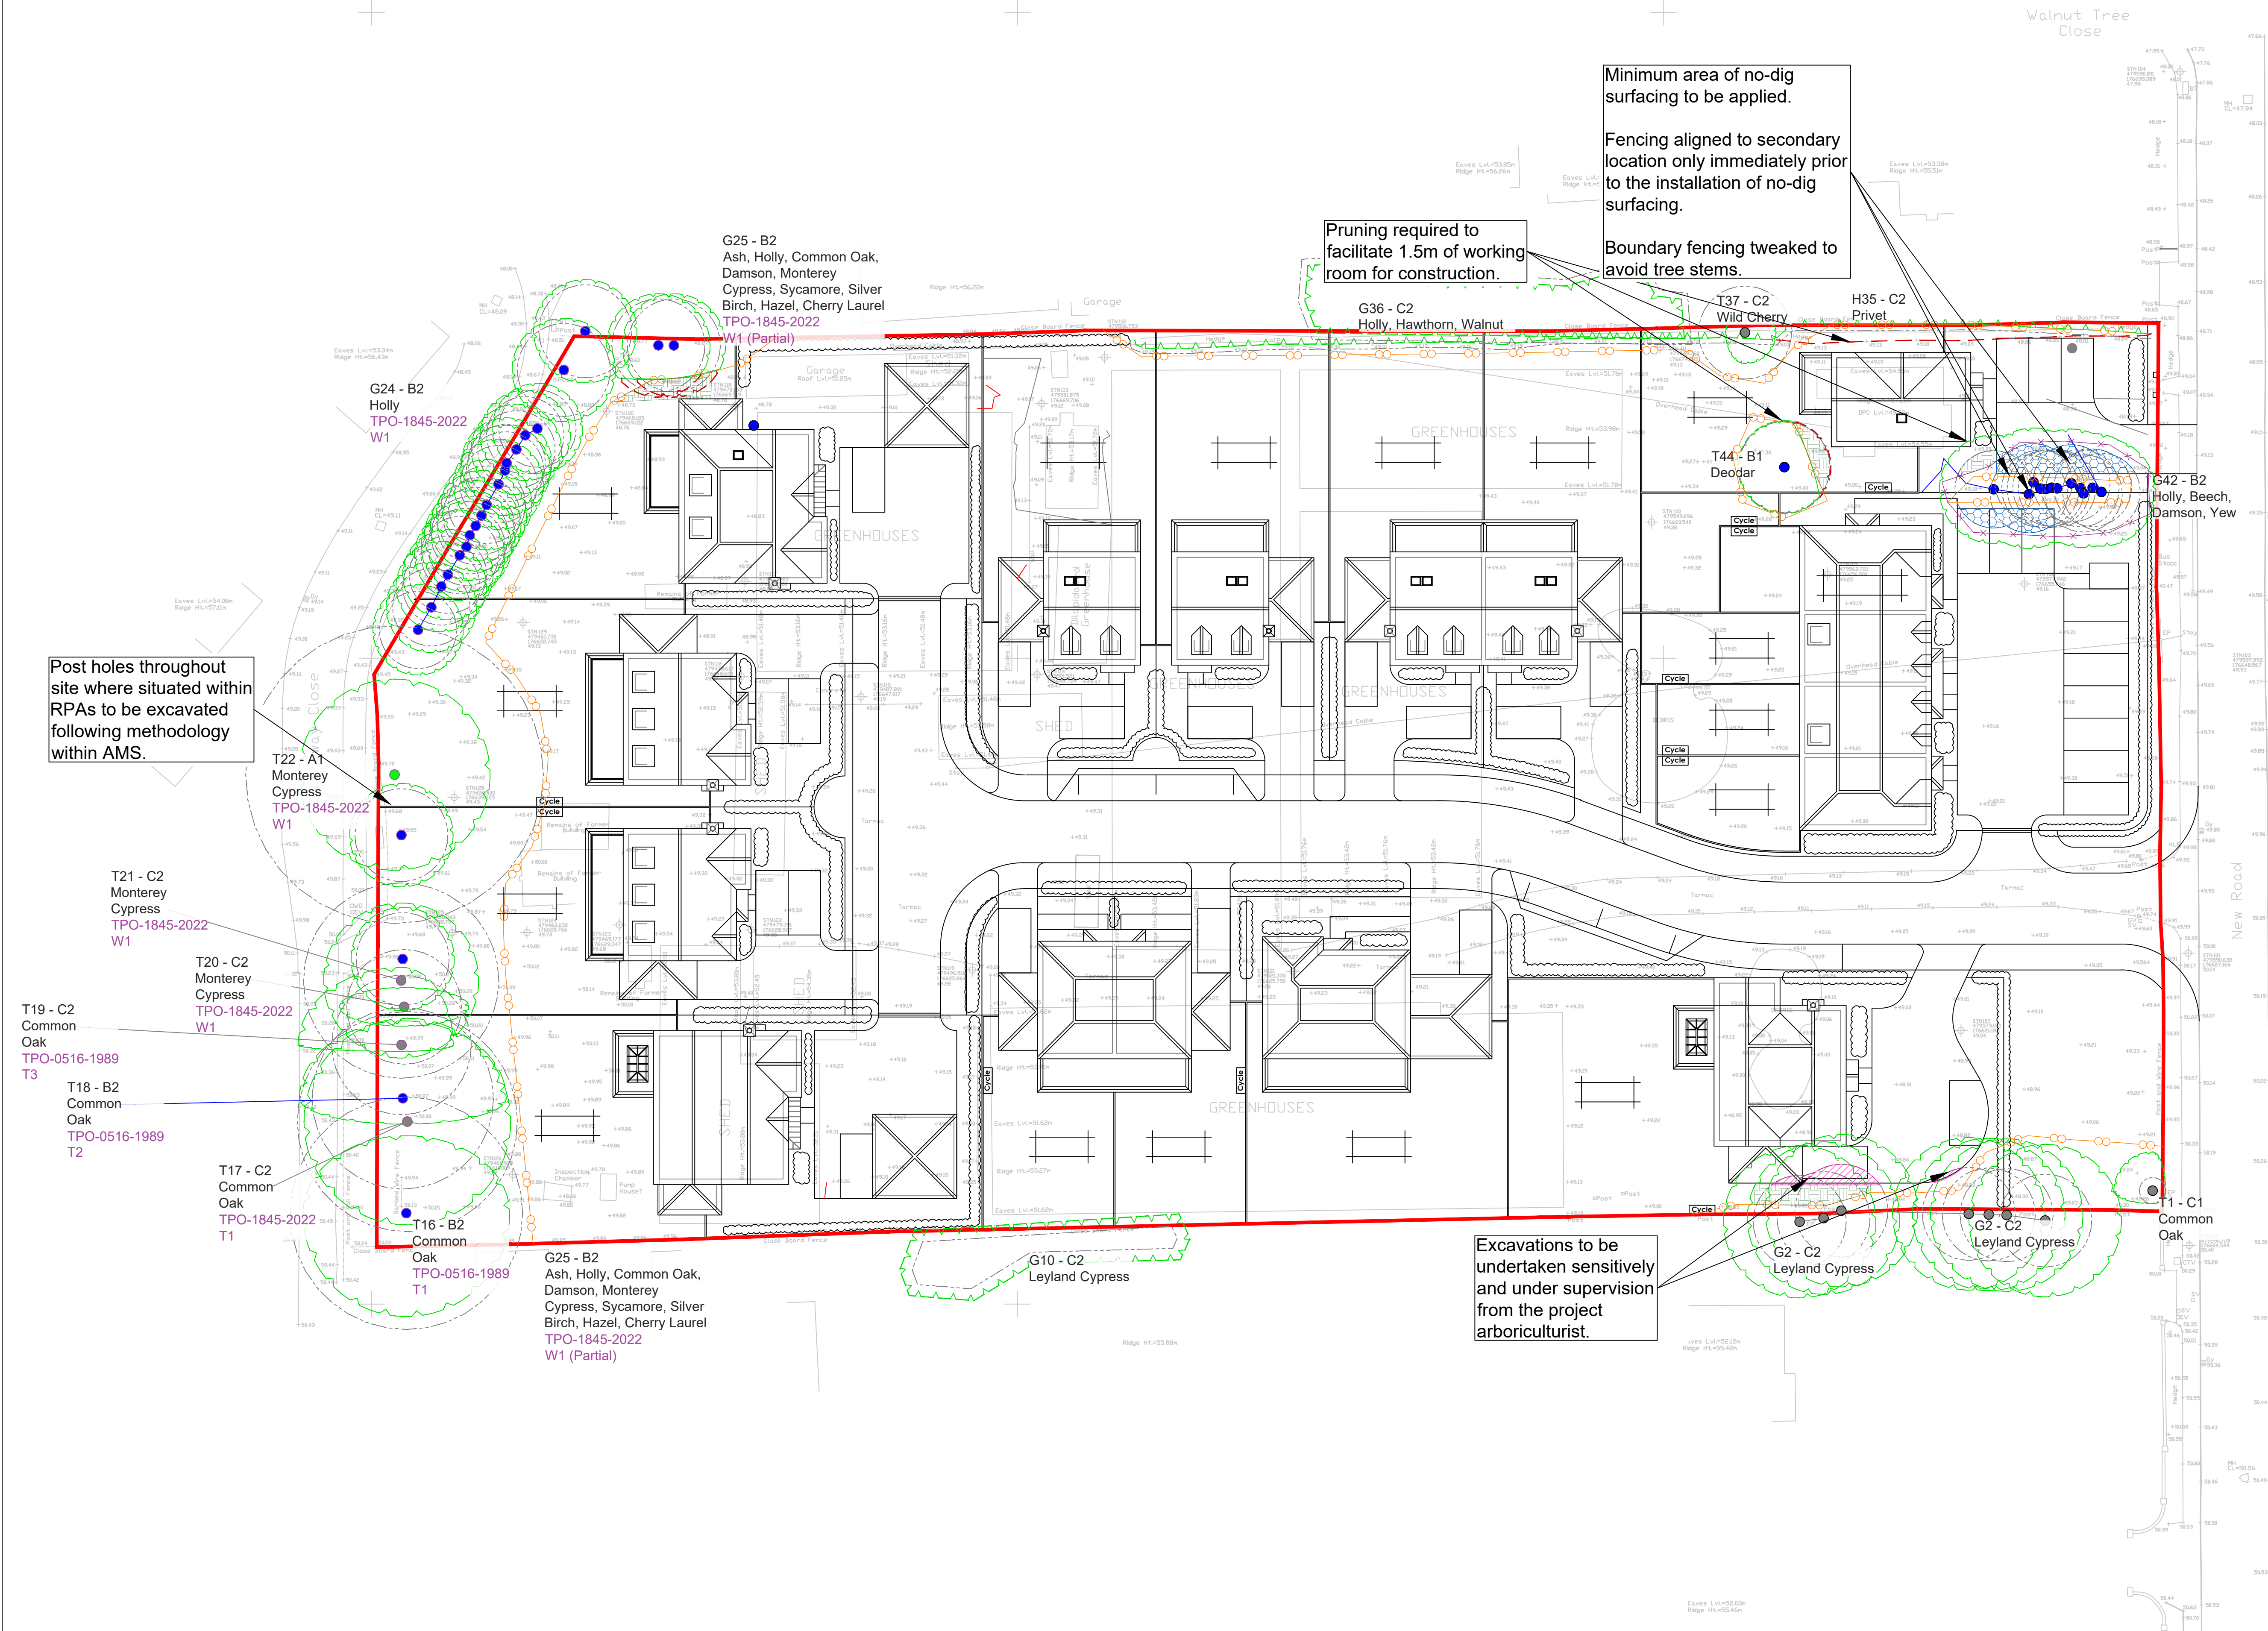

Post holes throughout site where situated within RPAs to be excavated following methodology within AMS.

Pruning required to facilitate 1.5m of working room for construction.

Minimum area of no-dig surfacing to be applied.

Fencing aligned to secondary location only immediately prior to the installation of no-dig surfacing.

Boundary fencing tweaked to avoid tree stems.

Excavations to be undertaken sensitively and under supervision from the project arboriculturist.

**LEGEND**

**TREE PROTECTION FENCING & EXCLUSION ZONE**  
All Tree Protection Fencing (TPF) shall be installed prior to any plant activity on site whatsoever, including demolition, utility installation, groundworks, and soil stripping. Once erected, all TPF will be registered as permanent, and will not be removed or altered without prior recommendation by the project arboriculturist and approval of the local planning authority.

Tree Protection Fencing shall comprise of Heavy Duty Panels on Posts, well braced by struts to scaffold pole uprights driven firmly into the ground. Once the exclusion zone has been protected by barriers and/or ground protection, construction work can commence. All weather notices may be erected on the barriers.

1 Weldmesh (e.g. Hesco) Panels  
2 Concrete or rubber blocks  
3 Scaffold pole uprights driven firmly into ground, then secured to panels with wire ties, or  
4 Uprights driven firmly into ground through hole in block, then secured to panels with wire ties.  
5 Panels to be interlinked using clamps

**TEMPORARY FENCING**  
The fencing is used to protect areas of special detail and is to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist.

**NO-DIG SURFACE**  
Cellular Confinement System (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50-75mm for pedestrian surfaces and 100-200mm for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. All specifications subject to engineering design.  
Cells to be filled with 20-40mm clean graded angular stone to manufacturers details and specifications  
TreeTex T300 geotextile or similar laid over CellWeb  
Porous surface to finish  
Top soil to BS3882:2015  
Original ground level  
Depressions and soft spots in formation to be filled with sharp sand to levels required  
CCS/Cellular confinement system (Geocymex CellWeb or similar approved) required

**GROUND PROTECTION ADJACENT TO PROPOSED BUILDINGS**  
Where Tree Protection Fencing has been offset to allow working room for building construction, Ground protection must be installed over the exposed soft ground within the retained RPA as per the below specification.

**GROUND PROTECTION WITHIN ROOT PROTECTION AREAS**  
Platform level at first lift of scaffold  
Protective fencing  
Protected area  
Ground undisturbed and protected by additional level of scaffold boards mounted 150mm above ground level  
For further details see BS5837:2012 Section 6

**SENSITIVE EXCAVATION**  
Foundations for most to be excavated in a sensitive manner, with the use of excavator using a 'toothless' bucket incrementally scraping the ground layer away from the stems. Works to be conducted under arboricultural supervision.

**TREE TO BE RETAINED**  
**TREE TO BE REMOVED**  
**TREE CANOPY TO BE REDUCED**  
**HEDGE/GROUP SECTION TO BE PRUNED**  
Hedge/Group section to be removed from the red dashed line to the green line as indicated.

**A CATEGORY TREE**  
**B CATEGORY TREE**  
**C CATEGORY TREE**  
**ROOT PROTECTION AREA (RPA) FOR RETAINED TREES**

The original of this drawing was produced in colour - a monochrome copy should not be relied upon.



|     |          |                |       |
|-----|----------|----------------|-------|
| A   | 02/10/26 | Updated Layout | HEP   |
| Rev | Date     | Details        | Drawn |

**ACD ENVIRONMENTAL**  
Arboriculture  
Archaeology  
Ecology  
Landscape Architecture  
Phone: 01666 825646  
Email: mail@acdenv.co.uk  
Web: www.acdenvironmental.co.uk

project: Hyde Nursery  
New Road, Ruscombe  
client: Westbourne Homes  
drawing: Tree Protection Plan  
date: 16/09/2026  
scale: 1:250@A1  
drawing no: WEST25231-03 (2 of 2)  
drawn: WTW checked: AJB

Copyright of ACD Environmental Ltd. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally asserted. 2011. Copyright of this plan remains with ACD until all fees have been paid in full.
