


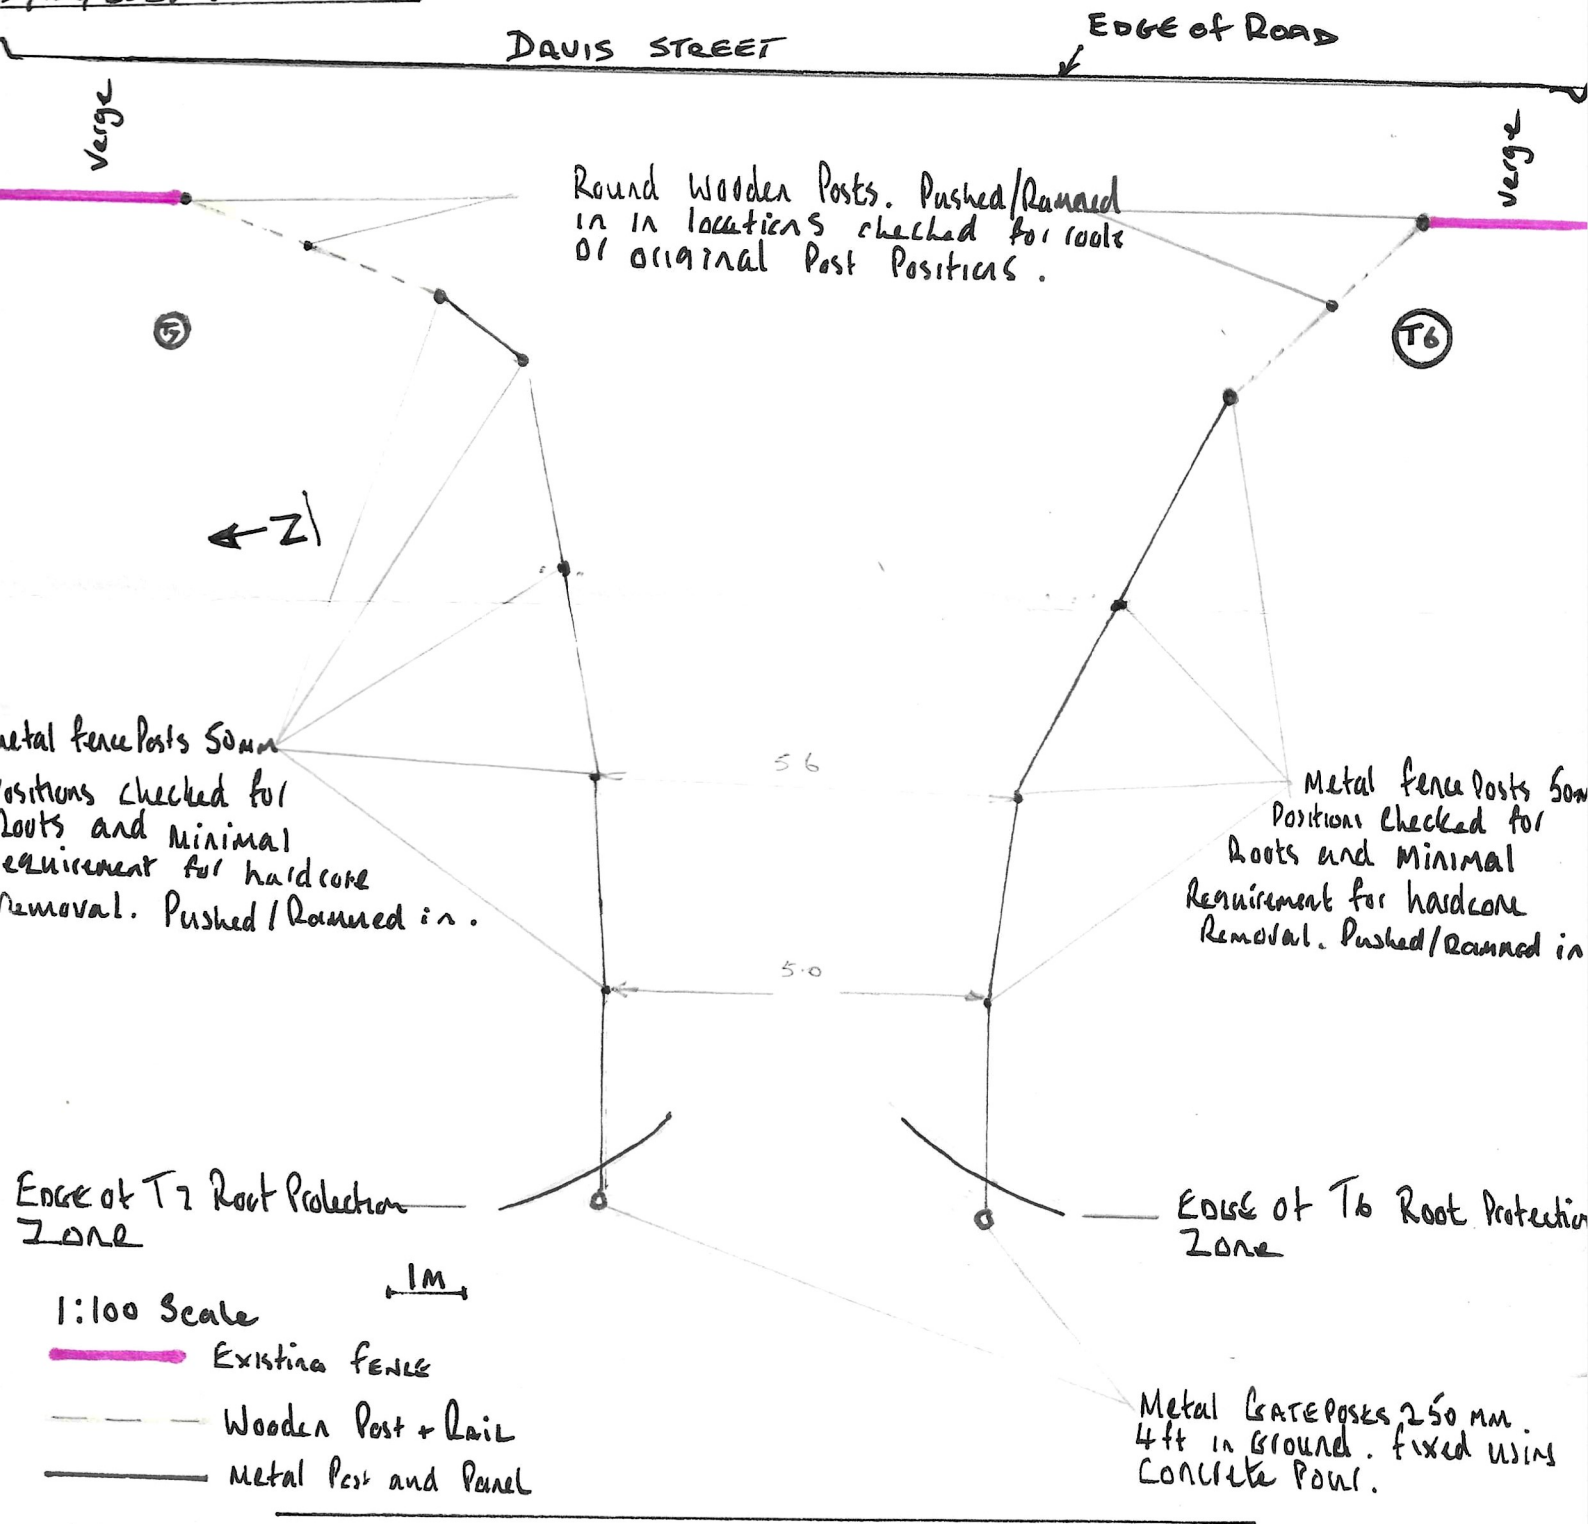

NECESSARY works following Break in. Due to Secure gates being a requirement and the upheave of the ground following the ramming of the gate posts the only location for posts to be secured to the required depth falls outside the root protection area. To secure to the existing boundary fence a bolted Metal and Shear fastener approach has been adopted. This allowed the use of the smallest posts to the lowest depth. The Gate posts are the only posts secured using concrete. All other posts are pushed/rammed in to place. Positions for these posts were "Surveyed" using a tin Steel rod to check for roots, due to the historic hard core pushed in to the Sub Soil various positions were trialled until positions avoiding incompatible hardcore and no roots over 30mm were found.
