# Tree Code: Sgl/017941

**Tree Tag:**

**Seq No:** 9

**Position:**

**Stems:** 1

**Species:** Betula pendula (Silver Birch)

**Site:** St Andrews Close, Crowthorne

**Location:** Wokingham Without

**Grid Ref:** SU 82923 64754

**OS X/Y:** 482922.34, 164753.01

**Lat Long:** 51.375786, -0.809996

**what3words:** /// tides.retail.work

**Planted:**

**Stock Type:**

**Owner:** Wokingham Council

**Notes:**

**Value:** £0.00

| | | | |
|---|---|---|---|
| **Felled:** | No | **Proposed:** | No |
| **TPO:** | Yes | **Private:** | No |
| **CRP - NONE:** | Yes | **CRP - FAR:** | No |
| **CPR - PRF:** | No | **Insurance:** | No |
| **Property:** | No | **Con Area:** | No |



06/08/2026 16:00:

**Regimes:**



06/08/2026 15:59:



06/08/2026 16:00:



06/08/2026 16:00:



06/08/2026 16:00:



06/08/2026 16:01:

## Inspection: 06/08/2026

**Height:** 05 to 10m

**Age:** Established

**Trunk:** 150-300mm

**Spread:** 00 to 05m

**Features:** Adjacent - Building - >3m
Growing In - Mown Grass
Target - Boundary Wall/Fence
Target - Garden
Target - Building

**Conditions:** Crown - Minor Deadwood < 100mm
Trunk - Major Trunk Decay
Trunk - Trunk Cavity
Trunk - Surface Bark Wound

**Comments:** TPO-0245-1983 W1

**Dry Weight:** 127,706.338 KG

**Carbon Weight:** 63,853.169 KG

**CO2 Sequestered:** 191,559.507 KG (£16,282.56)

**CO2 Seq Per Year:** 677.503 KG (£57.59)

## Visited By: CT

**Condition:** Poor

**CrLightExp:** 1 Side Exposed

**Prob of F.:** Probable/Soon

**Target:** Medium

**Deg ofHarm:** Moderate

**SLE:** Under 5 years

**FuncValue:**

**Cdbh(Auto):** < 5.9

**Risk:** Moderate Risk

**THREATS:** 960


**Next Inspection:** 08/2029

**Recommendations:** Standing monolith - Retain a monolith up to 2.0m

**Priority:** 13W - Within 13 wks

**Recom Due Date:** 05/11/2026

**Works:**

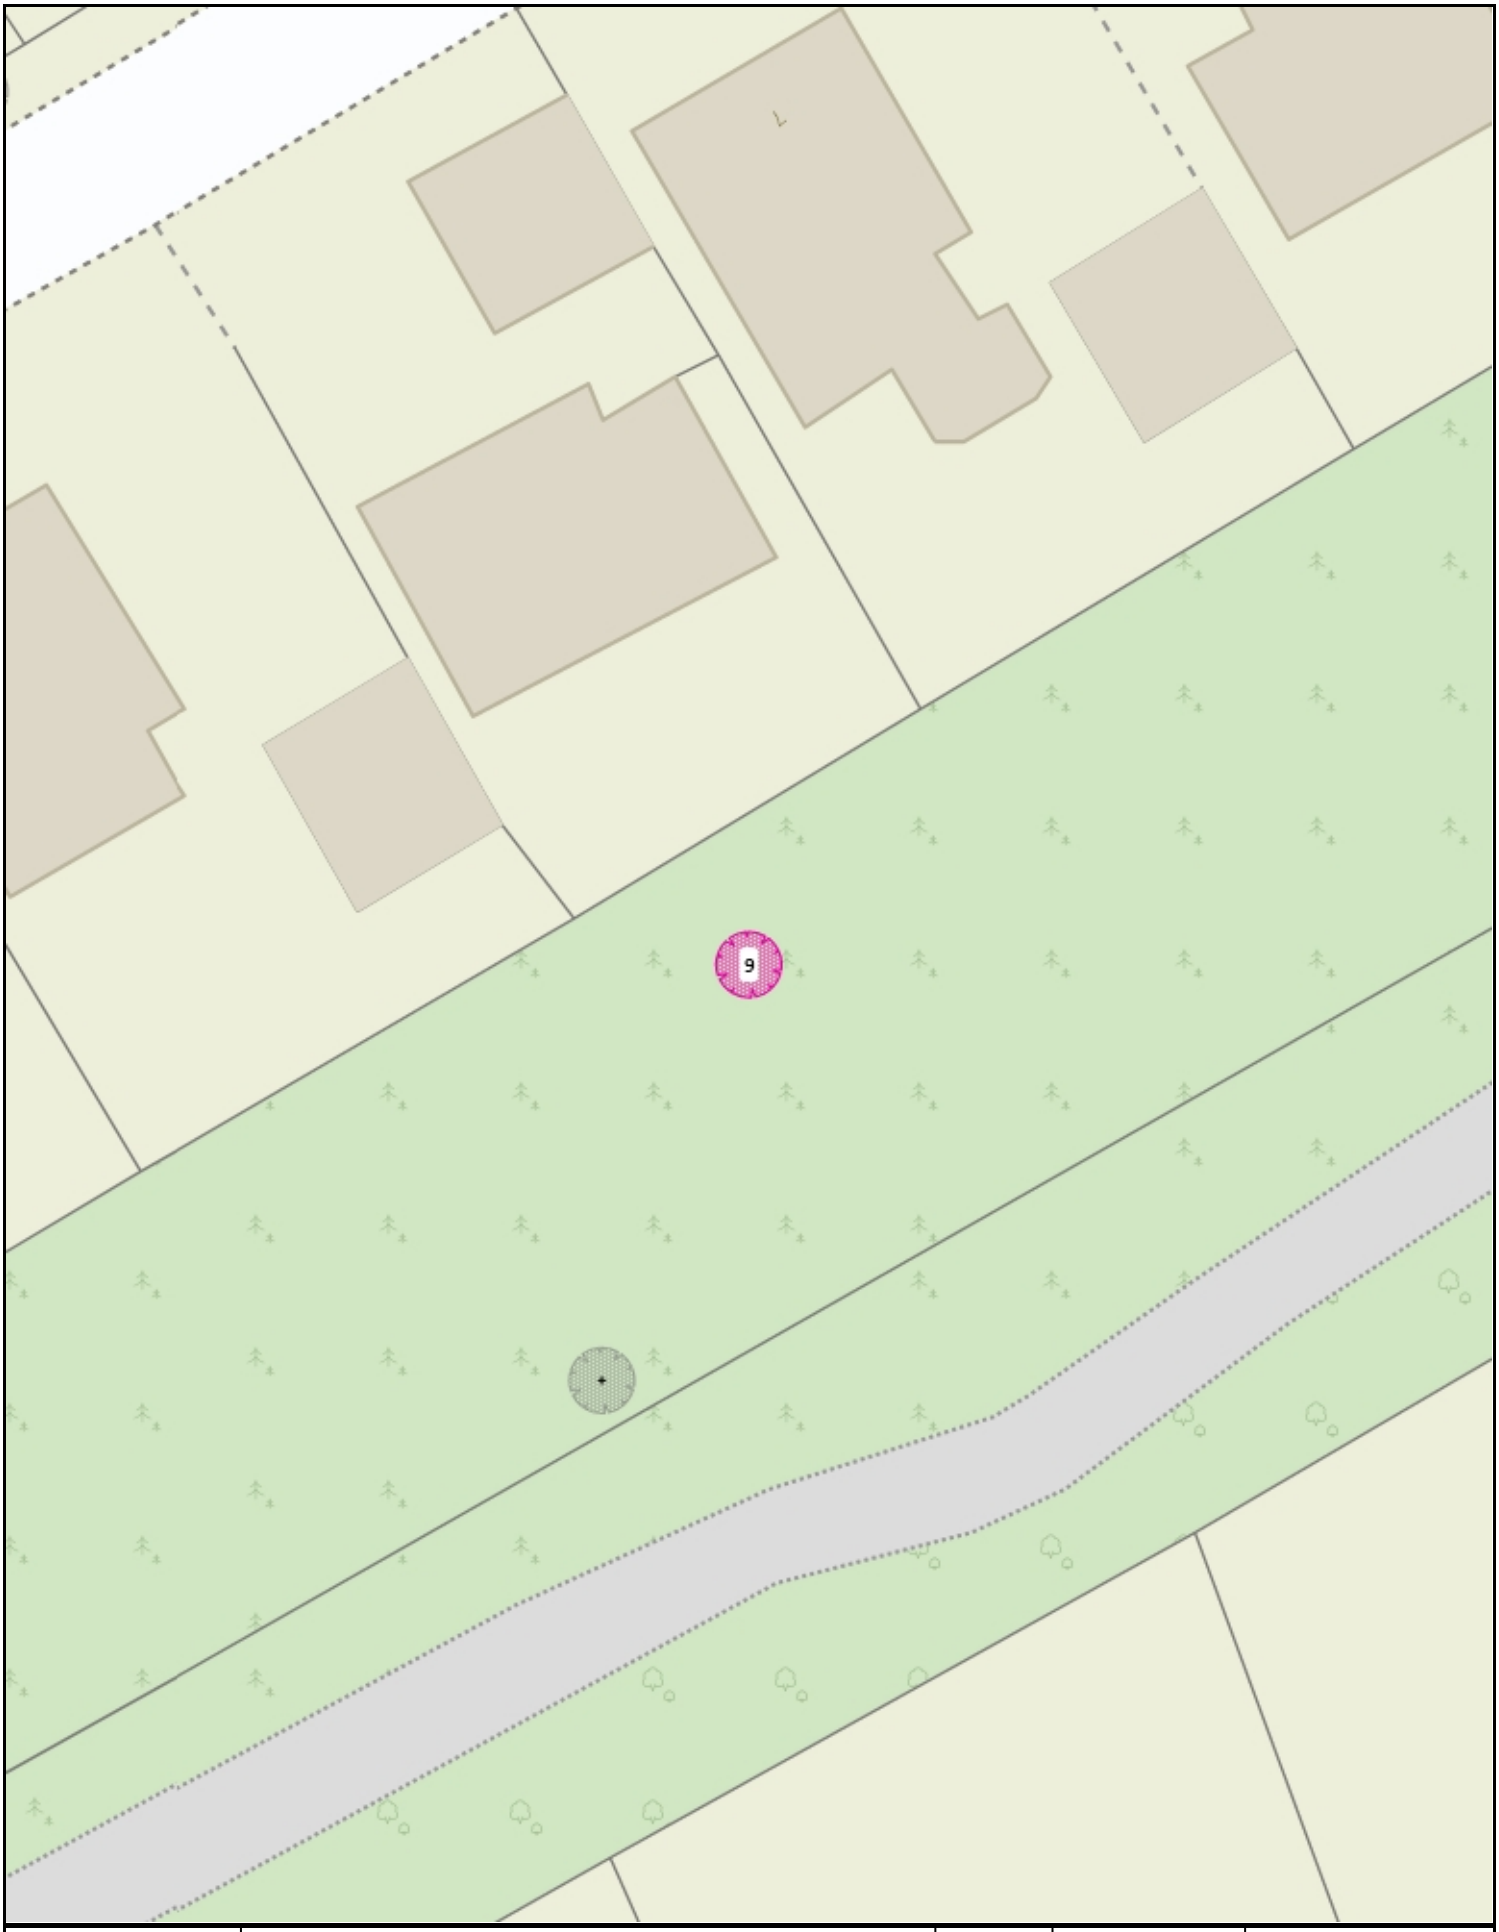


WOKINGHAM BOROUGH COUNCIL

**Overview**

| | |
|---|---|
| **Scale** | **1: 229** |
| **Date** | **18/08/2026** |

N
W E
S
